


Job Name: 25-2471 - Texas Roadhouse Job Location: Danville, KY Contractor: McCain Bros Excavating LLC				Plant: 100 6/12/2026 3:42:06 PM		Tech: Jared - F PC: M. Sullivan				
Structure ID: 10										
P1 MH048BA60				MH BASE T/n						
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 42" P1) 48" - MH BASE T/n - 60" 1) 48" - SGL 1"x14.5' Butyl (2x) 1) Hole - 38 9) MH Step ML-10-TDS-NCR - 10"						0 lb 3200 lb 4988 lb 0 lb 0 lb 0 lb ----- 8188 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. (7" TALL CASTING BY OTHERS) REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.		
Rim: 1035.43' Rim to Invert: 9' Slack: 1.55" Sump: 2.55" Step Position: 180°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1026.43'	0°	0"	30" HDPE	35.1"	Hole 38	38"	43.85"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

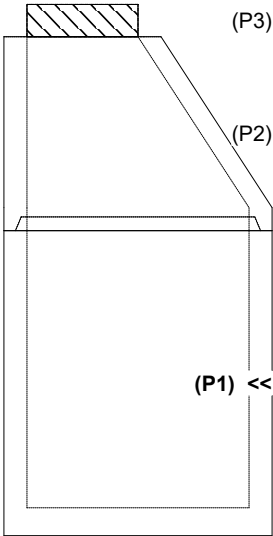


(P3)

(P2)

(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

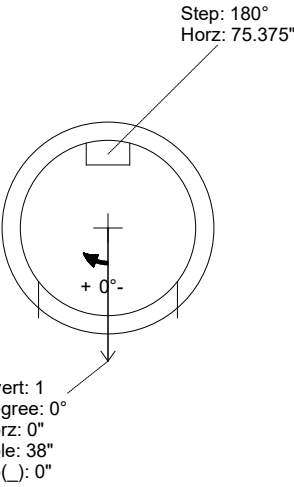

Step: 180°
Horz: 75.375"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 38"
Up(): 0"


UPSIDE-DOWN VIEW (int. dimensions)

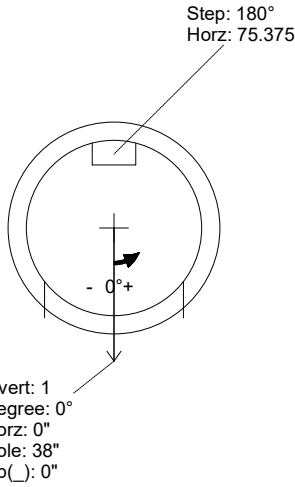

Step: 180°
Horz: 75.375"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 38"
Up(): 0"

INSIDE WALL DIMENSIONS

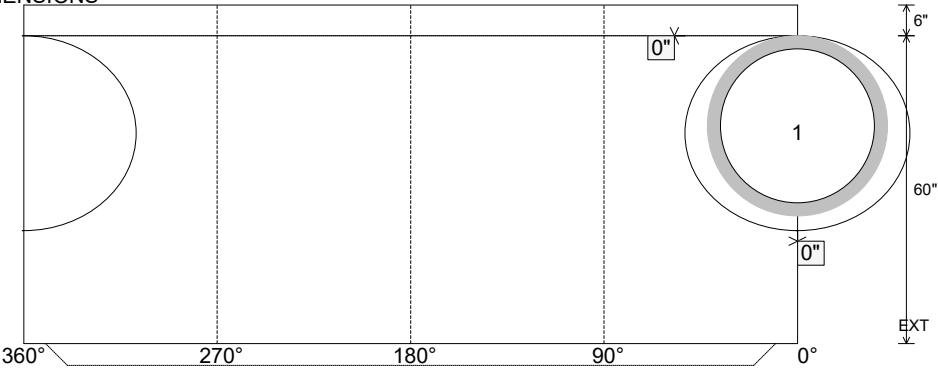

(P1)

360° 270° 180° 90° 0°

0" 6" 60" EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 60" Height (Ext): 66"	Weight (Net): 4988 lb Volume (Net): 1.27cu.yd
----------------------------------	---------------------------------	--	--	--
