



Job Name: 25-2471 - Texas Roadhouse Job Location: Danville, KY Contractor: McCain Bros Excavating LLC					Plant: 100 6/11/2026 11:35:20 AM		Tech: Jared - F PC: M. Sullivan				
Structure ID: 3											
P1 MH060BA72 MH BASE T/n											
P4) 24" - CASTING HEIGHT - 7" P3) 60" - MH FLAT TOP w/ 24" ECC Hole F/G - 13" P2) 60" - MH RISER Custom Ht T/G - 31" P1) 60" - MH BASE T/n - 72" 2) 60" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 30 1) DOGHOUSE INVRTD - 30"x29" 4) MH Step ML-10-TDS-NCR - 10"						0 lb 2869 lb 3236 lb 9101 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 15206 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. (7" TALL CASTING BY OTHERS) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.			
Rim: 1036' Rim to Invert: 8.31' Slack: 0.72" Sump: 24" Step Position: 90°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	1027.69'	0°	0"	24" HDPE	27.8"	Hole 30	30"	31.416"	22.125"	0"	
Invert 2	1027.69'	180°	113.125"	24" HDPE	27.8"	Hole 30	30"	31.416"	22.125"	0"	
Invert 3	1029.42'	270°	169.625"	24" HDPE	27.8"	DOGHOUSE INVRTD 30"x29"	30" x 29"	31.416"	42.875"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

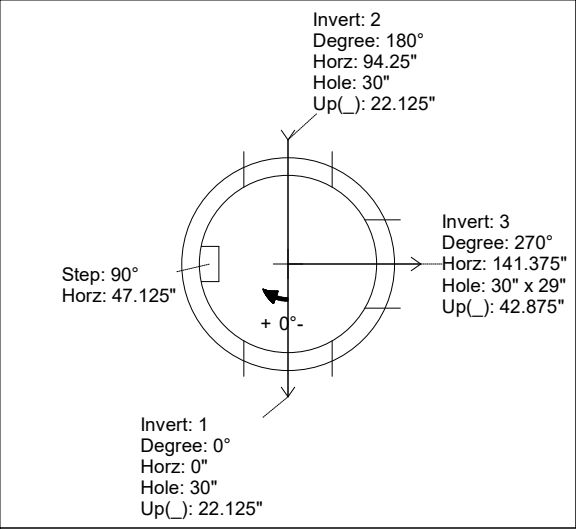

UPSIDE-DOWN VIEW (int. dimensions)

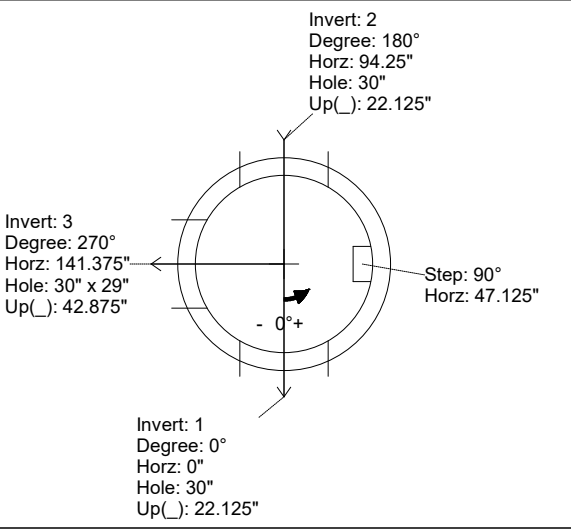

INSIDE WALL DIMENSIONS

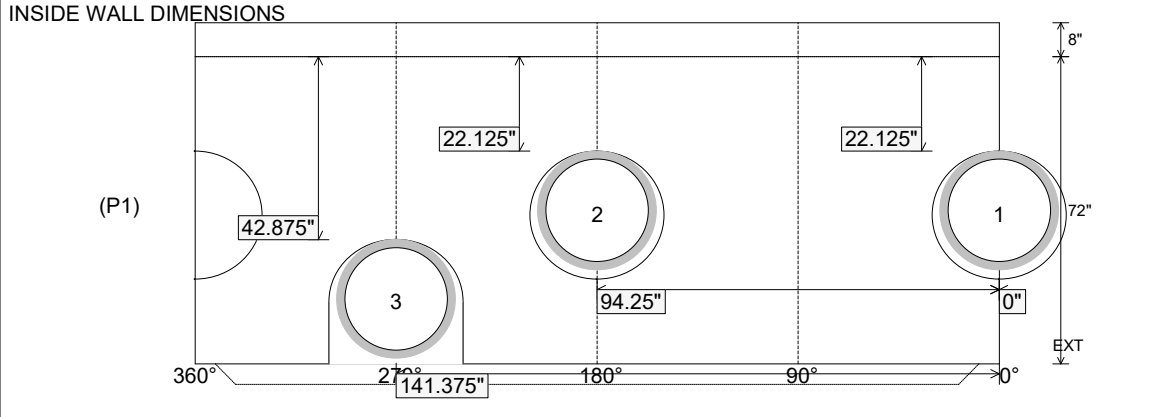

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 72" Height (Ext): 80"	Weight (Net): 9101 lb Volume (Net): 2.33cu.yd
----------------------------------	---------------------------------	--	--	--
