

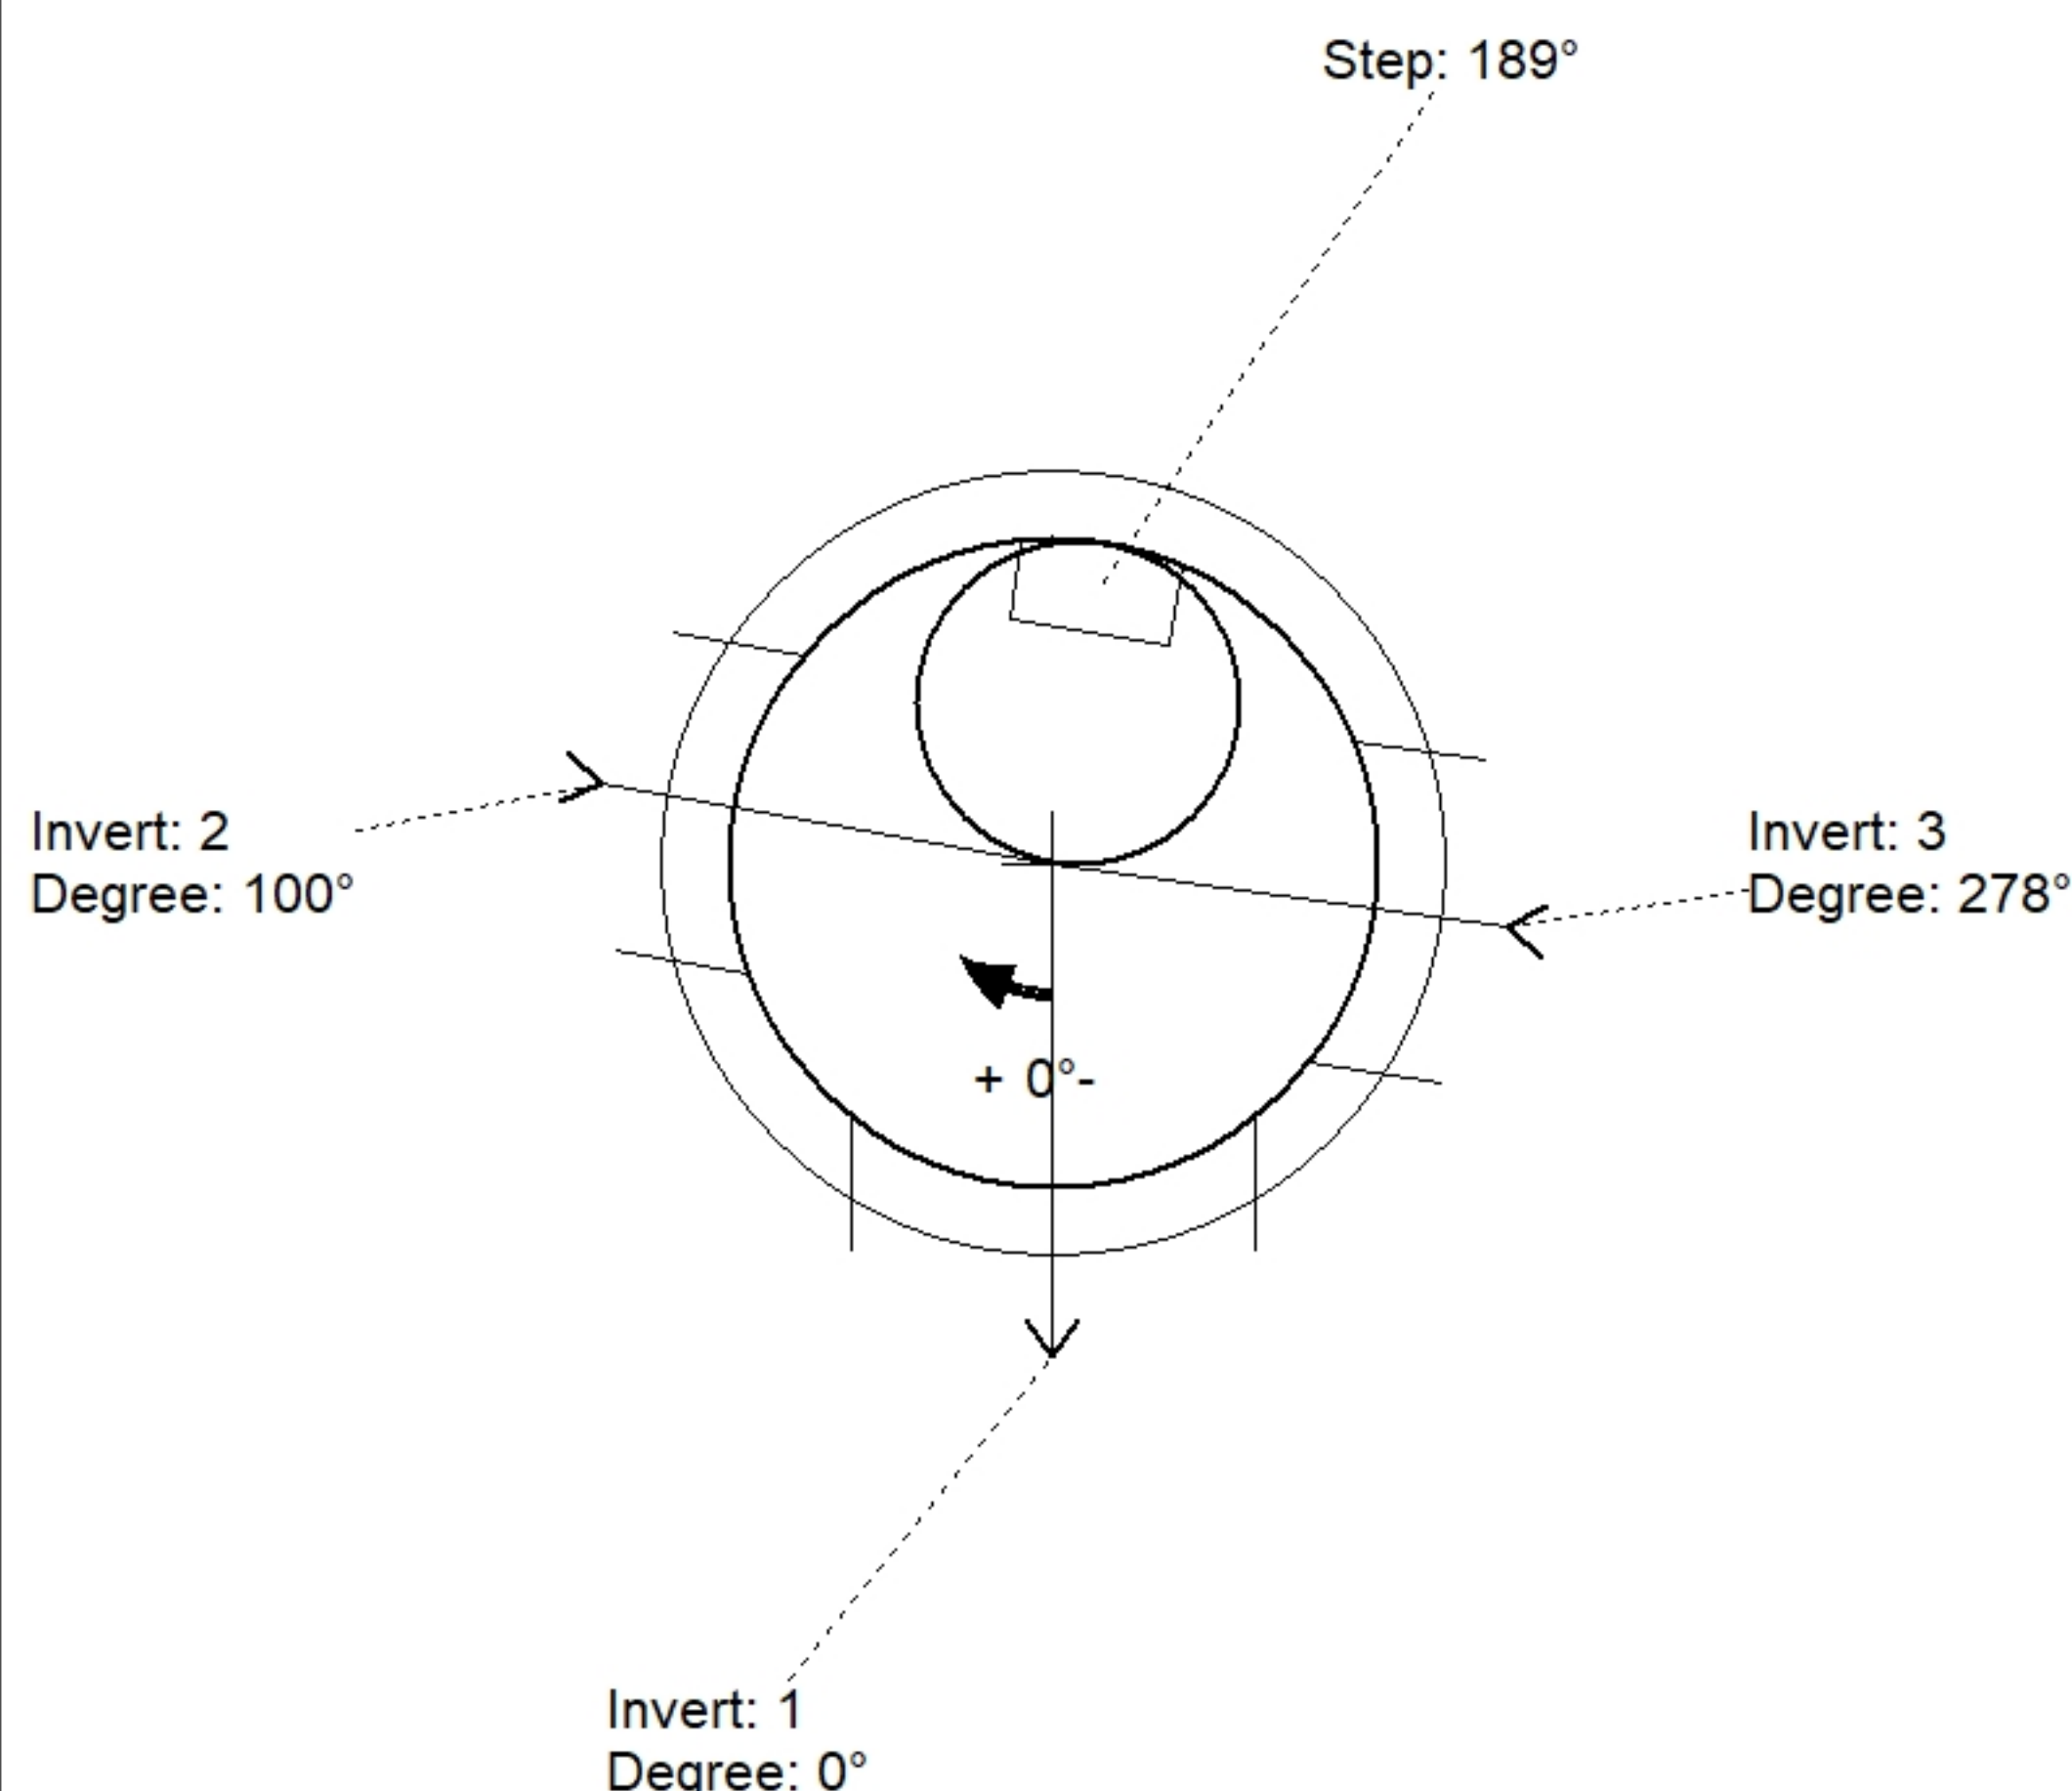


Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. (7" TALL CASTING BY OTHERS) REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	STRUCTURE SUMMARY: P3) 24" - CASTING HEIGHT - 7" 0 lb P2) 48" - ECC CONE w/ 24" HOLE - 36" 3000 lb P1) 48" - MH BASE - 42" 3554 lb 1) 48" - Conseal CS-102 1.00" 0 lb 1) 24" - Conseal CS-102 1.00" 0 lb 1) Hole - 30 0 lb 2) Hole - 24 0 lb 6) MH Step ML-10-TDS-NCR - 10" 0 lb Structure Total: 6554 lb
--	--

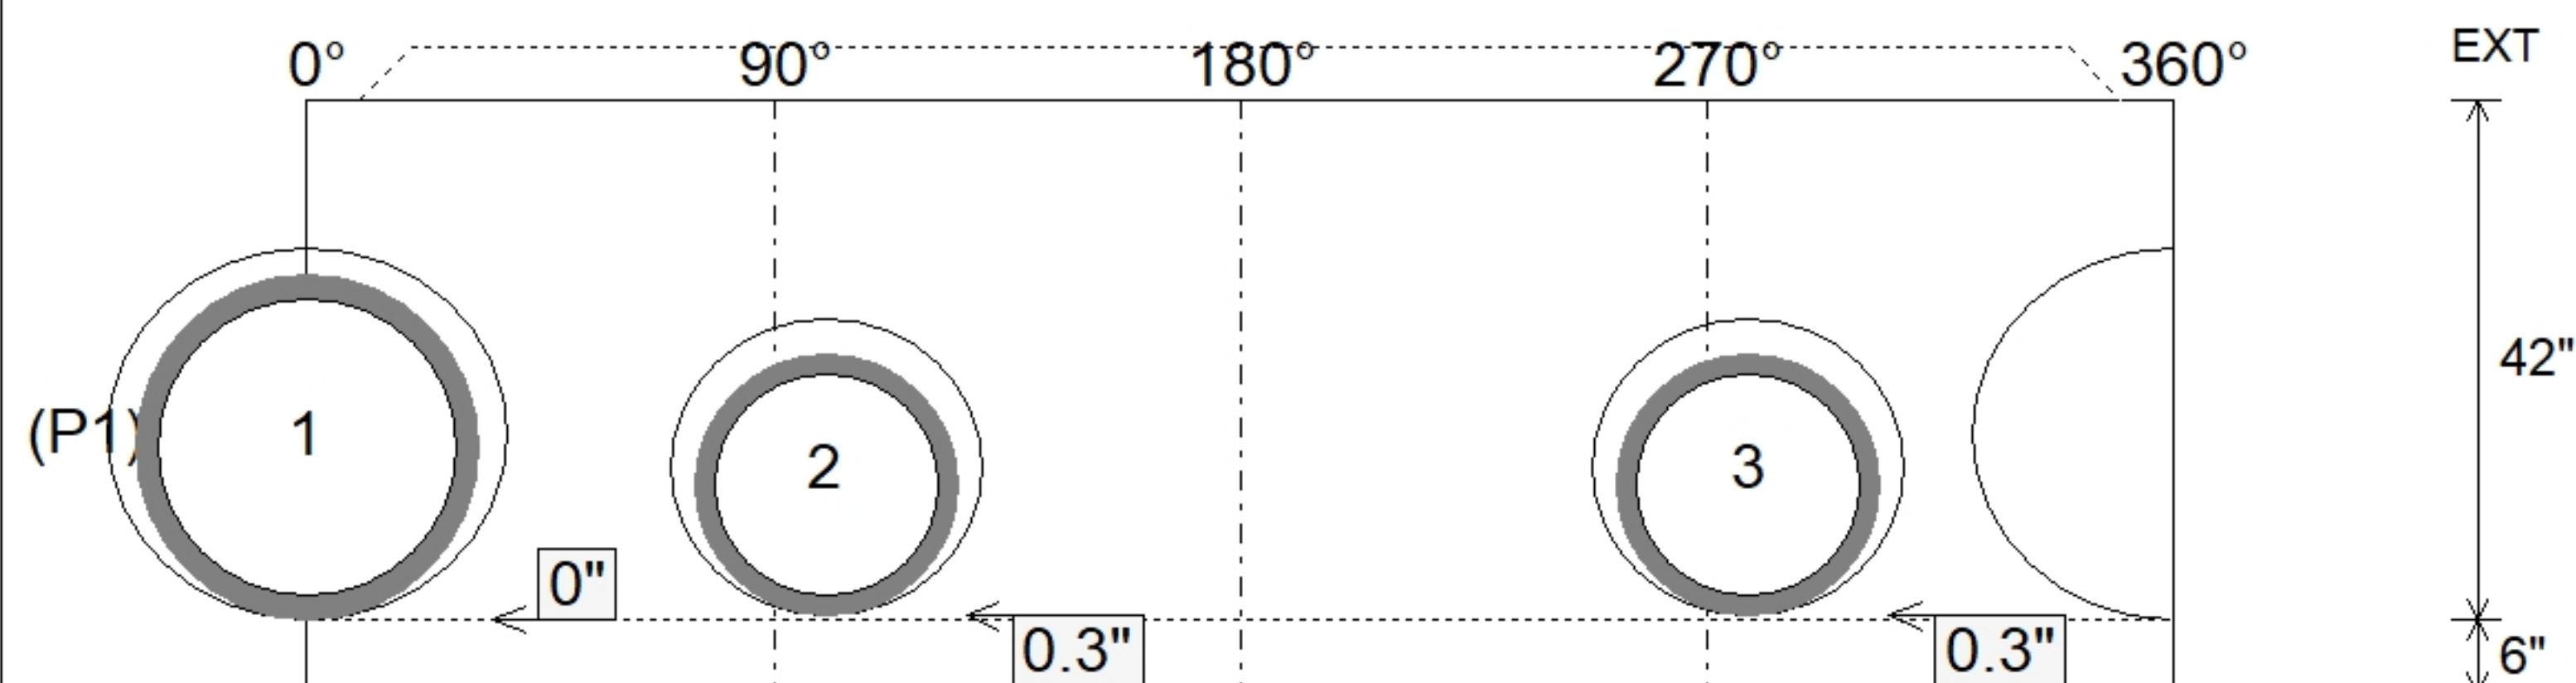

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	1036.05'							
Reducer								
Invert 1	1028.9'	0°	24" HDPE	27.8"	30"	Hole 30	0"	P1
Invert 2	1028.9'	100°	18" HDPE	21.2"	24"	Hole 24	0.3"	P1
Invert 3	1028.9'	278°	18" HDPE	21.2"	24"	Hole 24	0.3"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

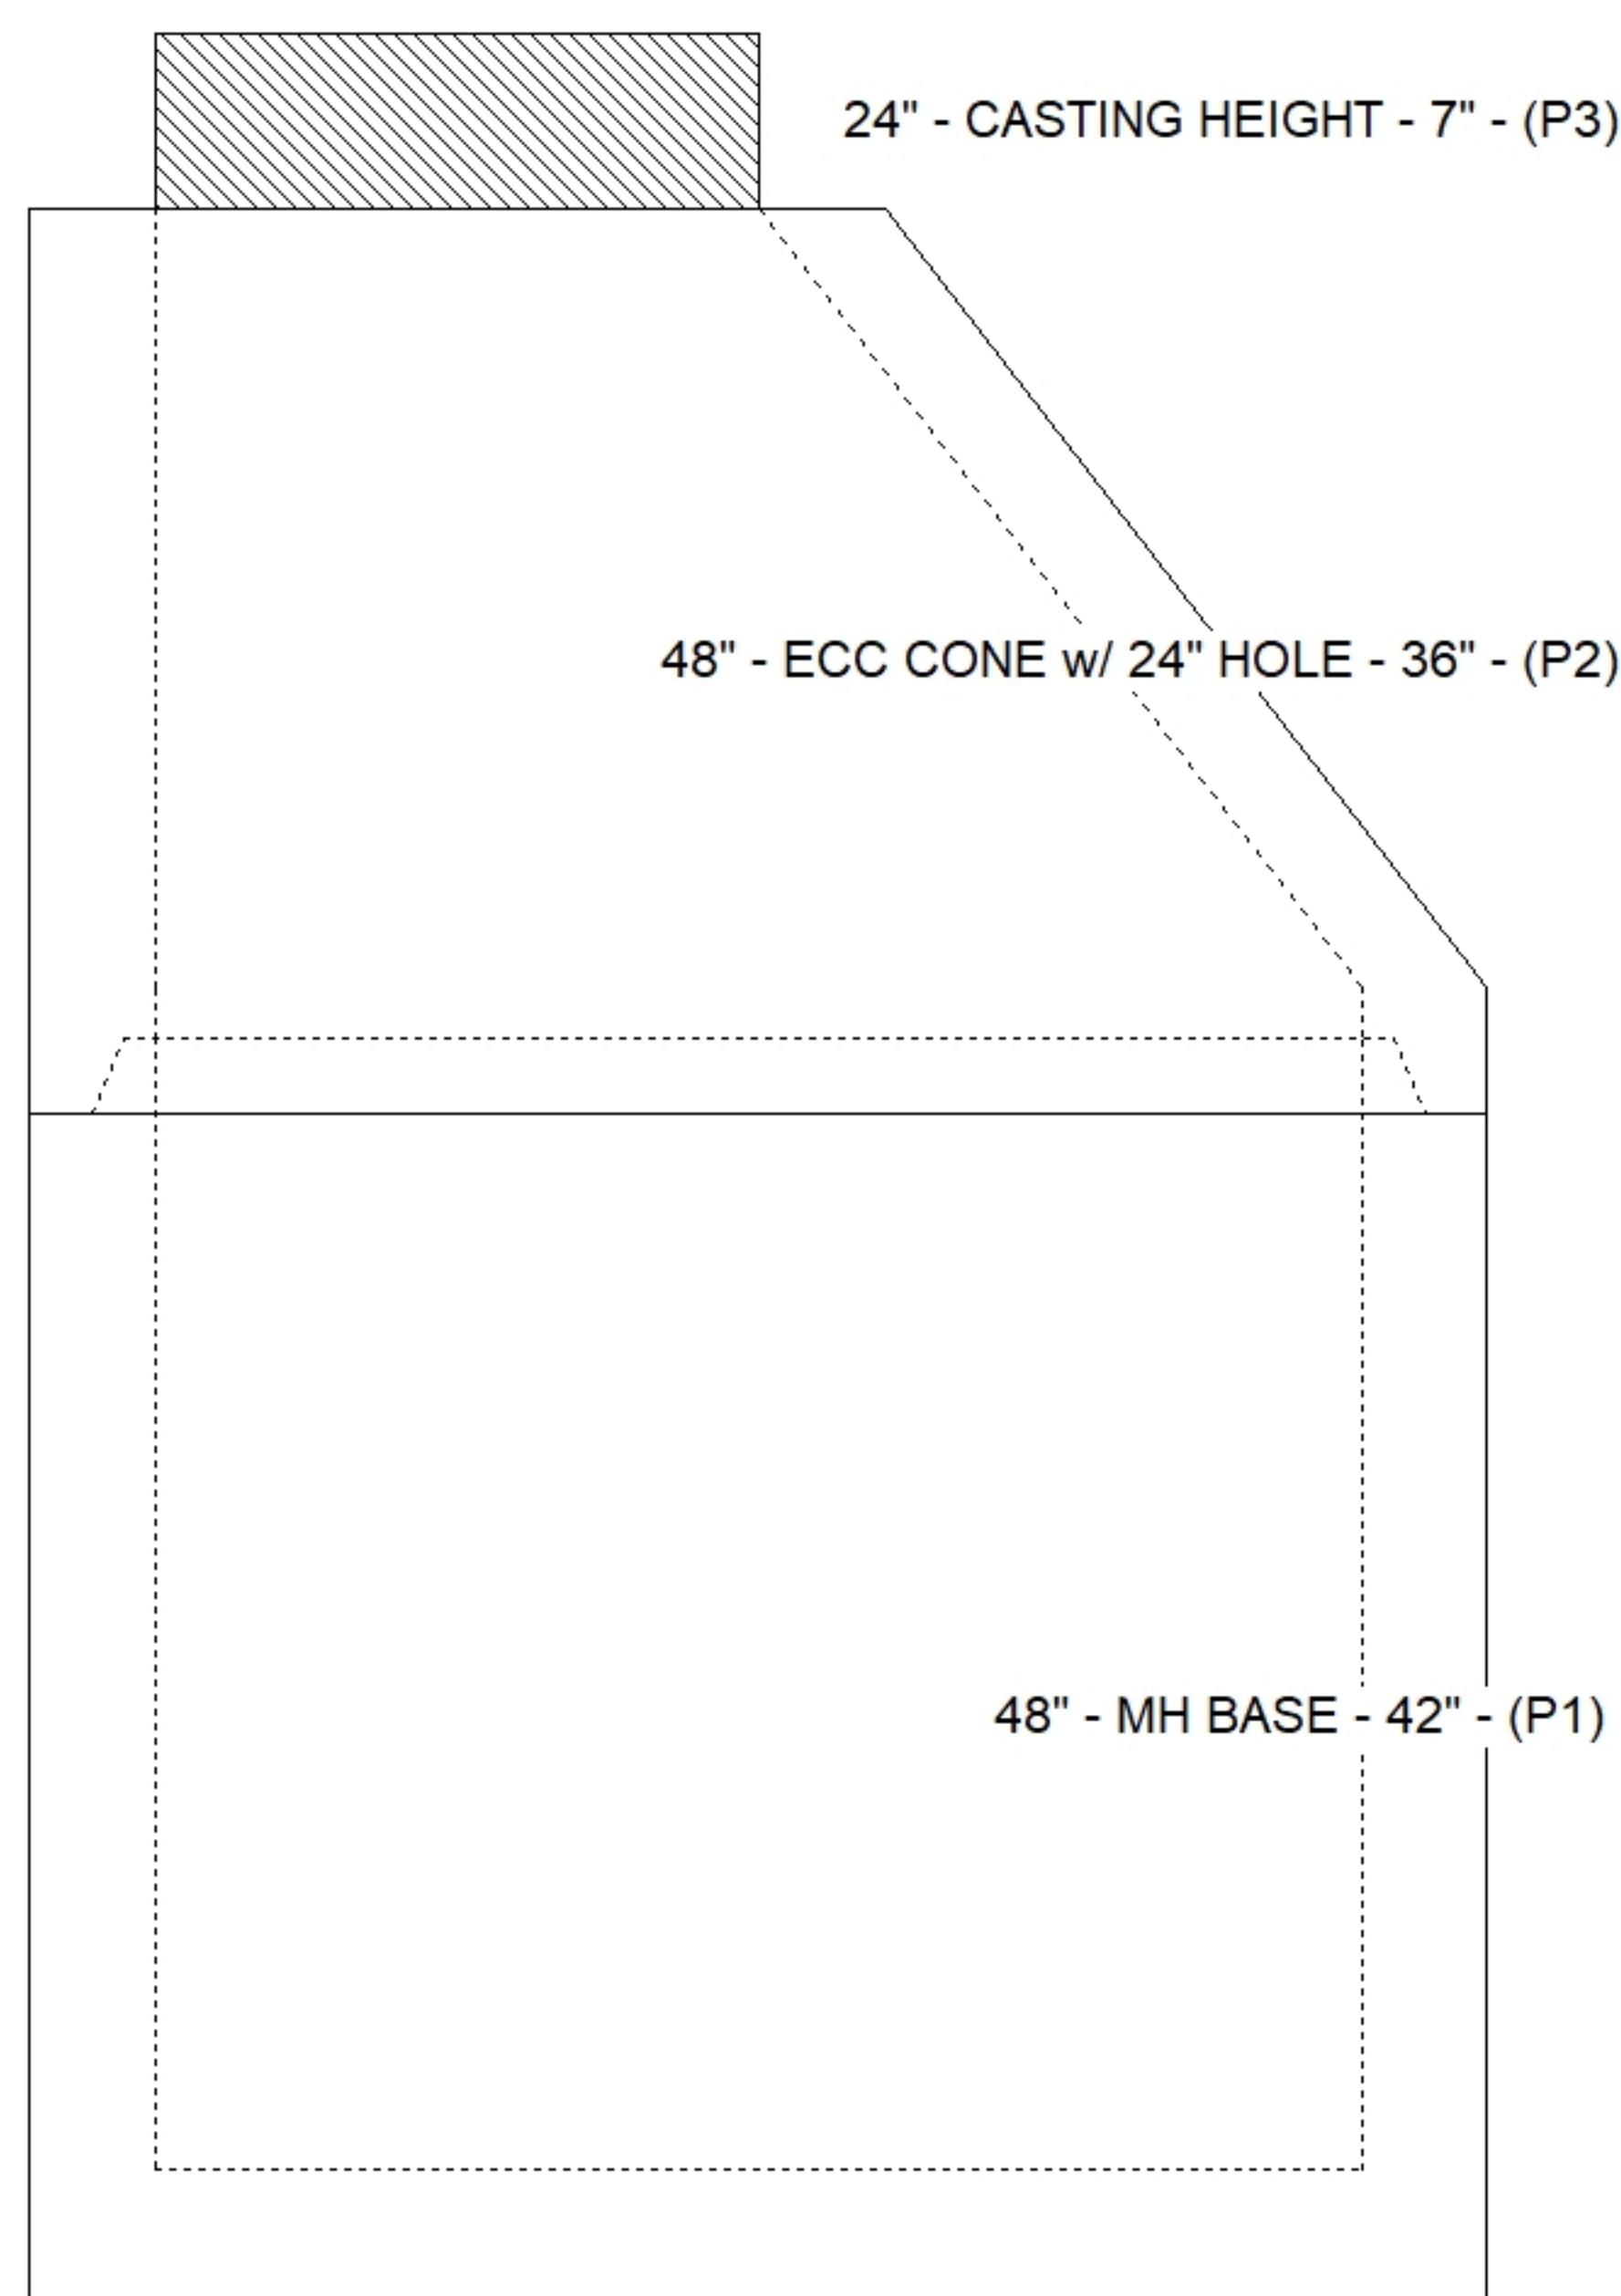

SUBMITTAL
APPROVED BY:
