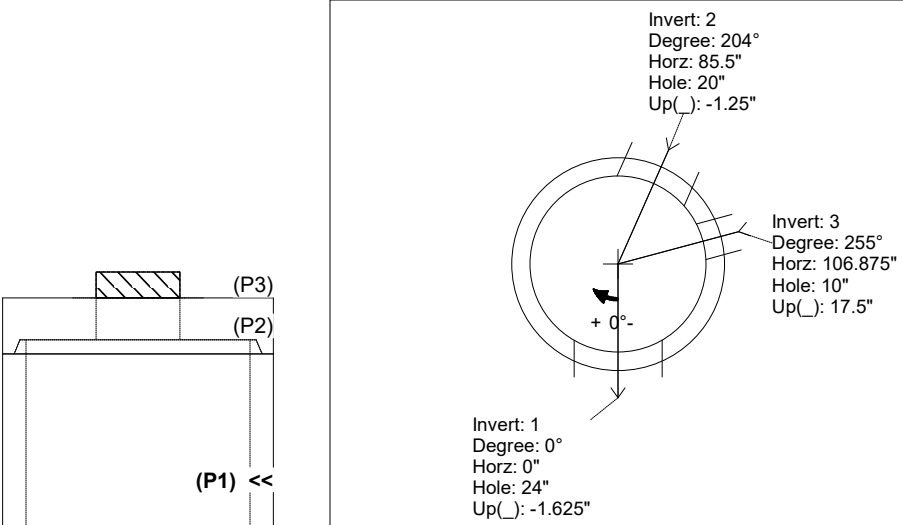
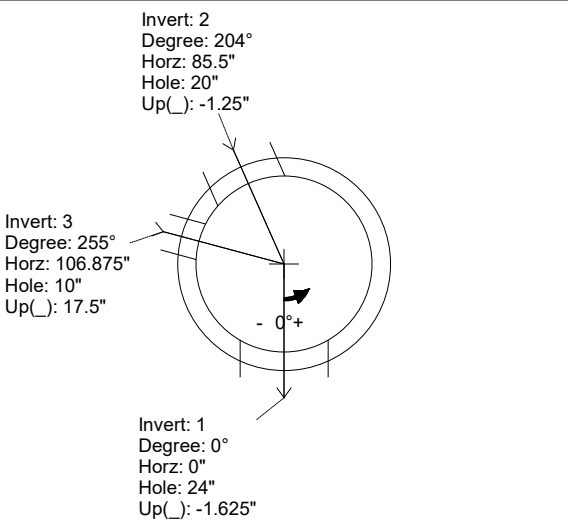
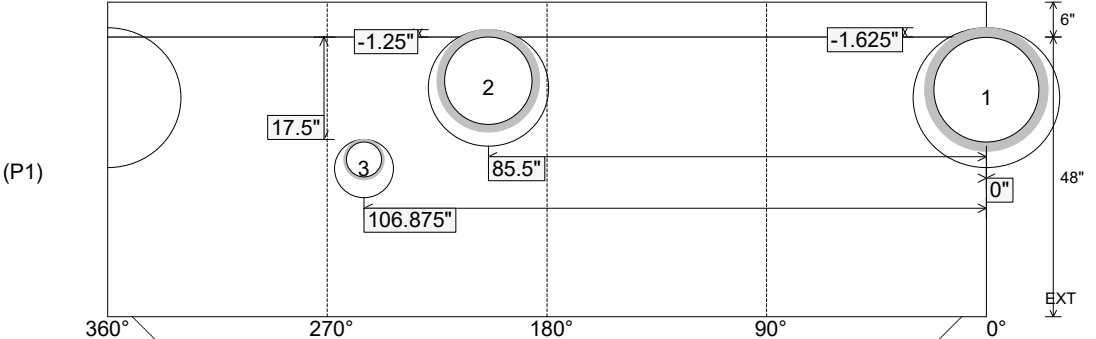


Job Name: 25-2471 - Texas Roadhouse Job Location: Danville, KY Contractor: McCain Bros Excavating LLC					Plant: 100 6/11/2026 11:35:20 AM		Tech: Jared - F PC: M. Sullivan				
Structure ID: 4A											
P1 MH048BA48		MH BASE T/n									
P3) 18" x 36" - CASTING HEIGHT - 5.5" P2) 48" - MH FLAT TOP w/18"x36" Hole F/G - 12" P1) 48" - MH BASE T/n - 48" 1) 48" - Conseal CS-102 1.00" 1) 18" x 36" - Conseal CS-102 1.00" 1) Hole - 24 1) Hole - 20 1) Hole - 10						0 lb 2008 lb 4318 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 6326 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING SUPPLIED BY OTHERS (HOE 580-A F/G). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1037'		Rim to Invert: 5.5'		Slack: 0.5"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	1031.5'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	-1.625"	0"	
Invert 2	1031.5'	204°	103.25"	15" HDPE	17.6"	Hole 20	20"	20.629"	-1.25"	0"	
Invert 3	1033'	255°	129.125"	6" HDPE	6.9"	Hole 10	10"	10.074"	17.5"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions) 											
INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 48" Height (Ext): 54"		Weight (Net): 4318 lb Volume (Net): 1.1cu.yd		
