

Job Name: 25-2471 - Texas Roadhouse

Job Location: Danville, KY

Contractor: McCain Bros Excavating LLC

Plant: 100

6/11/2026 11:35:21 AM

Tech: Jared - F

PC: M. Sullivan

Structure ID: 5

P1 BX036096-08BAVF

BOX BASE 8inW, 8inF F/n

P3) 18" x 36" - CASTING HEIGHT - 5.5"

P2) 36" x 96" - BX FLAT TOP 8inW w/(2) 18"x36" HOLES F/F - 8"

P1) 36" x 96" - BOX BASE 8inW, 8inF F/n - 42"

1) 36" x 96" - Conseal CS-102 1.00"

1) 18" x 36" - Conseal CS-102 1.00"

2) Hole - 24

1) Hole - 20

0 lb

3042 lb

11437 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 14479 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. NO STEPS AND NO INVERT CHANNEL.

4. CASTING SUPPLIED BY OTHERS (2ea. HOE 580-A F/G)

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.

- WALLS (As .12) #5 BARS AT 12" C.C.E.W.

- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

Rim: 1034.75' Rim to Invert: 4.69' Slack: 0.78" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1030.06'	90°	56"	18" HDPE	21.2"	Hole 24	24"	24"	-1.625"	0"
Invert 2	1030.06'	180°	26"	18" HDPE	21.2"	Hole 24	24"	24"	-1.625"	0"
Invert 3	1030.06'	0°	26"	15" HDPE	17.6"	Hole 20	20"	20"	-1.25"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

1ST POUR (FLOOR) = 3,909 LBS

2ND POUR (WALLS) = 7,528 LBS

1ST POUR (FLOOR) STUB #5 L BARS OUT TOP FLOOR, SPA AT 12" C/C FOR CONNECTING WALLS

INSIDE WALL DIMENSIONS

Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 42"

Height (Ext): 50"

Weight (Net): 11437 lb

Volume (Net): 2.92cu.yd

Job Name: 25-2471 - Texas Roadhouse
Job Location: Danville, KY
Contractor: McCain Bros Excavating LLC

Plant: 100

6/11/2026 11:35:21 AM

Tech: Jared - F
PC: M. Sullivan



Structure ID: 5

P1 BX036096-08BAVF

BOX BASE 8inW, 8inF F/n

P3) 18" x 36" - CASTING HEIGHT - 5.5"
P2) 36" x 96" - BX FLAT TOP 8inW w/(2) 18"x36" HOLES F/F - 8"
P1) 36" x 96" - BOX BASE 8inW, 8inF F/n - 42"
1) 36" x 96" - Conseal CS-102 1.00"
1) 18" x 36" - Conseal CS-102 1.00"
2) Hole - 24
1) Hole - 20

0 lb
3042 lb
11437 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 14479 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING SUPPLIED BY OTHERS (2ea. HOE 580-A F/G)


REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

Rim: 1034.75' Rim to Invert: 4.69' Slack: 0.78" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1030.06'	90°	56"	18" HDPE	21.2"	Hole 24	24"	24"	-1.625"	0"
Invert 2	1030.06'	180°	26"	18" HDPE	21.2"	Hole 24	24"	24"	-1.625"	0"
Invert 3	1030.06'	0°	26"	15" HDPE	17.6"	Hole 20	20"	20"	-1.25"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

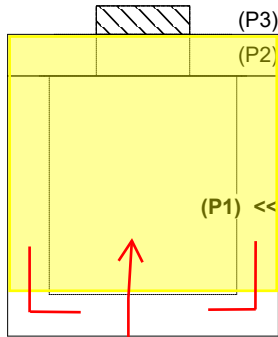


2ND POUR (WALLS)

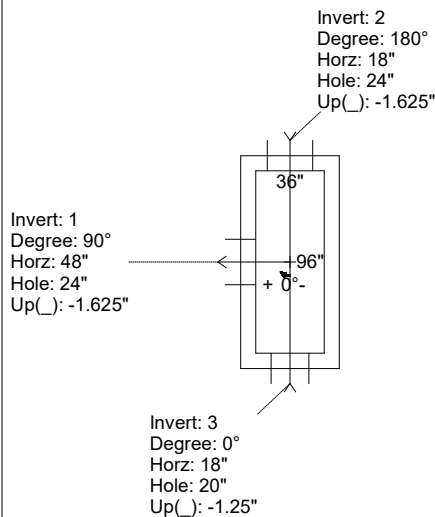

**1ST POUR (FLOOR) = 3,909 LBS
2ND POUR (WALLS) = 7,528 LBS**

INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 42"
Height (Ext): 50"

Weight (Net): 11437 lb
Volume (Net): 2.92cu.yd
