




Job Name: 25-2471 - Texas Roadhouse Job Location: Danville, KY Contractor: McCain Bros Excavating LLC					Plant: 100 6/11/2026 11:35:22 AM		Tech: Jared - F PC: M. Sullivan				
Structure ID: 6											
P1		MH048BAVF									
MH BASE Custom Ht F/n											
P3) 18" x 36" - CASTING HEIGHT - 5.5" P2) 48" - MH FLAT TOP w/18"x36" Hole F/F - 6" P1) 48" - MH BASE Custom Ht F/n - 19" 1) 48" - Conseal CS-102 1.00" 1) 18" x 36" - Conseal CS-102 1.00" 1) DOGHOUSE INVRTD - 24"x20" 1) Hole - 16						0 lb 1004 lb 2379 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 3383 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING SUPPLIED BY OTHERS (HOE 580-A F/G). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1034'		Rim to Invert: 2.59'		Slack: 0.58"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector		Hole	Horz Size	Up (_)	Offset
Invert 1	1031.41'	0°	0"	18" HDPE	21.2"	DOGHOUSE INVRTD 24"x20"		24" x 20"	25.133"	-1.625"	0"
Invert 2	1031.41'	102°	51.625"	12" HDPE	14.5"	Hole 16		16"	16.312"	-1.25"	0"
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

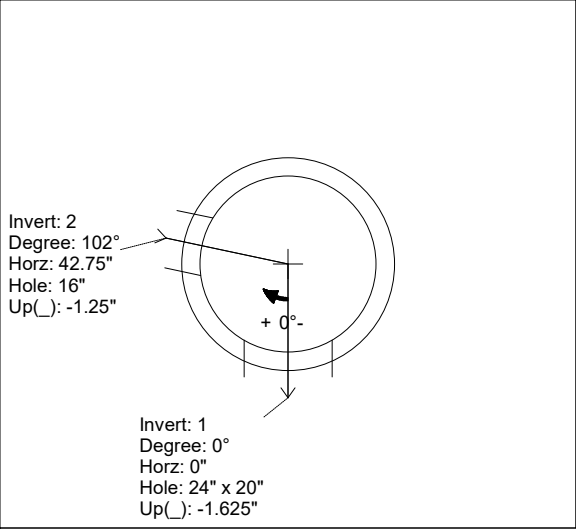

RIGHT-SIDE UP VIEW (int. dimensions)

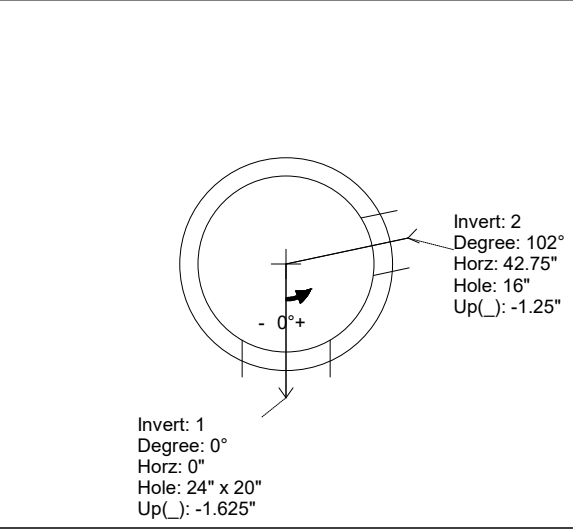

UPSIDE-DOWN VIEW (int. dimensions)

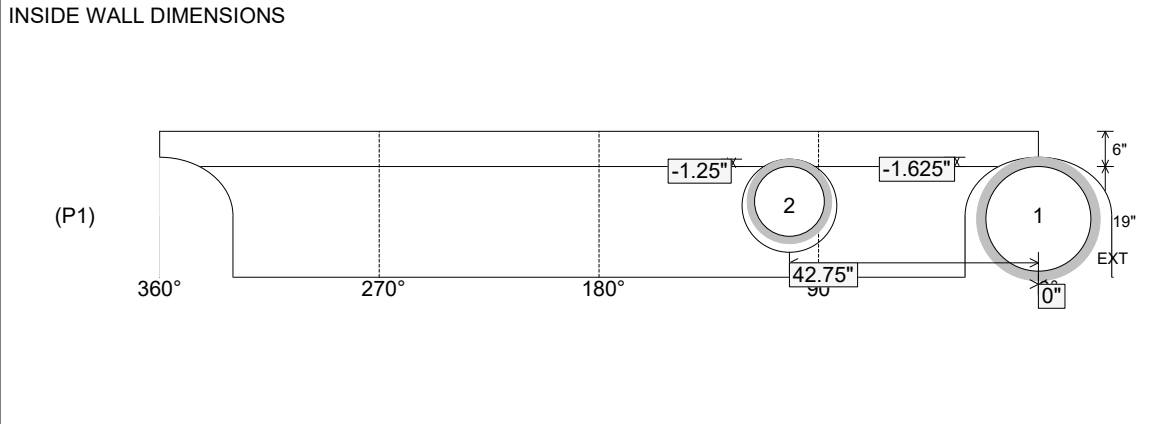

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 19" Height (Ext): 25"	Weight (Net): 2379 lb Volume (Net): 0.61cu.yd
----------------------------------	-------------------------------	--	--	--
