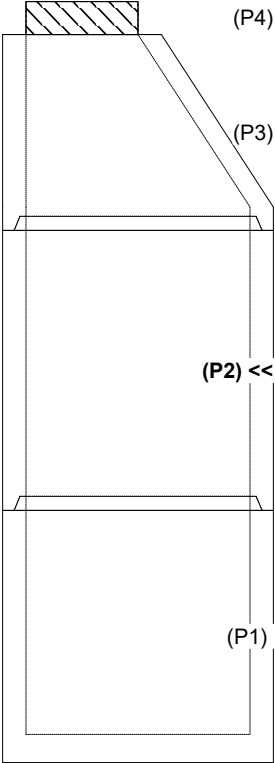

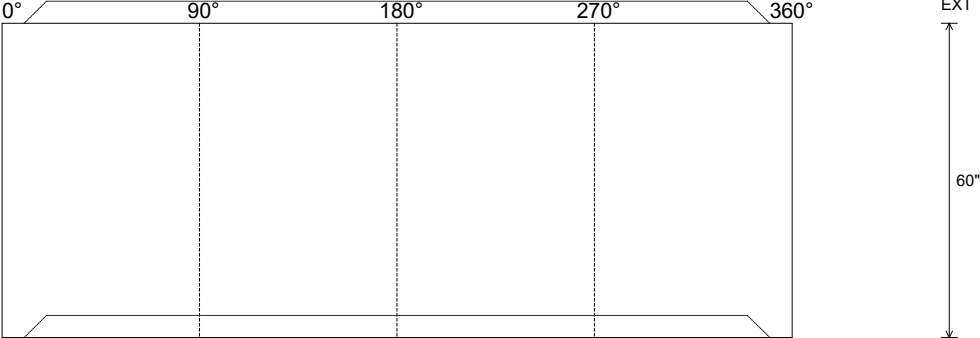


Job Name: 25-2471 - Texas Roadhouse Job Location: Danville, KY Contractor: McCain Bros Excavating LLC					Plant: 100 6/12/2026 3:42:52 PM		Tech: Jared - F PC: M. Sullivan				
Structure ID: 9											
P2 MH048RS60			MH RISER T/G								
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 42" P2) 48" - MH RISER T/G - 60" P1) 48" - MH BASE T/n - 48" 2) 48" - SGL 1"x14.5' Butyl (2x) 2) Hole - 38 13) MH Step ML-10-TDS-NCR - 10"						0 lb 3200 lb 4192 lb 3615 lb 0 lb 0 lb 0 lb ----- Structure Total: 11007 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. (7" TALL CASTING BY OTHERS) REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.			
Rim: 1038.9' Rim to Invert: 13.05' Slack: 2.15" Sump: 2.55" Step Position: 270°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 60" Height (Ext): 60"		Weight (Net): 4192 lb Volume (Net): 1.07cu.yd		
