



Job Name: 25-2541 WARTRACE CREEK INTERCEPTOR Job Location: Springfield, TN Contractor: Cumberland Pipeline LLC					Plant: Beaver Dam 8/7/2025 12:40:08 PM		Tech: C. Russ PC: E.Bradley				
Structure ID: SF-103 R emake											
P1 MH048BAVFX			MH BASE Custom Ht, w/XYPEX T/n								
P5) 24" - CASTING HEIGHT - 6" P4) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 24" P3) 48" - MH RISER w/XYPEX T/G - 60" P2) 48" - MH RISER w/XYPEX T/G - 60" P1) 48" - MH BASE Custom Ht, w/XYPEX T/n - 44" 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 3) 48" - DBL 1"x14.5' Butyl (2x) 2) A-Lok - 0820						0 lb 1738 lb 4192 lb 4192 lb 3899 lb 1440 lb 0 lb 0 lb 0 lb 2 lb ----- 15462 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. JBS 1155 "SANITARY" PROVIDED BY ICAST 4. NO STEPS REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 606.9' Rim to Invert: 16.03' Slack: 0.36" Sump: 2" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	590.87'	0°	0"	24" DI	25.75"	A-Lok 0820	27"	28.676"	0.5"	0"	
Invert 2	590.87'	170°	86.045"	24" DI	25.75"	A-Lok 0820	27"	28.676"	0.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

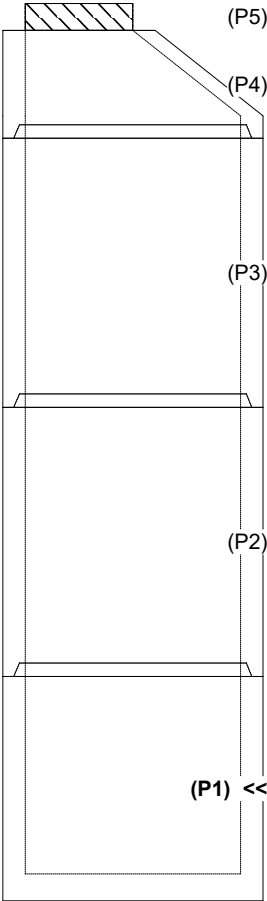

(P5)
(P4)
(P3)
(P2)
(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

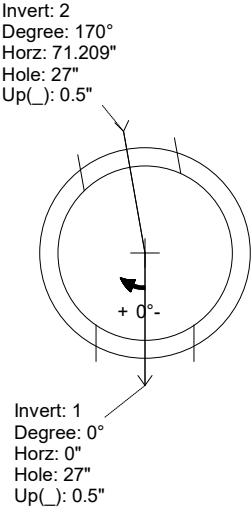

Invert: 2
Degree: 170°
Horz: 71.209"
Hole: 27"
Up(): 0.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 27"
Up(): 0.5"


UPSIDE-DOWN VIEW (int. dimensions)

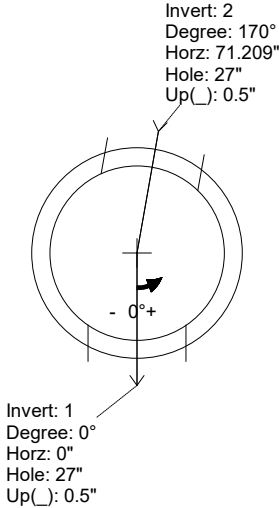

Invert: 2
Degree: 170°
Horz: 71.209"
Hole: 27"
Up(): 0.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 27"
Up(): 0.5"

INSIDE WALL DIMENSIONS

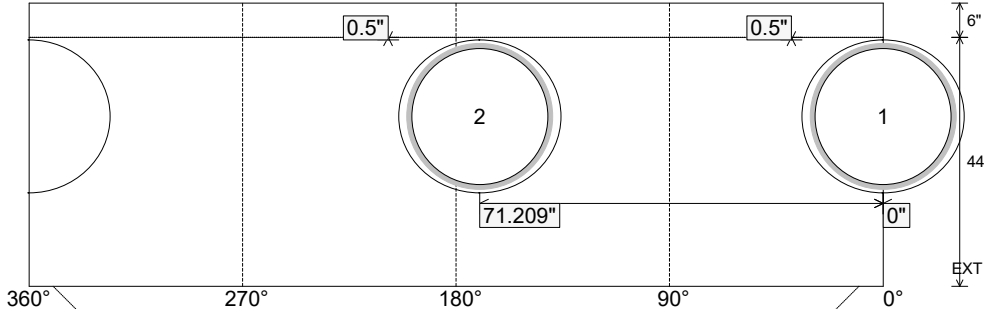

(P1)


360° 270° 180° 90° 0°

0.5" 0.5" 6" 44" 0" 71.209"

EXT


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 44" Height (Ext): 50"	Weight (Net): 3899 lb Volume (Net): 1cu.yd
----------------------------------	---------------------------------	--	--	---

Job Name: 25-2541 WARTRACE CREEK INTERCEPTOR Job Location: Springfield, TN Contractor: Cumberland Pipeline LLC					Plant: Beaver Dam 8/7/2025 12:40:16 PM		Tech: C. Russ PC: E.Bradley				
Structure ID: SF-103 R emake											
P1 MH048BAVFX			MH BASE Custom Ht, w/XYPEX T/n								
P5) 24" - CASTING HEIGHT - 6" P4) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 24" P3) 48" - MH RISER w/XYPEX T/G - 60" P2) 48" - MH RISER w/XYPEX T/G - 60" P1) 48" - MH BASE Custom Ht, w/XYPEX T/n - 44" 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 3) 48" - DBL 1"x14.5' Butyl (2x) 2) A-Lok - 0820						0 lb 1738 lb 4192 lb 4192 lb 3899 lb 1440 lb 0 lb 0 lb 0 lb 2 lb ----- 15462 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. JBS 1155 "SANITARY" PROVIDED BY ICAST 4. NO STEPS REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 606.9' Rim to Invert: 16.03' Slack: 0.36" Sump: 2" Step Position:						INVERT					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	590.87'	0°	0"	24" DI	25.75"	A-Lok 0820	27"	28.676"	0.5"	0"	
Invert 2	590.87'	170°	86.045"	24" DI	25.75"	A-Lok 0820	27"	28.676"	0.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

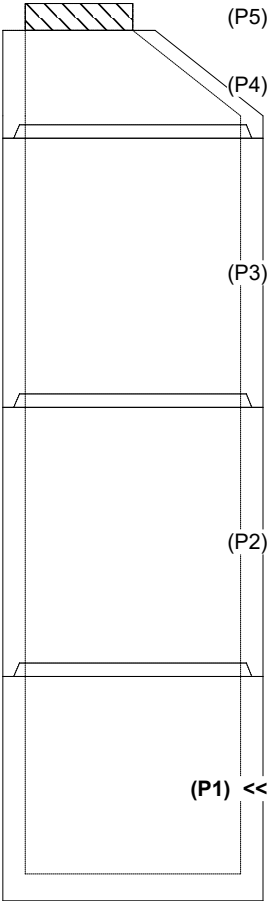

(P5)
(P4)
(P3)
(P2)
(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

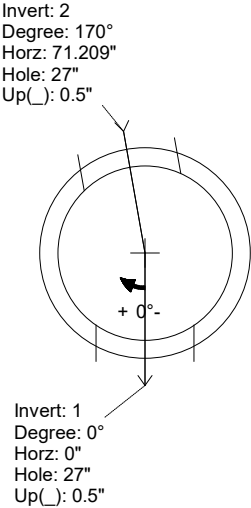

Invert: 2
Degree: 170°
Horz: 71.209"
Hole: 27"
Up(): 0.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 27"
Up(): 0.5"


UPSIDE-DOWN VIEW (int. dimensions)

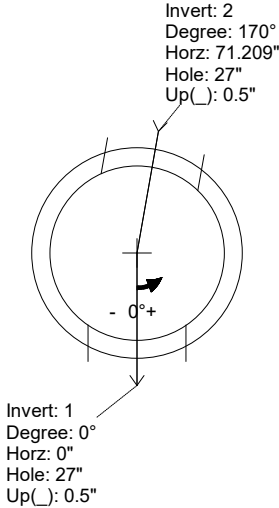

Invert: 2
Degree: 170°
Horz: 71.209"
Hole: 27"
Up(): 0.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 27"
Up(): 0.5"

INSIDE WALL DIMENSIONS

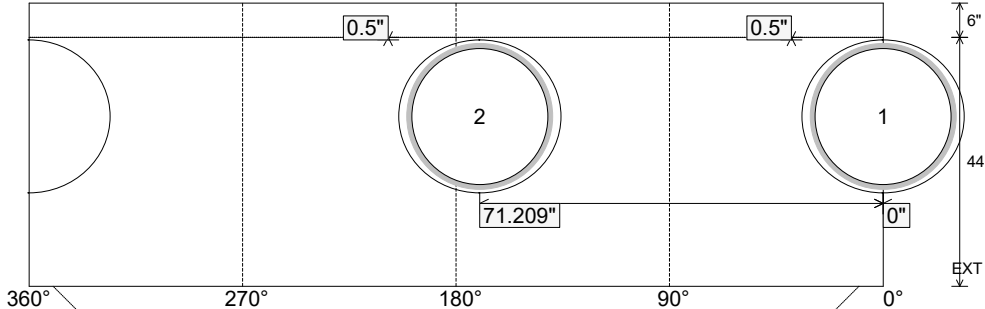

(P1)

360° 270° 180° 90° 0°

0.5" 0.5" 71.209" 0" 44" 6" EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 44" Height (Ext): 50"	Weight (Net): 3899 lb Volume (Net): 1cu.yd
----------------------------------	---------------------------------	--	--	---
