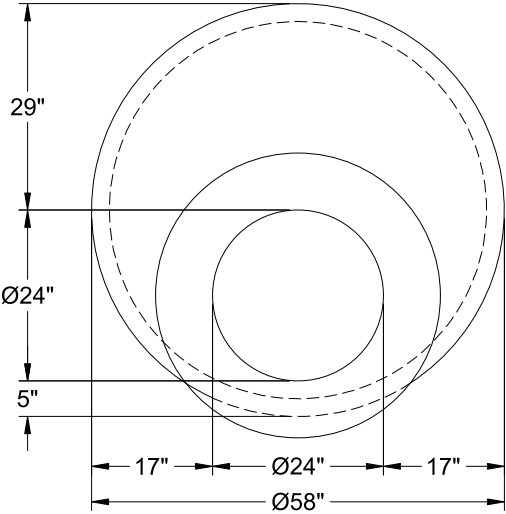


Job Name: 25-2541 - Wartrace Creek Interceptor Job Location: Springfield, TN 37172 Contractor: Cumberland Pipeline LLC		Plant: Beaver Dam, KY 6/7/2026 10:44:50 AM	Tech: C. Russ PC: E. Bradley	
Structure ID: SF-97				
P2 MH048CN30X-SP		ECC XYPEX CONE w/ 24" HOLE-SPECIAL F/G		
P3) 24" - CASTING HEIGHT - 6" P2) 48" - ECC XYPEX CONE w/ 24" HOLE-SPECIAL F/G - 30" P1) 48" - MH BASE Custom Ht, w/XYPEX T/n - 52" 1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE XYPEX C-500 NF RED 1) CASTING - JBS 1155 F/C SANITARY 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0820 1) PSX - 12-08 NYLO		0 lb 1981 lb 4410 lb 1440 lb 0 lb 0 lb 0 lb 250 lb 0 lb 0 lb 0 lb 2 lb 8 lb ----- Structure Total: 8091 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. XYPEX C-500 ADMIXTURE REQUIRED 5. NO STEPS 6. JBS 1155 FRAME & COVER "SANITARY" SUPPLIED BY ICAST	
				
 48" - ECC XYPEX CONE w/ 24" HOLE-SPECIAL F/G - 30" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 1981 lb Volume (Net): 0.51cu.yd
