


Job Name: 25-2541 WARTRACE CREEK INTERCEPTOR Job Location: Springfield, TN Contractor: Cumberland Pipeline LLC					Plant: Beaver Dam 8/7/2025 12:34:43 PM		Tech: C. Russ PC: E.Bradley				
Structure ID: SF-99											
P1 MH048BAVFX MH BASE Custom Ht, w/XYPEX T/n											
P3) 24" - CASTING HEIGHT - 6" P2) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 42" P1) 48" - MH BASE Custom Ht, w/XYPEX T/n - 69" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - DBL 1"x14.5' Butyl (2x) 2) A-Lok - 0820 1) PSX - 8QRS-S NYLO						0 lb 3095 lb 5645 lb 1440 lb 0 lb 0 lb 0 lb 2 lb 6 lb ----- Structure Total: 10189 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. JBS 1155 "SANITARY" PROVIDED BY ICAST 4. NO STEPS REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 599.7' Rim to Invert: 9.64' Slack: 0.68" Sump: 2" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	590.06'	0°	0"	24" DI	25.75"	A-Lok 0820	27"	28.676"	0.5"	0"	
Invert 2	590.06'	190°	96.168"	24" DI	25.75"	A-Lok 0820	27"	28.676"	0.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

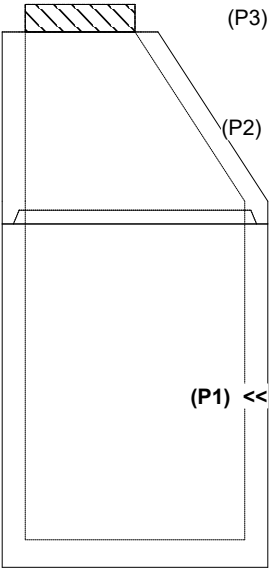


(P3)

(P2)

(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

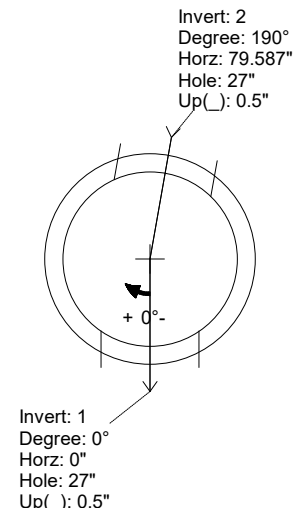

Invert: 2
Degree: 190°
Horz: 79.587"
Hole: 27"
Up(): 0.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 27"
Up(): 0.5"


UPSIDE-DOWN VIEW (int. dimensions)

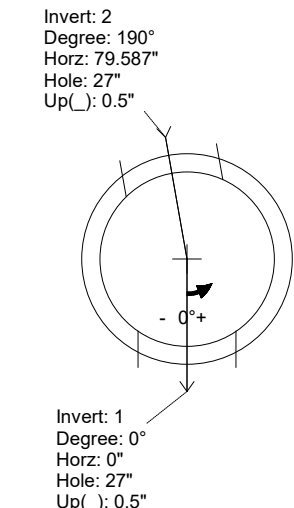

Invert: 2
Degree: 190°
Horz: 79.587"
Hole: 27"
Up(): 0.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 27"
Up(): 0.5"

INSIDE WALL DIMENSIONS

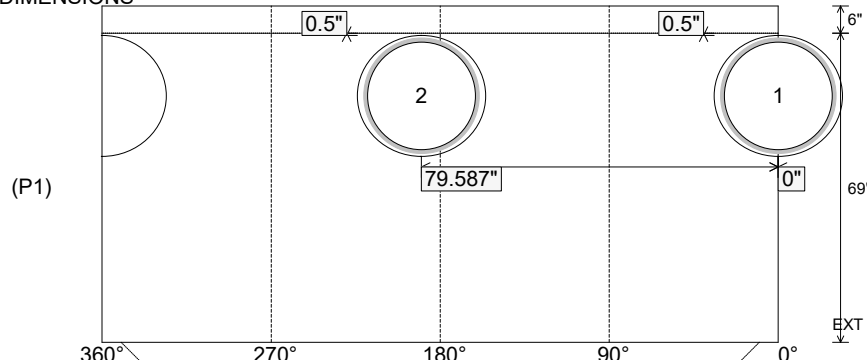

(P1)

0.5"

0.5"

79.587"

0"

69"


6"

EXT

360° 270° 180° 90° 0°

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 69" Height (Ext): 75"	Weight (Net): 5645 lb Volume (Net): 1.44cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-2541 WARTRACE CREEK INTERCEPTOR Job Location: Springfield, TN Contractor: Cumberland Pipeline LLC					Plant: Beaver Dam 8/7/2025 12:34:50 PM		Tech: C. Russ PC: E.Bradley				
Structure ID: SF-99											
P1 MH048BAVFX MH BASE Custom Ht, w/XYPEX T/n											
P3) 24" - CASTING HEIGHT - 6" P2) 48" - ECC XYPEX CONE w/ 24" HOLE F/G - 42" P1) 48" - MH BASE Custom Ht, w/XYPEX T/n - 69" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - DBL 1"x14.5' Butyl (2x) 2) A-Lok - 0820 1) PSX - 8QRS-S NYLO						0 lb 3095 lb 5645 lb 1440 lb 0 lb 0 lb 0 lb 2 lb 6 lb ----- Structure Total: 10189 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. JBS 1155 "SANITARY" PROVIDED BY ICAST 4. NO STEPS REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 599.7' Rim to Invert: 9.64' Slack: 0.68" Sump: 2" Step Position:						INVERT					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	590.06'	0°	0"	24" DI	25.75"	A-Lok 0820	27"	28.676"	0.5"	0"	
Invert 2	590.06'	190°	96.168"	24" DI	25.75"	A-Lok 0820	27"	28.676"	0.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

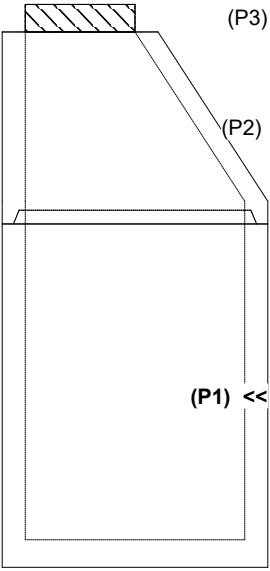


(P3)

(P2)

(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

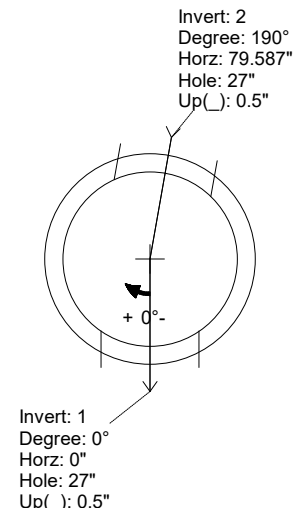

Invert: 2
Degree: 190°
Horz: 79.587"
Hole: 27"
Up(): 0.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 27"
Up(): 0.5"


UPSIDE-DOWN VIEW (int. dimensions)

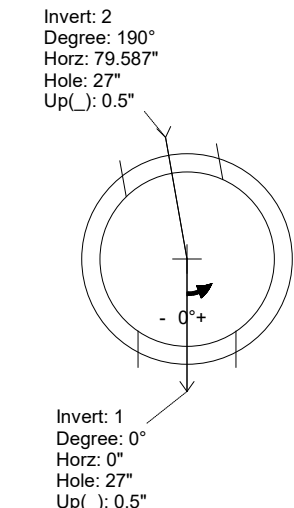

Invert: 2
Degree: 190°
Horz: 79.587"
Hole: 27"
Up(): 0.5"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 27"
Up(): 0.5"

INSIDE WALL DIMENSIONS

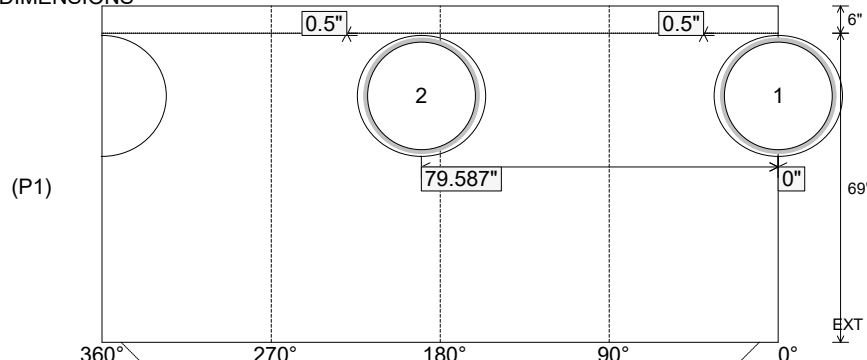

(P1)

0.5"

0.5"

79.587"

69"

6"

EXT

360° 270° 180° 90° 0°

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 69" Height (Ext): 75"	Weight (Net): 5645 lb Volume (Net): 1.44cu.yd
----------------------------------	---------------------------------	--	--	--
