

Job Name: 25-2621 Night Hawk Place Lot 2G Storm
 Job Location: Radcliff, KY
 Contractor: City of Radcliff

Plant: Beaver Dam
 11/13/2025 1:45:57 PM

Tech: C.Russ
 PC: J.Jarvis



Structure ID: JB G

P2 MH060RSVF

MH RISER Custom Ht

- P4) 24" - CASTING HEIGHT - 4"
- P3) 60" - MH FLAT TOP w/ 24" ECC Hole - 13"
- P2) 60" - MH RISER Custom Ht - 35"
- P1) 60" - MH BASE - 48"
- 2) 60" - SGL 1"x14.5' Butyl (2x)
- 2) Hole - 38
- 4) MH Step ML-10-TDS-NCR - 10"

- Structure Notes:
1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. HOE KY-206 BY ICAST
 4. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .18)
 - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.



0 lb
 2869 lb
 3654 lb
 6524 lb
 0 lb
 0 lb
 0 lb

 Structure Total: 13047 lb


Rim: 741' Rim to Invert: 8.11' Slack: 0.37" Sump: 3.05" Step Position: 90°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

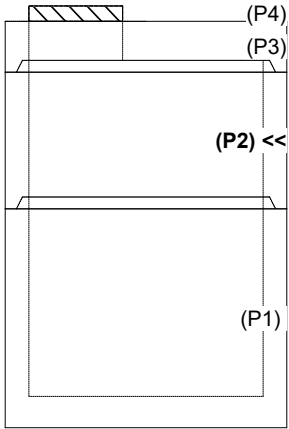

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 6" Floor Height: 0"	Height (Int): 35" Height (Ext): 35"	Weight (Net): 3654 lb Volume (Net): 0.93cu.yd
----------------------------------	------------------------------------	--	--	--
