


Structure ID: A2			
Spec: Storm	Rim: 504.1'	Sump: 2.25"	Floor (Bot): 500.113'
Type: BX 6inW, 6inF	Invert: 500.8'	Floor (Top): 500.613'	Overall Height: 3.958'
Size: 28" x 28"	Rim to Invert: 3.3'	Floor Height: 6"	Slack: 0.35"

Structure Notes:


1. (JBS 3300 SINGLE SET PROVIDED BY OTHERS)
2. PER ASTM C913 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:	
P2) 28" x 28" - CASTING HEIGHT - 7.50"	0 lb
P1) 28" x 28" - BOX BASE 6inW, 6inF, Variable Ht - 34"	2942 lb
1) 28" x 28" - Conseal CS-102 1.00"	0 lb
1) Hole - 22	0 lb


Structure Total:	2942 lb

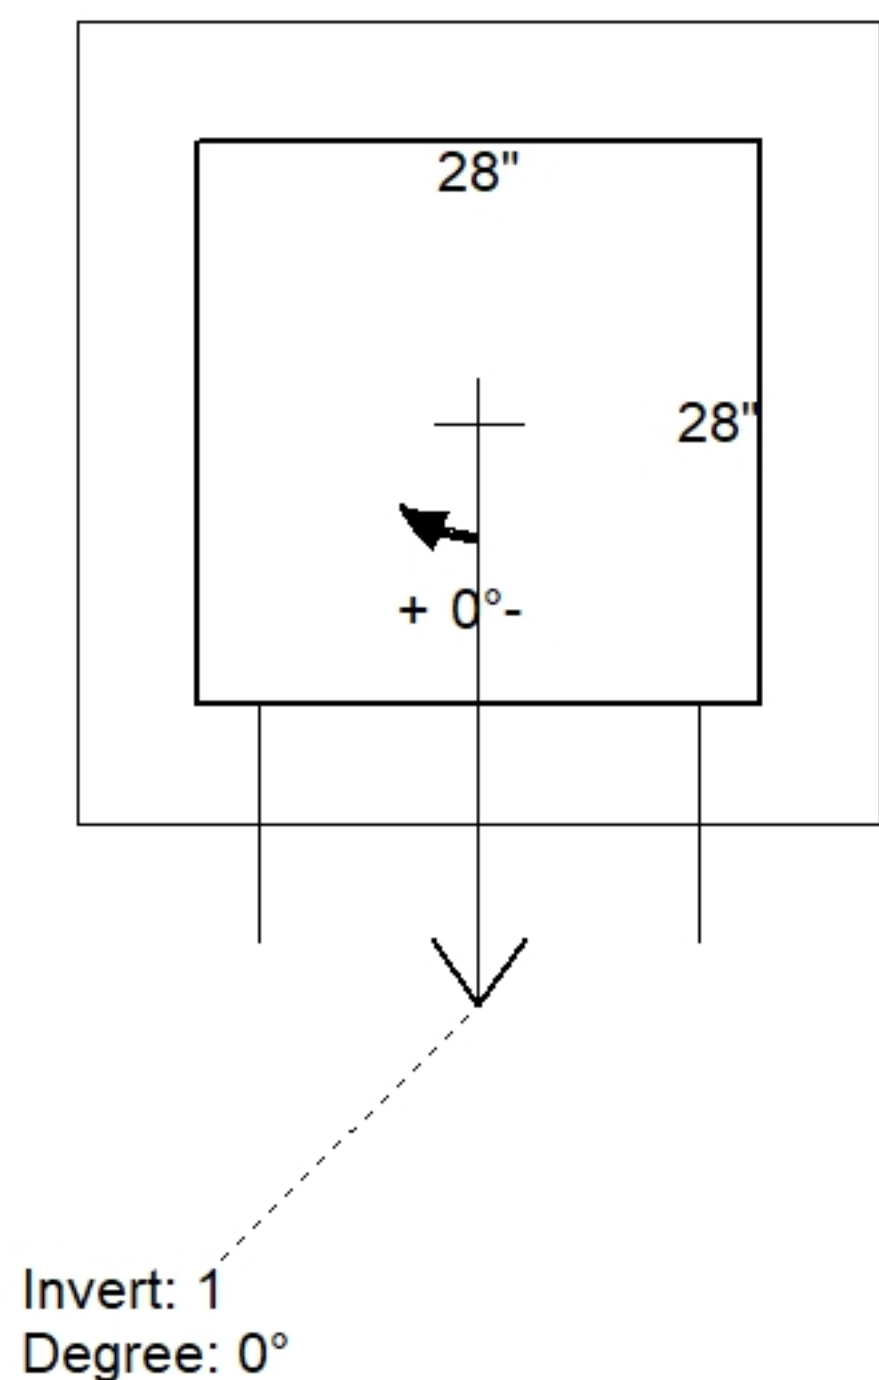

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	504.1'							
Reducer								
Invert 1	500.8'	0°	15" RCP B WALL	19.5"	22"	Hole 22	0"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

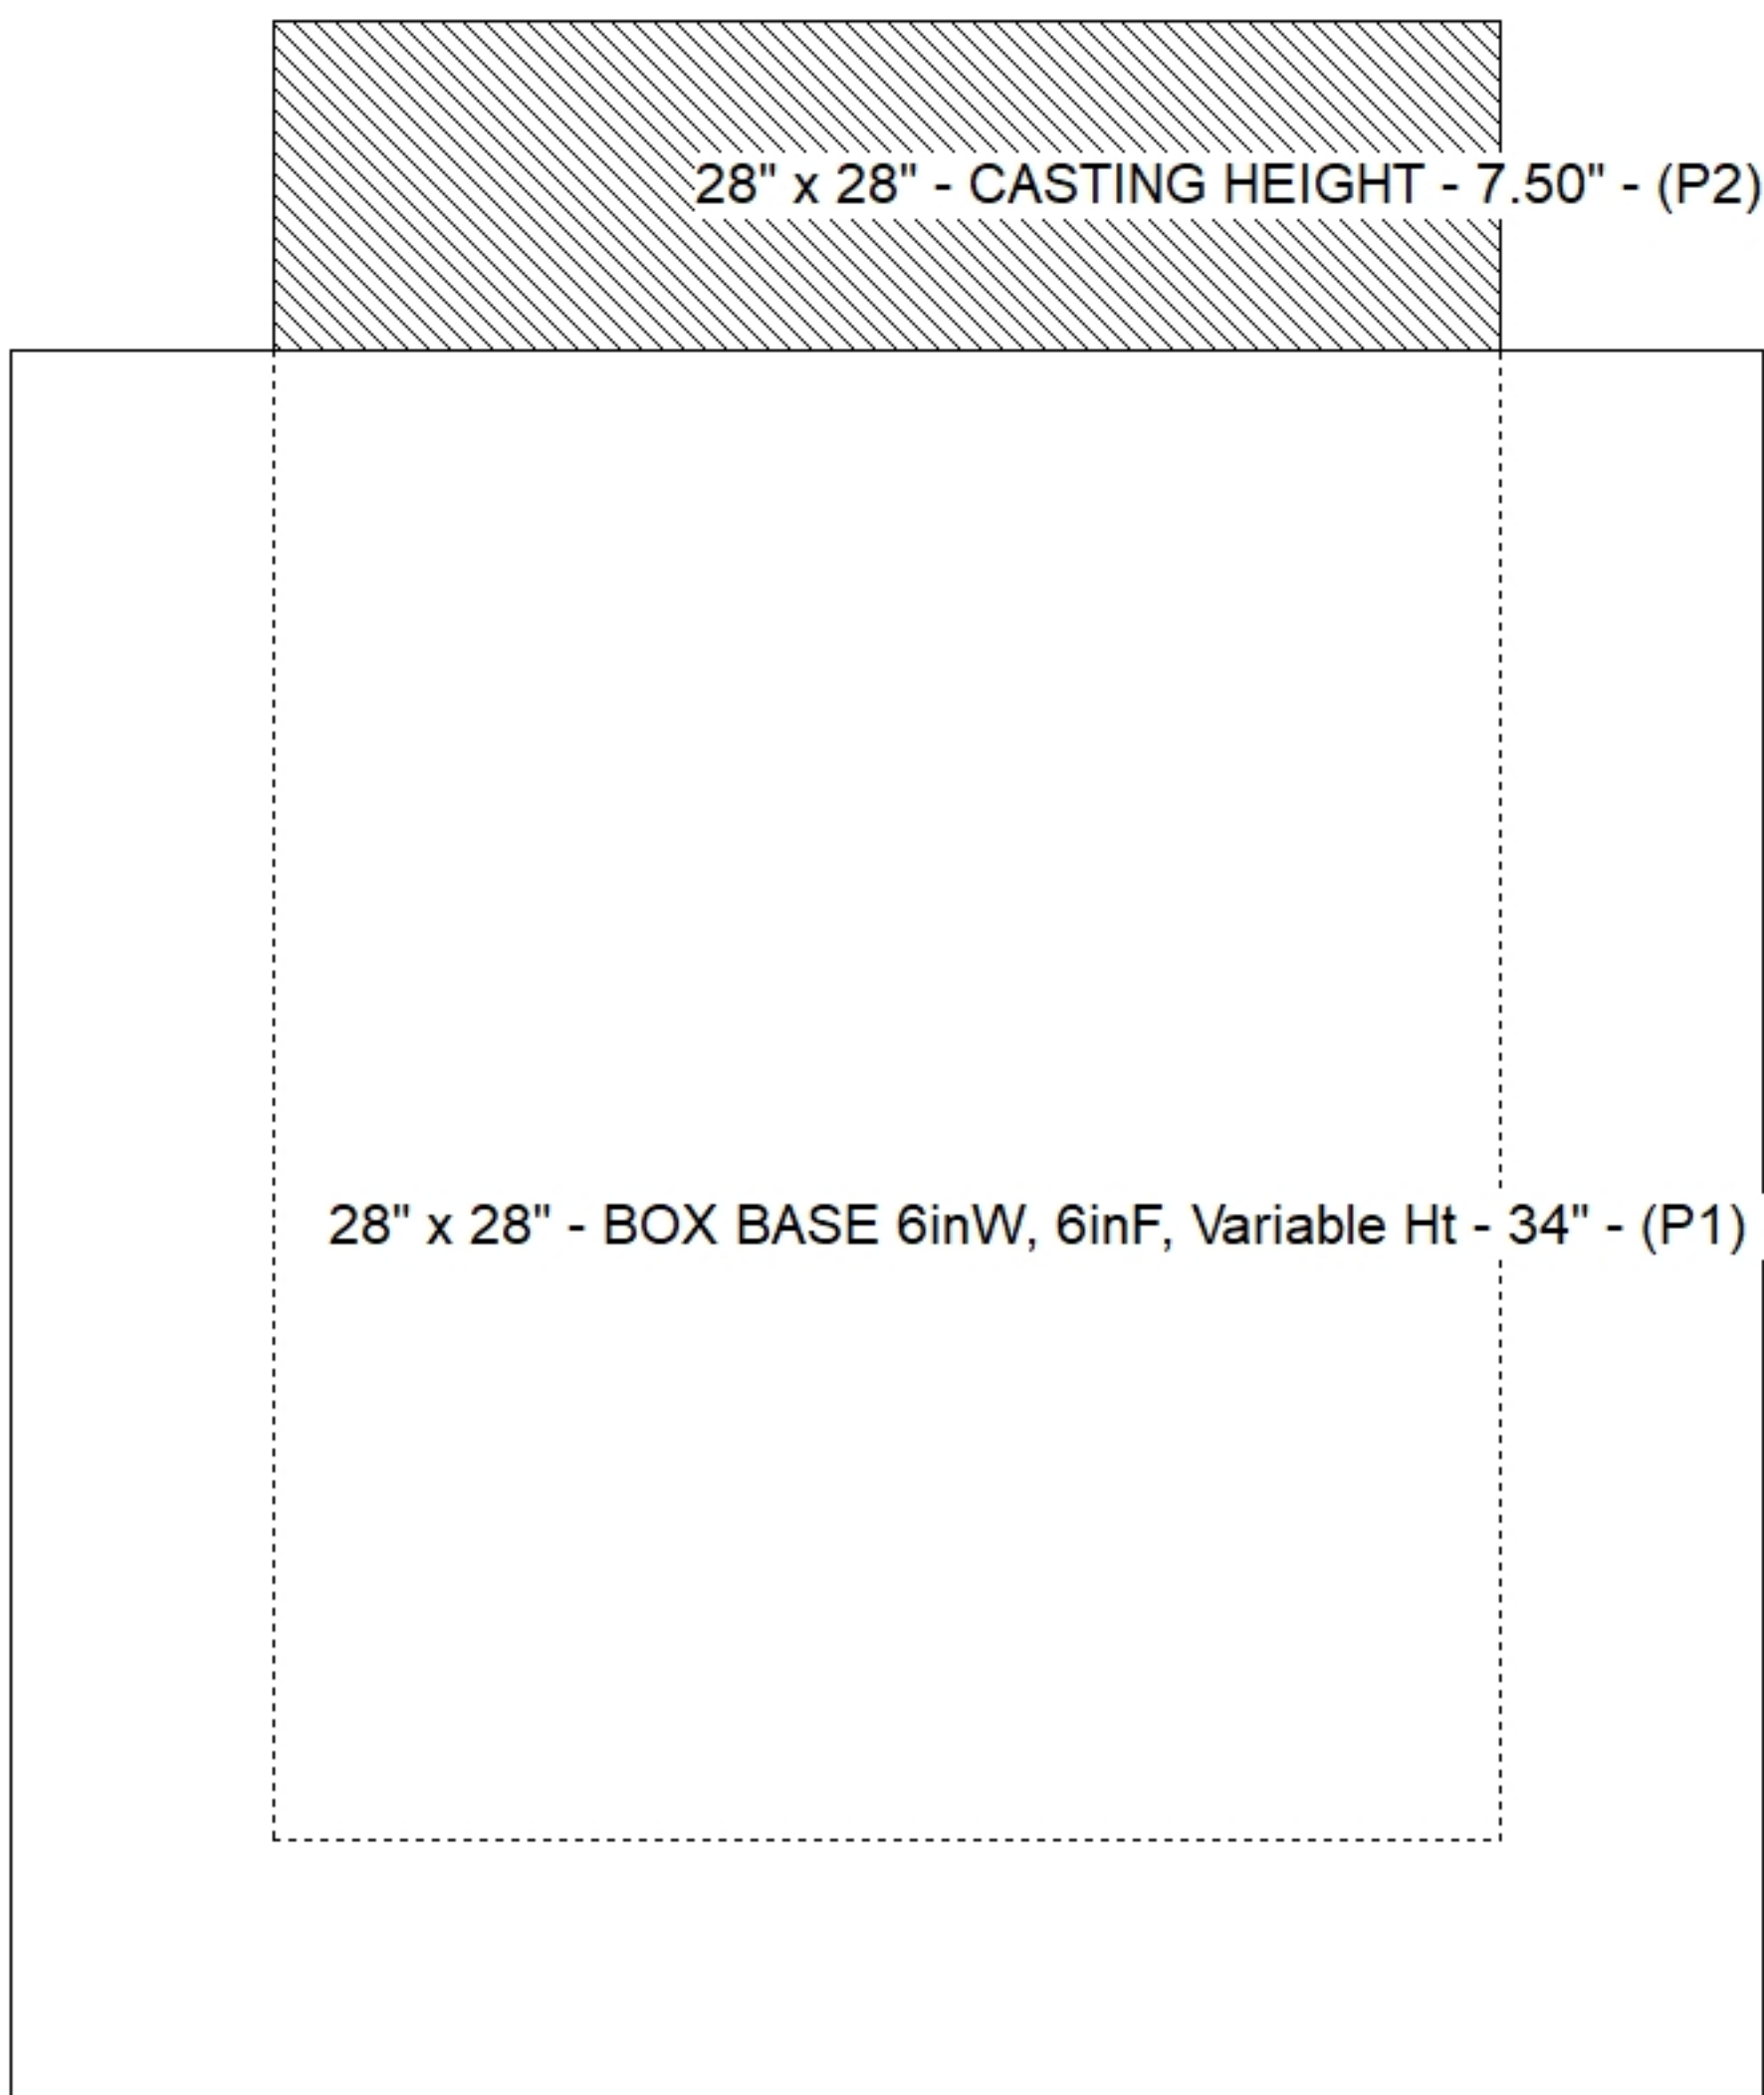

Default - Interior Dimensions

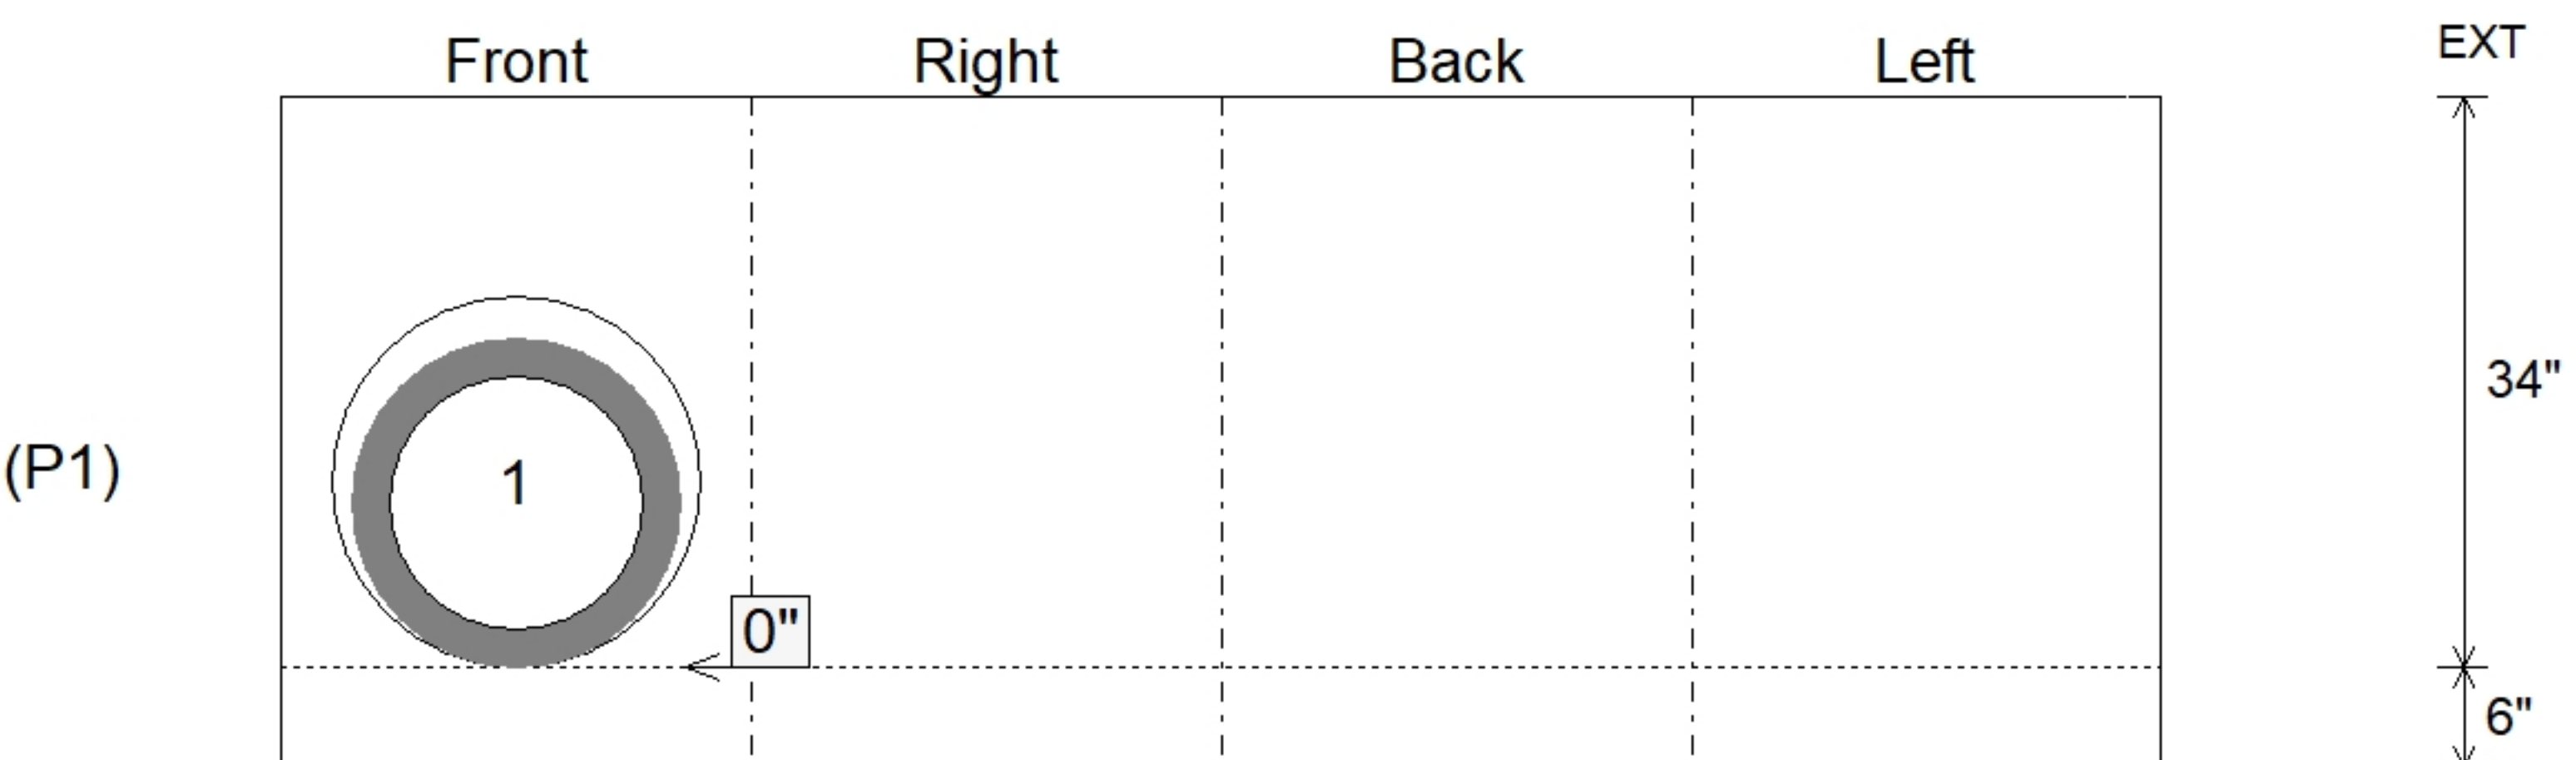

Submittal Drawing 10/5/2026 12:14:41 PM	SUBMITTAL APPROVED BY:
--	---------------------------
