




Job Name: 25-2647 Nichols West Job Location: Gallatin, TN Contractor: Hayes Pipe Supply				Plant: Beaver Dam 10/1/2026 10:32:42 AM		Tech: J. Coppage PC: E. Bradley				
Structure ID: B5										
P1 BX28280606VH				BOX BASE 6inW, 6inF, Variable Ht						
P2) 28" x 28" - CASTING HEIGHT - 7.50" P1) 28" x 28" - BOX BASE 6inW, 6inF, Variable Ht - 34" 1) 28" x 28" - Conseal CS-102 1.00" 1) Hole - 22						0 lb 2942 lb 0 lb 0 lb ----- Structure Total: 2942 lb		Structure Notes: . 1. (JBS 3300 SINGLE SET PROVIDED BY OTHERS) 2. PER ASTM C913 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Rim: 524.5' Rim to Invert: 3.3' Slack: 0.35" Sump: 2.25" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	521.2'	0°	20"	15" RCP B WALL	19.5"	Hole 22	22"	22"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										



RIGHT-SIDE UP VIEW (int. dimensions)



UPSIDE-DOWN VIEW (int. dimenions)

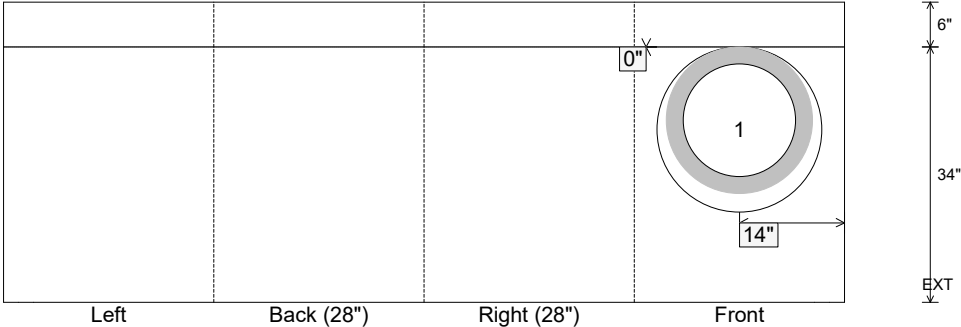

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 6" Floor Height: 6"	Height (Int): 34" Height (Ext): 40"	Weight (Net): 2942 lb Volume (Net): 0.75cu.yd
----------------------------------	-------------------------------	--	--	--
