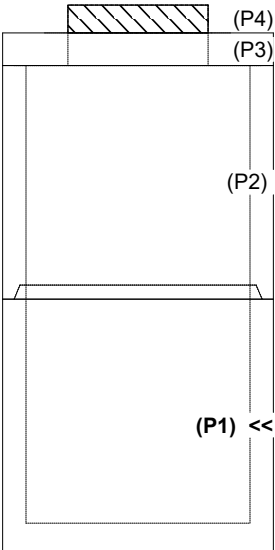
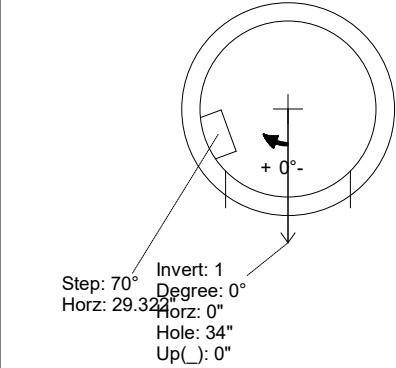
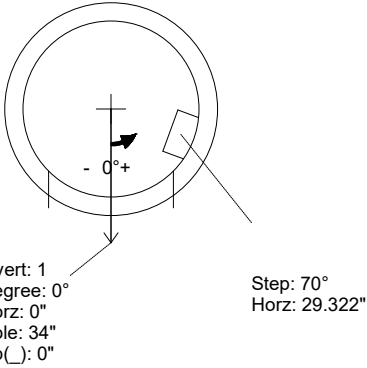
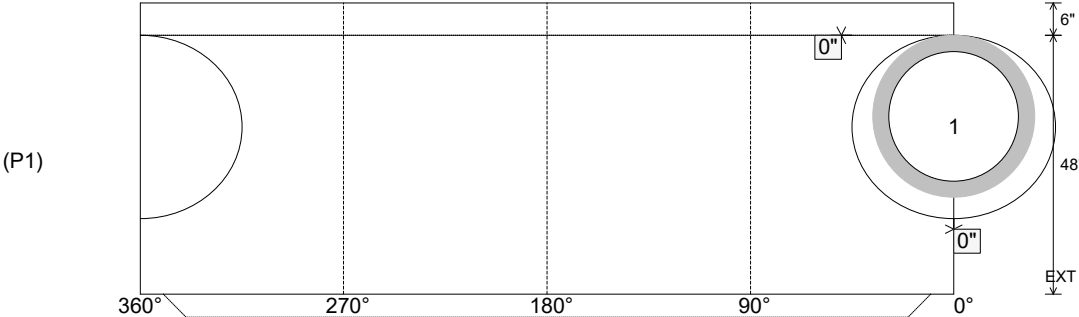


Job Name: 25-2647 Nichols West Job Location: Gallatin, TN Contractor: Hayes Pipe Supply					Plant: Beaver Dam 10/1/2026 10:32:44 AM		Tech: J. Coppage PC: E. Bradley																												
Structure ID: C1																																			
P1		MH048BA48																																	
P4) 30" x 30" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/30"x30" Hole - 7" P2) 48" - MH RISER Custom Ht - 50" P1) 48" - MH BASE - 48" 2) 48" - Conseal CS-102 1.00" 1) 30" x 30" - Conseal CS-102 1.00" 2) Hole - 34 8) MH Step ML-10-TDS-NCR - 10"					0 lb 1264 lb 3078 lb 4268 lb 0 lb 0 lb 0 lb 0 lb 0 lb 8610 lb		Structure Notes: 1. (JBS 4310 F/G PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.																												
Rim: 516.1'					Rim to Invert: 9'		Slack: 0"		Sump: 3"		Step Position: 70																								
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset																									
Invert 1	507.1'	0°	0"	24" RCP B WALL	30"	Hole 34	34"	37.782"	0"	0"																									
Invert 2																																			
Invert 3																																			
Invert 4																																			
Invert 5																																			
Invert 6																																			
Invert 7																																			
Invert 8																																			
RIGHT-SIDE UP VIEW (int. dimensions)												UPSIDE-DOWN VIEW (int. dimenions)																							
																																			
INSIDE WALL DIMENSIONS																																			
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a				Wall Thickness: 5" Floor Height: 6"				Height (Int): 48" Height (Ext): 54"				Weight (Net): 4268 lb Volume (Net): 1.09cu.yd																			
