




Job Name: 25-2647 Nichols West Job Location: Gallatin, TN Contractor: Hayes Pipe Supply					Plant: Beaver Dam 10/1/2026 10:50:01 AM		Tech: J. Coppage PC: E. Bradley				
Structure ID: C1											
P2		MH048RSVF		MH RISER Custom Ht							
P4) 30" x 30" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/30"x30" Hole - 7" P2) 48" - MH RISER Custom Ht - 50" P1) 48" - MH BASE - 48" 2) 48" - Conseal CS-102 1.00" 1) 30" x 30" - Conseal CS-102 1.00" 2) Hole - 34 8) MH Step ML-10-TDS-NCR - 10"					0 lb 1264 lb 3078 lb 4268 lb 0 lb 0 lb 0 lb 0 lb ----- 8610 lb		Structure Notes: . 1. (JBS 4310 F/G PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 516.1' Rim to Invert: 9' Slack: 0" Sump: 3" Step Position: 70											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2	512.1'	180°	91.106"	24" RCP B WALL	30"	Hole 34	34"	37.782"	7.75"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

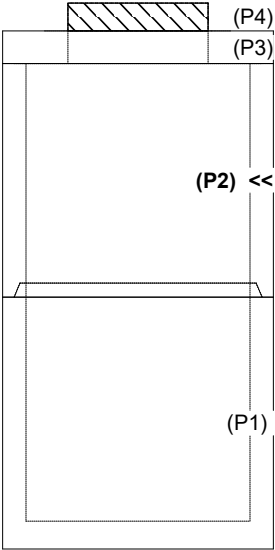

RIGHT-SIDE UP VIEW (int. dimensions)

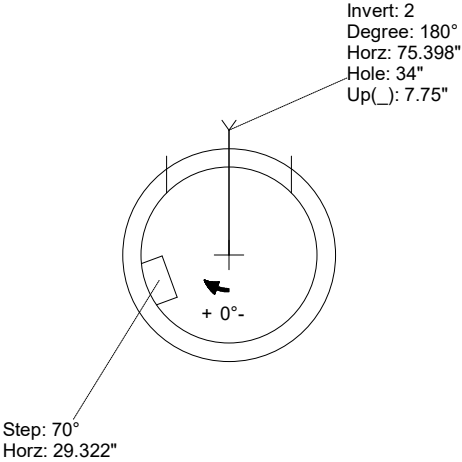

INSIDE WALL DIMENSIONS

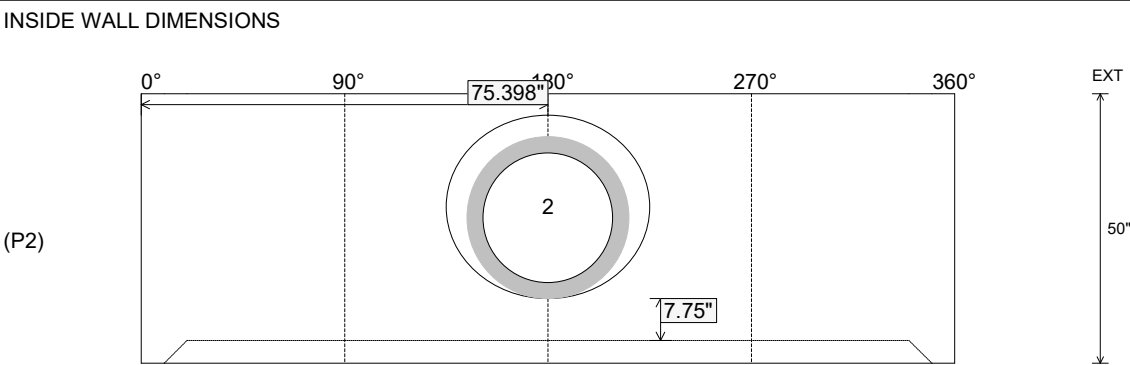

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 50" Height (Ext): 50"	Weight (Net): 3078 lb Volume (Net): 0.79cu.yd
----------------------------------	----------------------------------	--	--	--
