




Job Name: 25-2647 Nichols West Job Location: Gallatin, TN Contractor: Hayes Pipe Supply					Plant: Beaver Dam 10/1/2026 10:32:56 AM		Tech: J. Coppage PC: E. Bradley				
Structure ID: C17											
P1		BX28280606VH		BOX BASE 6inW, 6inF, Variable Ht							
P2) 28" x 28" - CASTING HEIGHT - 7.50" P1) 28" x 28" - BOX BASE 6inW, 6inF, Variable Ht - 31" 1) 28" x 28" - Conseal CS-102 1.00" 2) Hole - 22"					0 lb 2545 lb 0 lb 0 lb ----- Structure Total: 2545 lb		Structure Notes: 1. (JBS 3300 SINGLE SET PROVIDED BY OTHERS) 2. PER ASTM C913 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 535.8' Rim to Invert: 3.1' Slack: 0.956" Sump: 2.256" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	532.7'	0°	20"	15" RCP B WALL	19.5"	Hole 22	22"	22"	0.006"	0"	
Invert 2	532.8'	270°	20"	15" RCP B WALL	19.5"	Hole 22	22"	22"	1.206"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

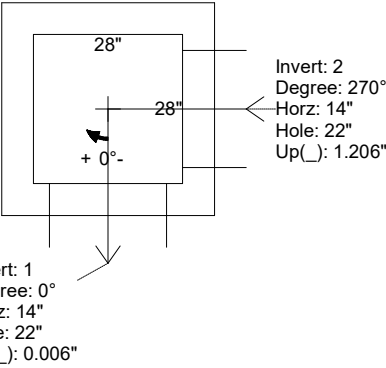

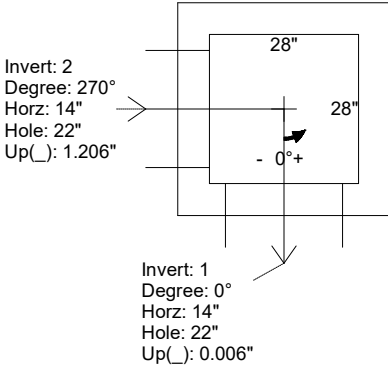

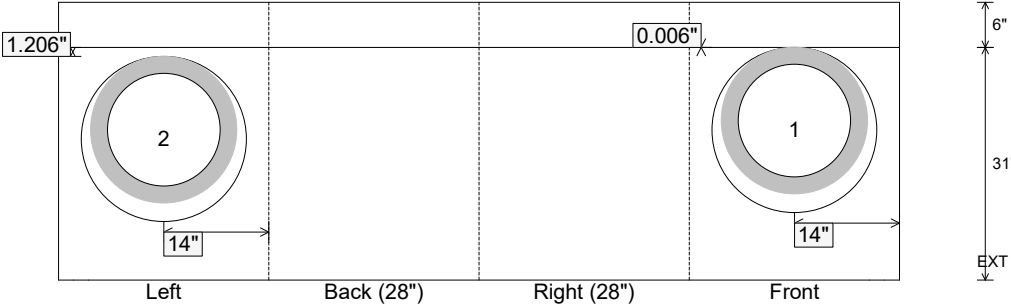

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 6" Floor Height: 6"	Height (Int): 31" Height (Ext): 37"	Weight (Net): 2545 lb Volume (Net): 0.65cu.yd
----------------------------------	-------------------------------	--	--	--
