




Job Name: 25-2647 Nichols West Job Location: Gallatin, TN Contractor: Hayes Pipe Supply					Plant: Beaver Dam 10/1/2026 10:32:58 AM		Tech: J. Coppage PC: E. Bradley				
Structure ID: C20											
P1 BX3636-08BAVF BOX BASE 8inW, 8inF, Variable Ht											
P3) 28" x 28" - CASTING HEIGHT - 7.50" P2) 36" x 36" - BX FLAT LID 8inW w/28"x28" HOLE - 8" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 25" 1) 36" x 36" - Conseal CS-102 1.00" 1) 28" x 28" - Conseal CS-102 1.00" 1) Hole - 22 1) DOGHOUSE INVRTD - 22"x23"						0 lb 1289 lb 4159 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5448 lb		Structure Notes: . 1. (JBS 3300 SINGLE SET PROVIDED BY OTHERS) 2. PER ASTM C913 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .40) #5 BARS AT 8" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 530.1' Rim to Invert: 3.2' Slack: 0.15" Sump: 2.25" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	526.9'	300°	29.464"	15" RCP B WALL	19.5"	Hole 22	22"	25.403"	0"	-10"	
Invert 2	527'	180°	26"	15" RCP B WALL	19.5"	DOGHOUSE INVRTD 22"x23"	22" x 23"	22"	1.2"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

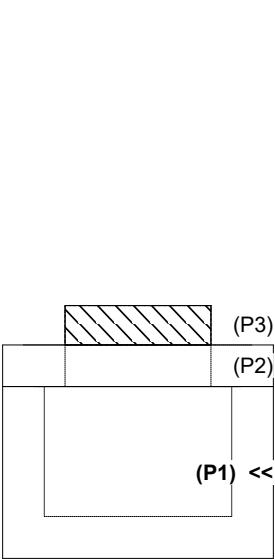

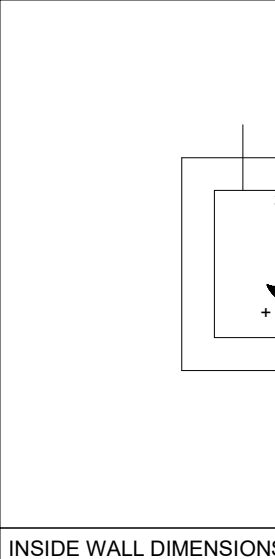

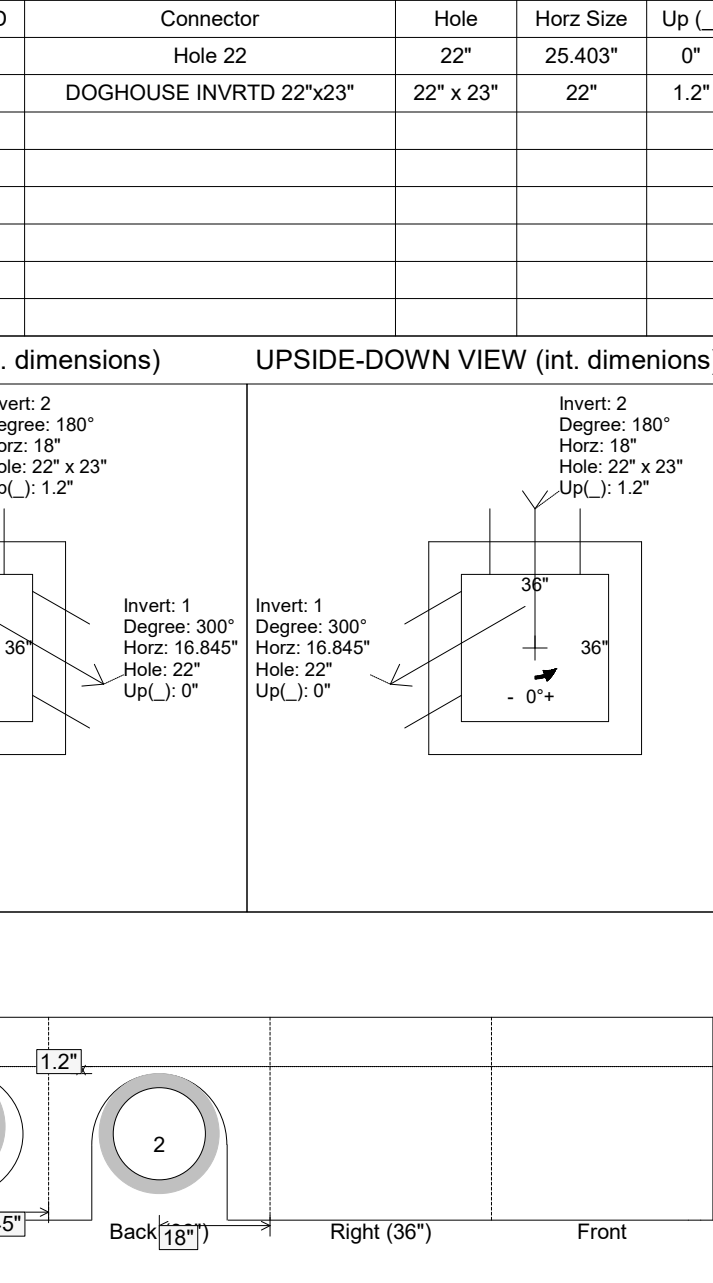

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 25" Height (Ext): 33"	Weight (Net): 4159 lb Volume (Net): 1.06cu.yd
----------------------------------	-------------------------------	--	--	--
