



Job Name: 25-2647 Nichols West Job Location: Gallatin, TN Contractor: Hayes Pipe Supply					Plant: Beaver Dam 10/1/2026 10:32:46 AM		Tech: J. Coppage PC: E. Bradley				
Structure ID: C3											
P1		MH072BA36		MH BASE							
P3) 30" x 64" - CASTING HEIGHT - 6" P2) 72" - MH FLAT TOP w/30"x64" Hole - 10" P1) 72" - MH BASE - 36" 1) 72" - Conseal CS-102 1.00" 1) DOGHOUSE INVRTD - 34"x36" 1) DOGHOUSE INVRTD - 34"x34" 3) MH Step ML-10-TDS-NCR - 10"					0 lb 3263 lb 7840 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 11103 lb		Structure Notes: . 1. (2X JBS 4310 F/G PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.				
Rim: 521.9'		Rim to Invert: 4.1'		Slack: 0.2"		Sump: 3"		Step Position: 90°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	517.8'	0°	0"	24" RCP B WALL	30"	DOGHOUSE INVRTD 34"x36"	34" x 36"	35.41"	0"	0"	
Invert 2	517.9'	180°	135.088"	24" RCP B WALL	30"	DOGHOUSE INVRTD 34"x34"	34" x 34"	35.41"	1.2"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

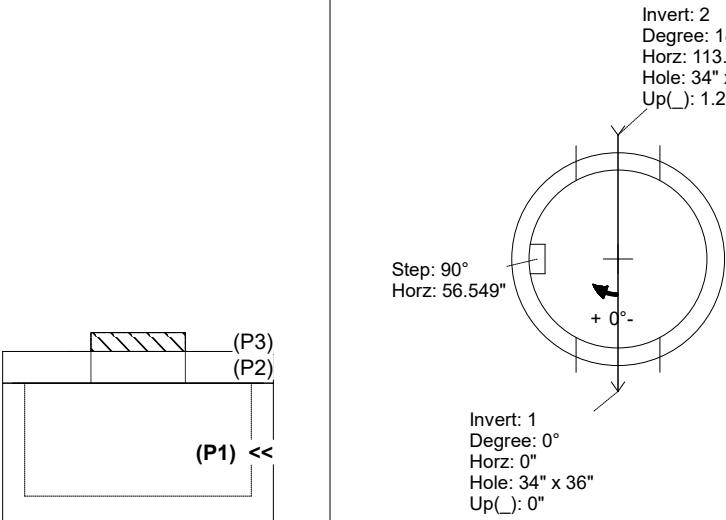

UPSIDE-DOWN VIEW (int. dimensions)

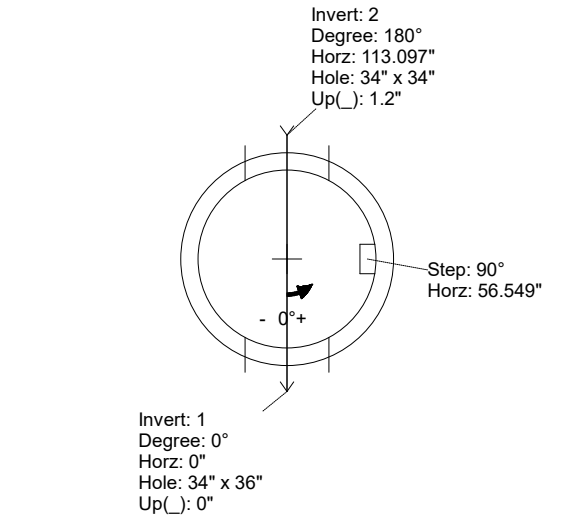

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 7" Floor Height: 8"	Height (Int): 36" Height (Ext): 44"	Weight (Net): 7840 lb Volume (Net): 2cu.yd
----------------------------------	-------------------------------	--	--	---
