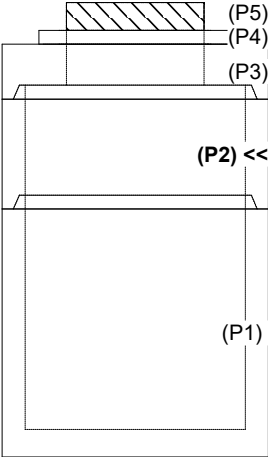

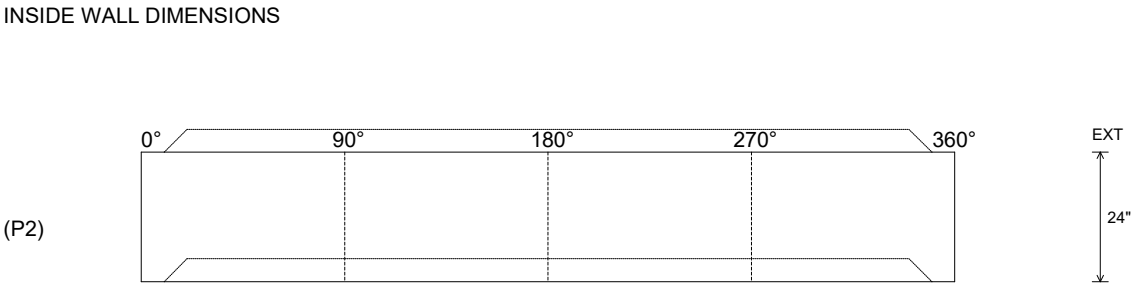


Job Name: 25-2647 Nichols West Job Location: Gallatin, TN Contractor: Hayes Pipe Supply					Plant: Beaver Dam 10/1/2026 10:50:02 AM		Tech: J. Coppage PC: E. Bradley				
Structure ID: C6											
P2		MH048RS24		MH RISER							
P5) 30" x 30" - CASTING HEIGHT - 6" P4) 30" x 30" - GRADE RING - 3" P3) 48" - MH FLAT TOP w/30"x30" Hole - 12" P2) 48" - MH RISER - 24" P1) 48" - MH BASE Custom Ht - 48" 2) 48" - Conseal CS-102 1.00" 2) 30" x 30" - Conseal CS-102 1.00" 1) Hole - 34 1) Hole - 22 1) Hole - 26 6) MH Step ML-10-TDS-NCR - 10"					0 lb 218 lb 1350 lb 1677 lb 3870 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 7115 lb		Structure Notes: . 1. (JBS 4310 F/G PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 531'		Rim to Invert: 7.5'		Slack: 0"		Sump: 3"		Step Position: 90°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 24" Height (Ext): 24"		Weight (Net): 1677 lb Volume (Net): 0.43cu.yd	
