

Job Name: 25-2647 Nichols West



Plant: Beaver Dam

Job Location: Gallatin, TN


Structure ID: D2

Spec: ~~Contractor: Hayes Pipe Supply~~ (Top): 503.3

Type: ~~SMV MH~~ Invert: 504.3' (Top): 504.3' Overall Height: 5.542'

Size: ~~72" RCP~~ to Invert Elevation: 504.3' Height: 8' (Slack: 0.12')

OTHERS)
2. PER ASTM C478

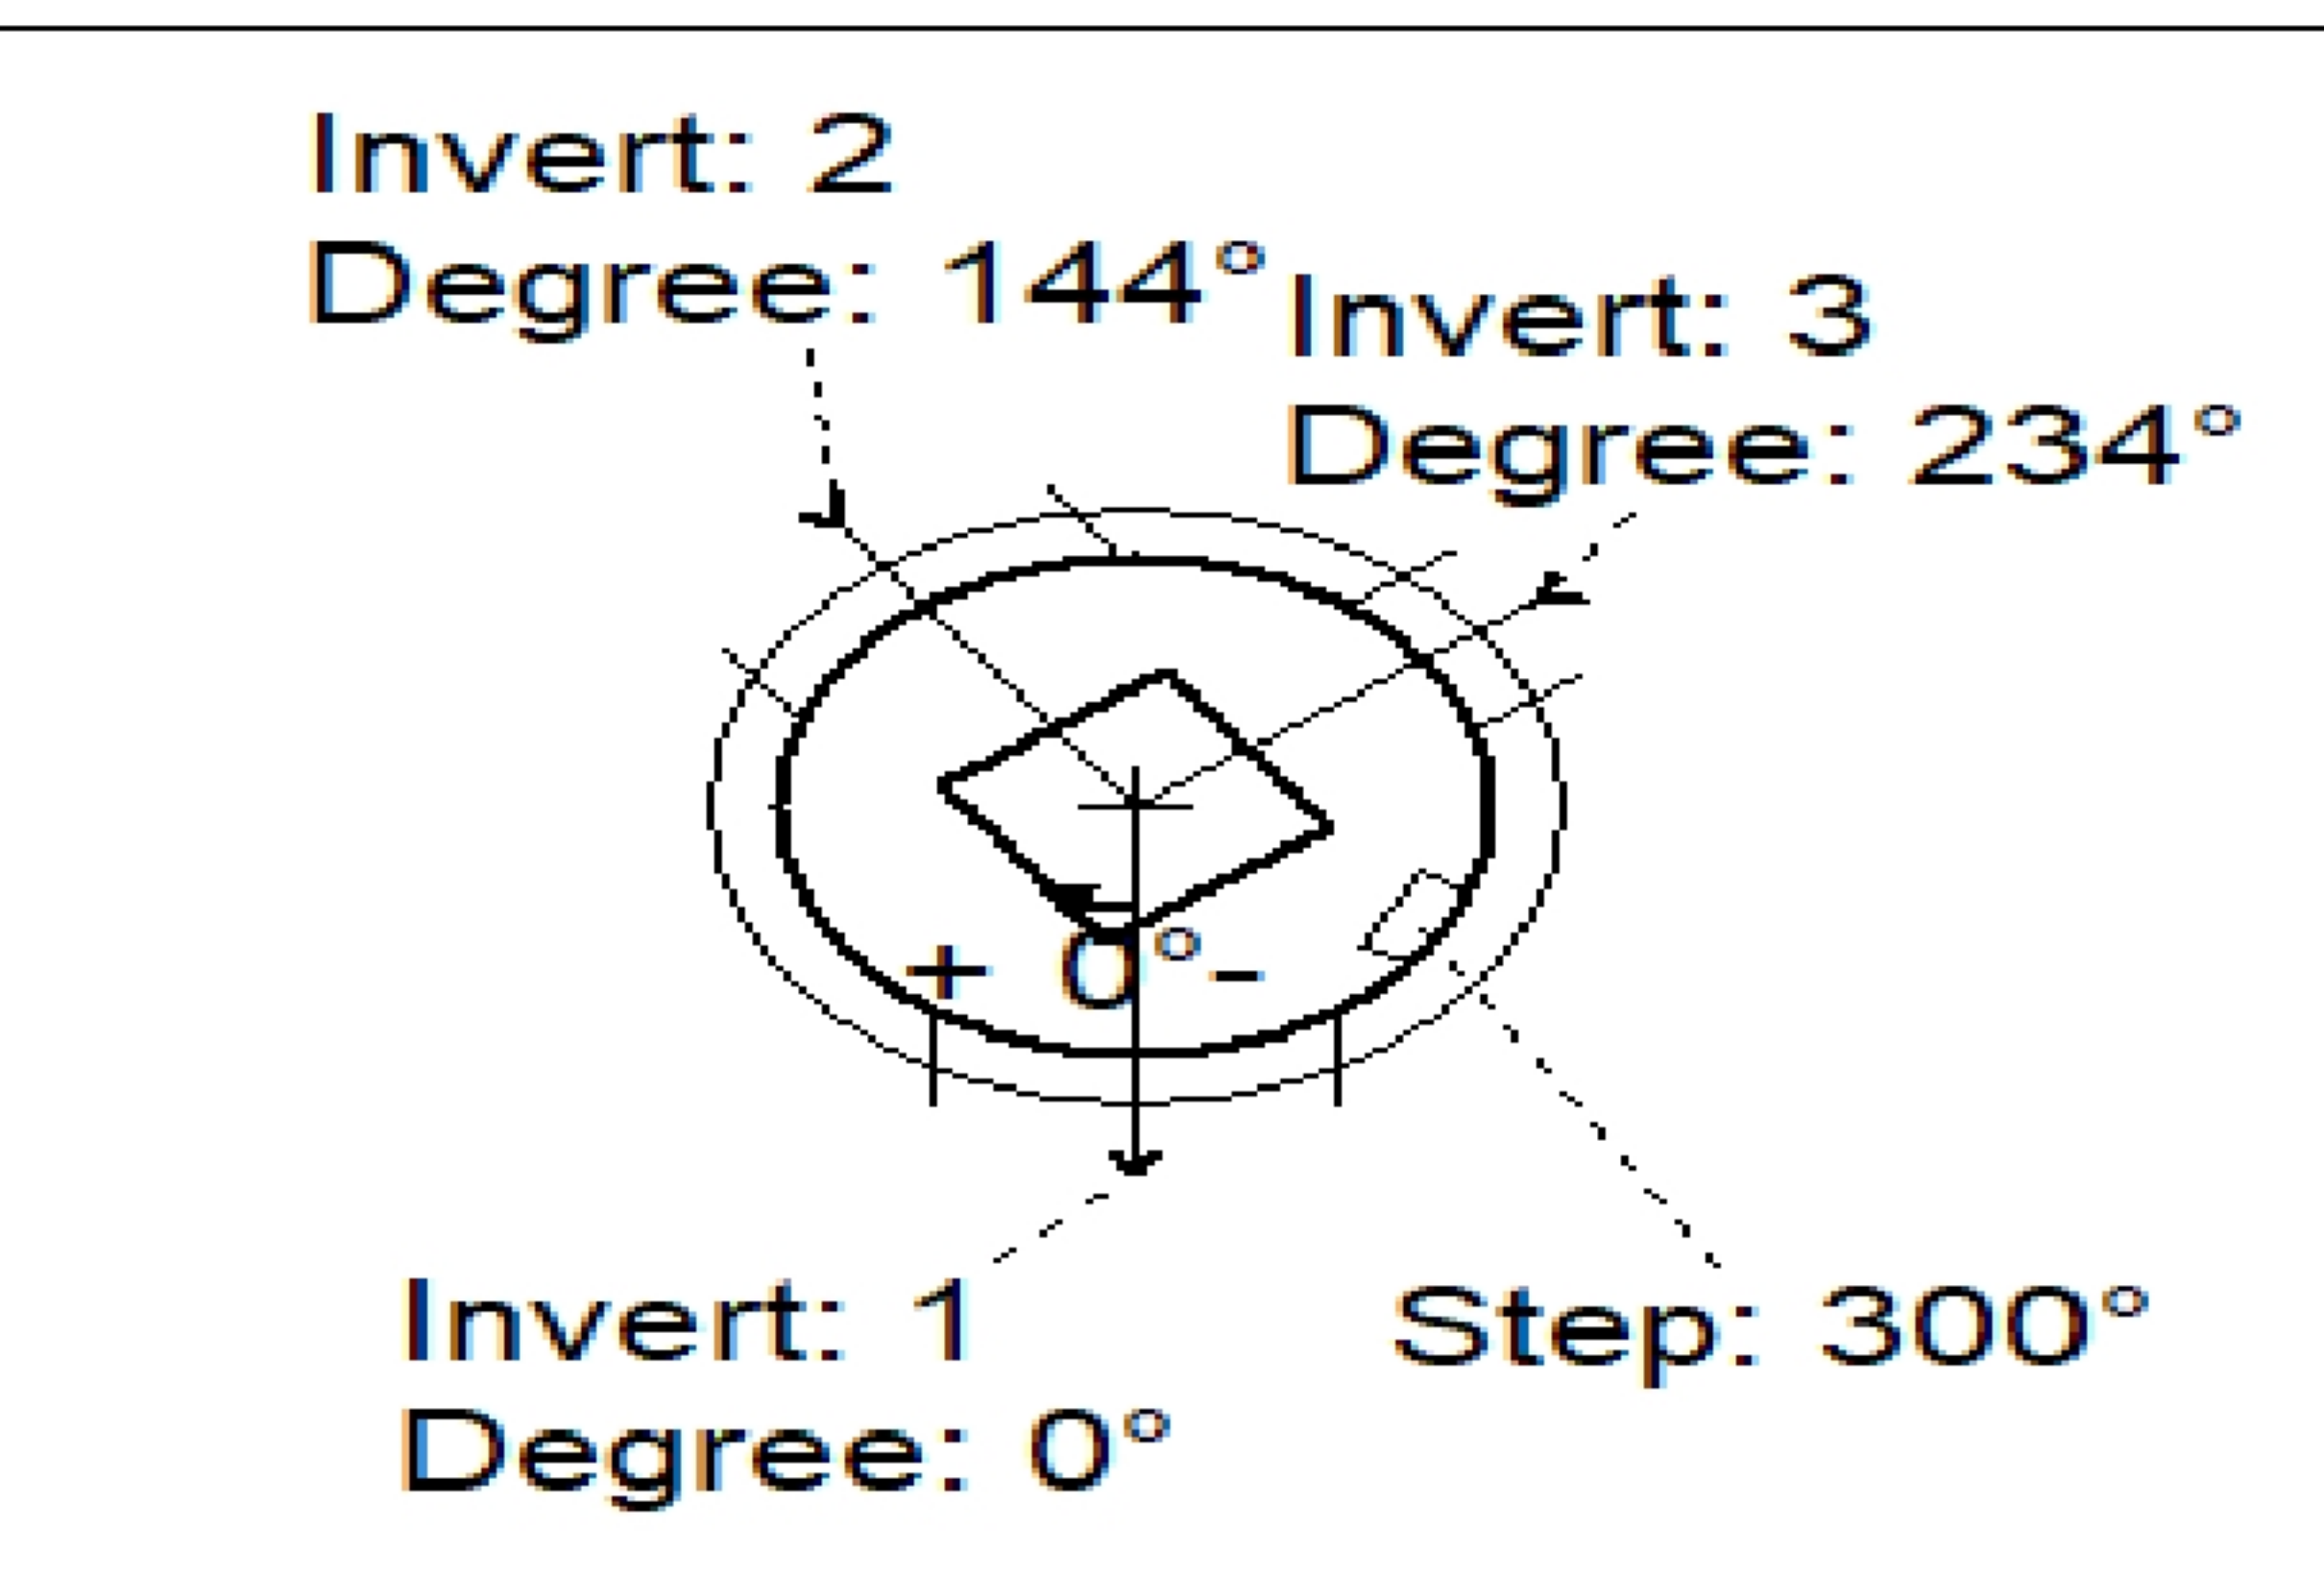

CASTING HEIGHT - 7.50" - (P3)
w/(2) 28"x28" Holes - 10" - (P2)
MH BASE Custom Ht - 41" - (P1)


STRUCTURE SUMMARY:

- 1) 72" - MH BASE Custom Ht - 4868 lb
- 1) 72" - Conseal CS-102 1.00" 0 lb
- 1) 28" x 28" - Conseal CS-102 1.00'0 lb
- 1) DOGHOUSE INVRTD - 40"x41" 0 lb
- 1) DOGHOUSE INVRTD - 40"x39" 0 lb
- 1) Hole - 22 0 lb
- 3) MH Step ML-10 TDS-NCR - 10" 0 lb

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (L)	Ref
Rim	508.9'							
Reducer								
Invert 1	504.3'	0°	30" RCP B WALL	37"	40" x 41"	DOGHOUSE INVRTD 40"x41"	0"	P1
Invert 2	504.4'	144°	30" RCP B WALL	37"	40" x 39"	DOGHOUSE INVRTD 40"x39"	1.2"	P1
Invert 3	504.4'	234°	15" RCP B WALL	19.5"	22"	Hole 22	2.45"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Structure Total: 11428 lb

Default - Interior Dimensions

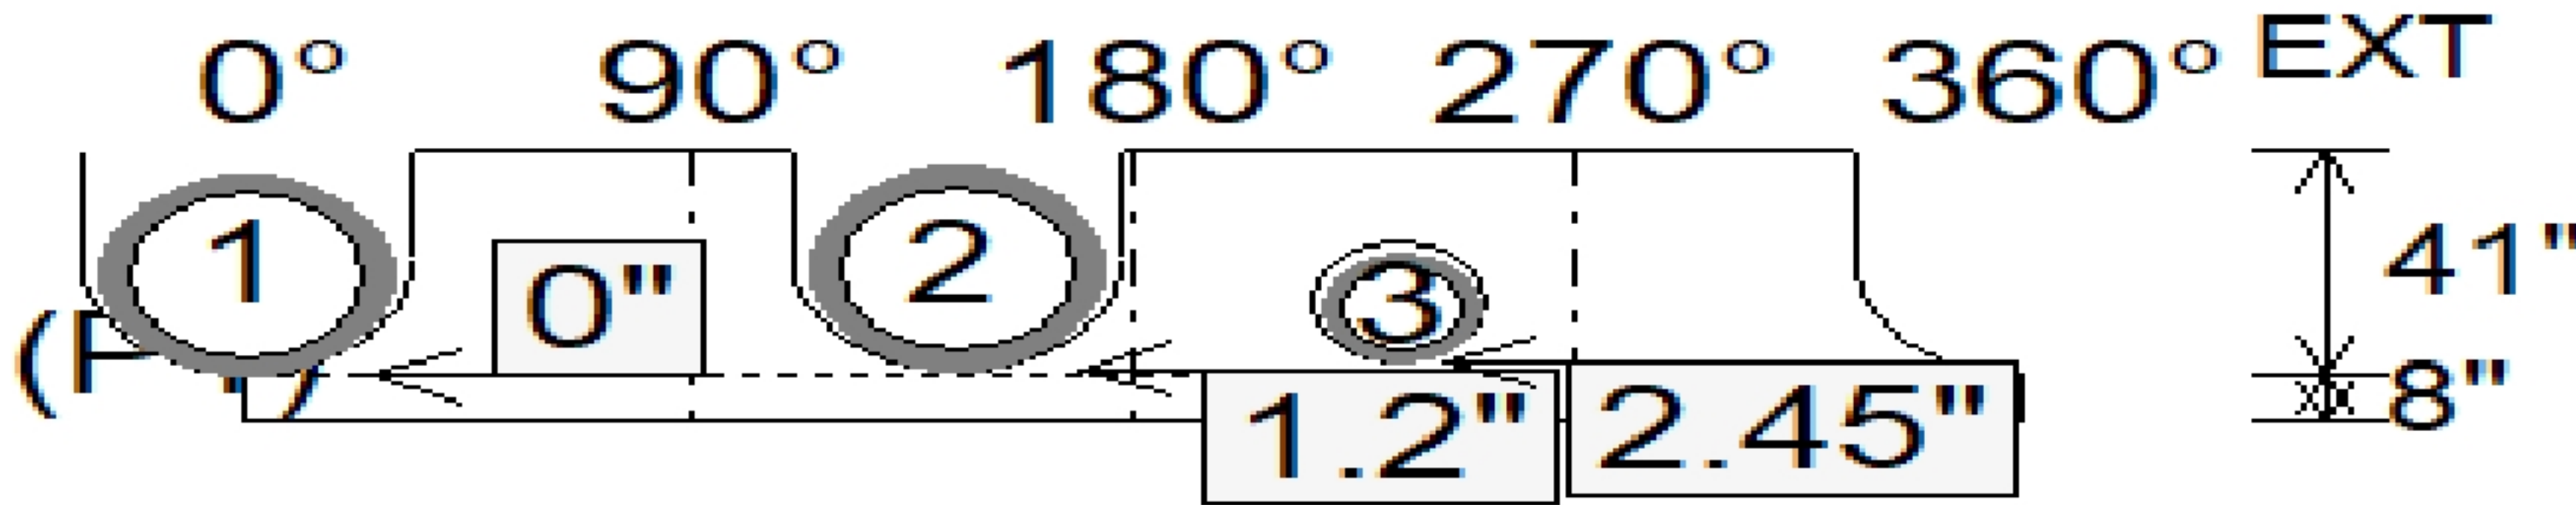

BY:
