

Structure ID: CB6

P1 BX3232-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

P2) 32" x 32" - CASTING HEIGHT - 7" P1) 32" x 32" - BOX BASE 8inW, 8inF, Variable Ht F/n - 43" 2) Hole - 26	0 lb 5452 lb 0 lb <hr style="width: 50px; margin: 0;"/> Structure Total: 5452 lb
---	---

Structure Notes:

1. JBS-3123 MOD. PROVIDED BY ICAST
2. PER TDOT D-CB-12LP / ASTM C913 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).

**** PER TDOT STD DRAWING D-CB-12LP ****




- WALLS (As .62) #5 BARS AT 6" C.C.E.W.
- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

Rim: 886.28' Rim to Invert: 3.98' Slack: 0.26" Sump: 2.5" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	882.3'	270°	24"	18" RCP B WALL	23"	Hole 26	26"	26"	0"	0"
Invert 2	882.4'	90°	24"	18" RCP B WALL	23"	Hole 26	26"	26"	1.25"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

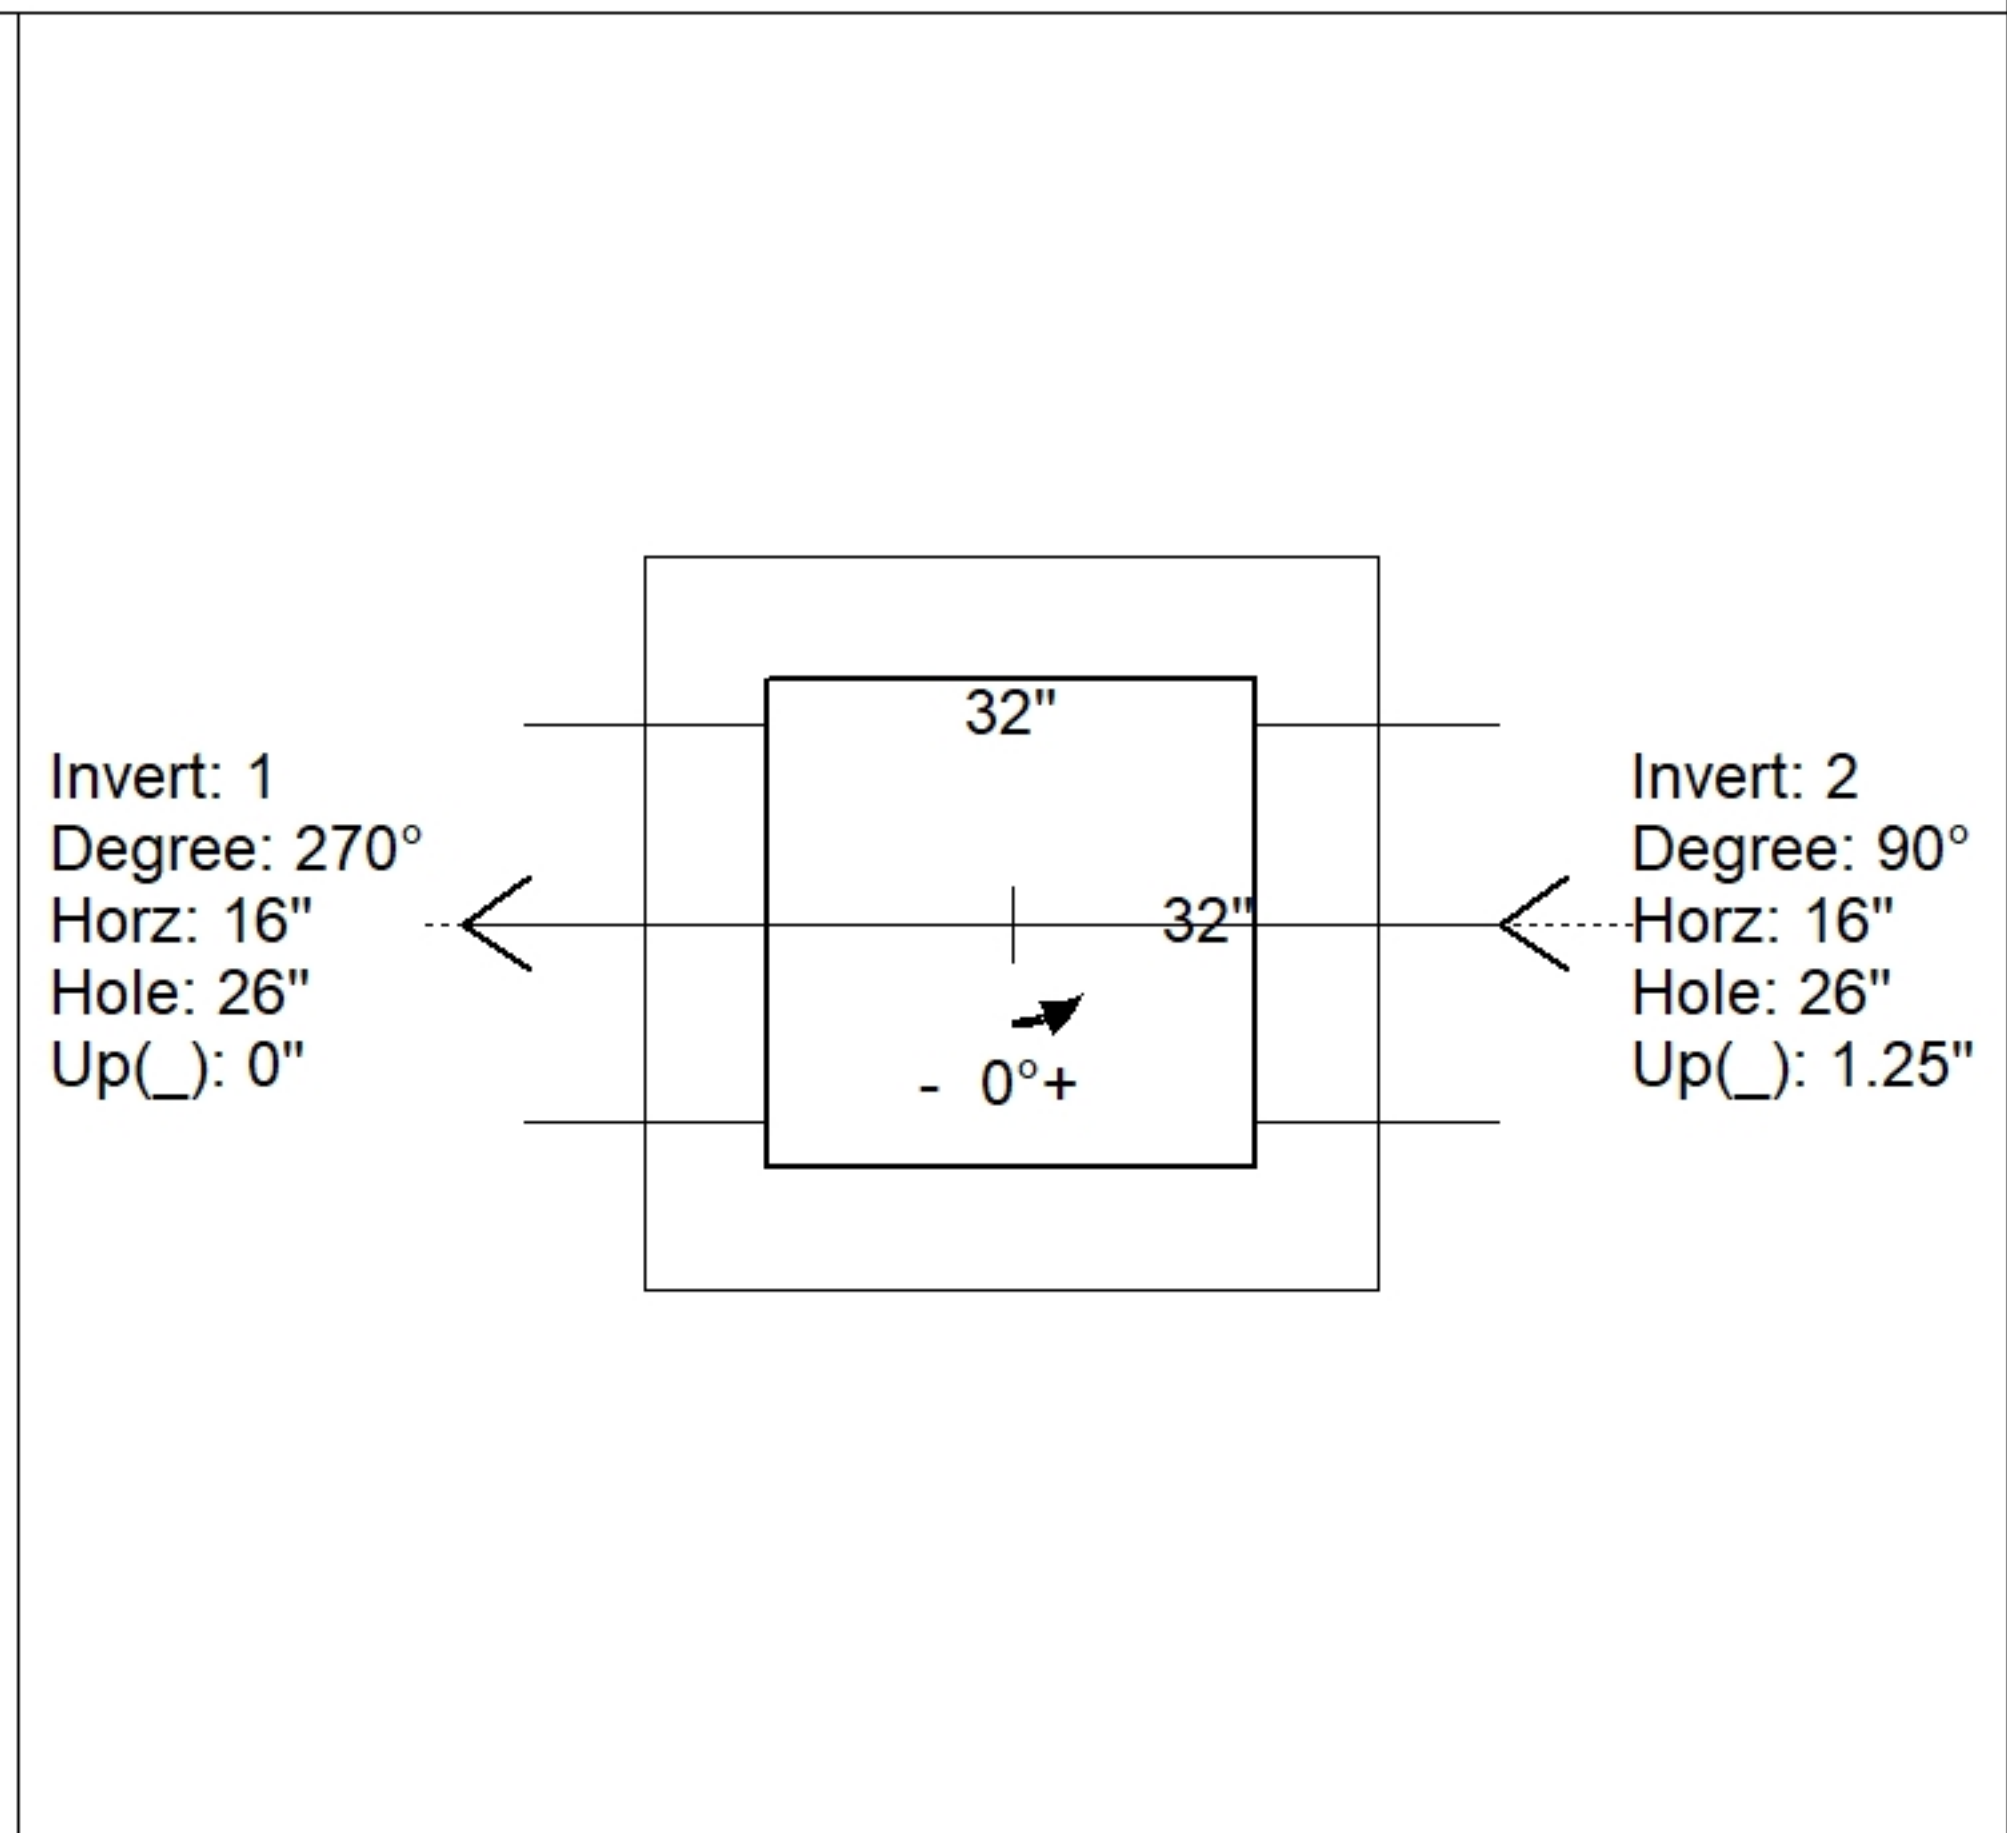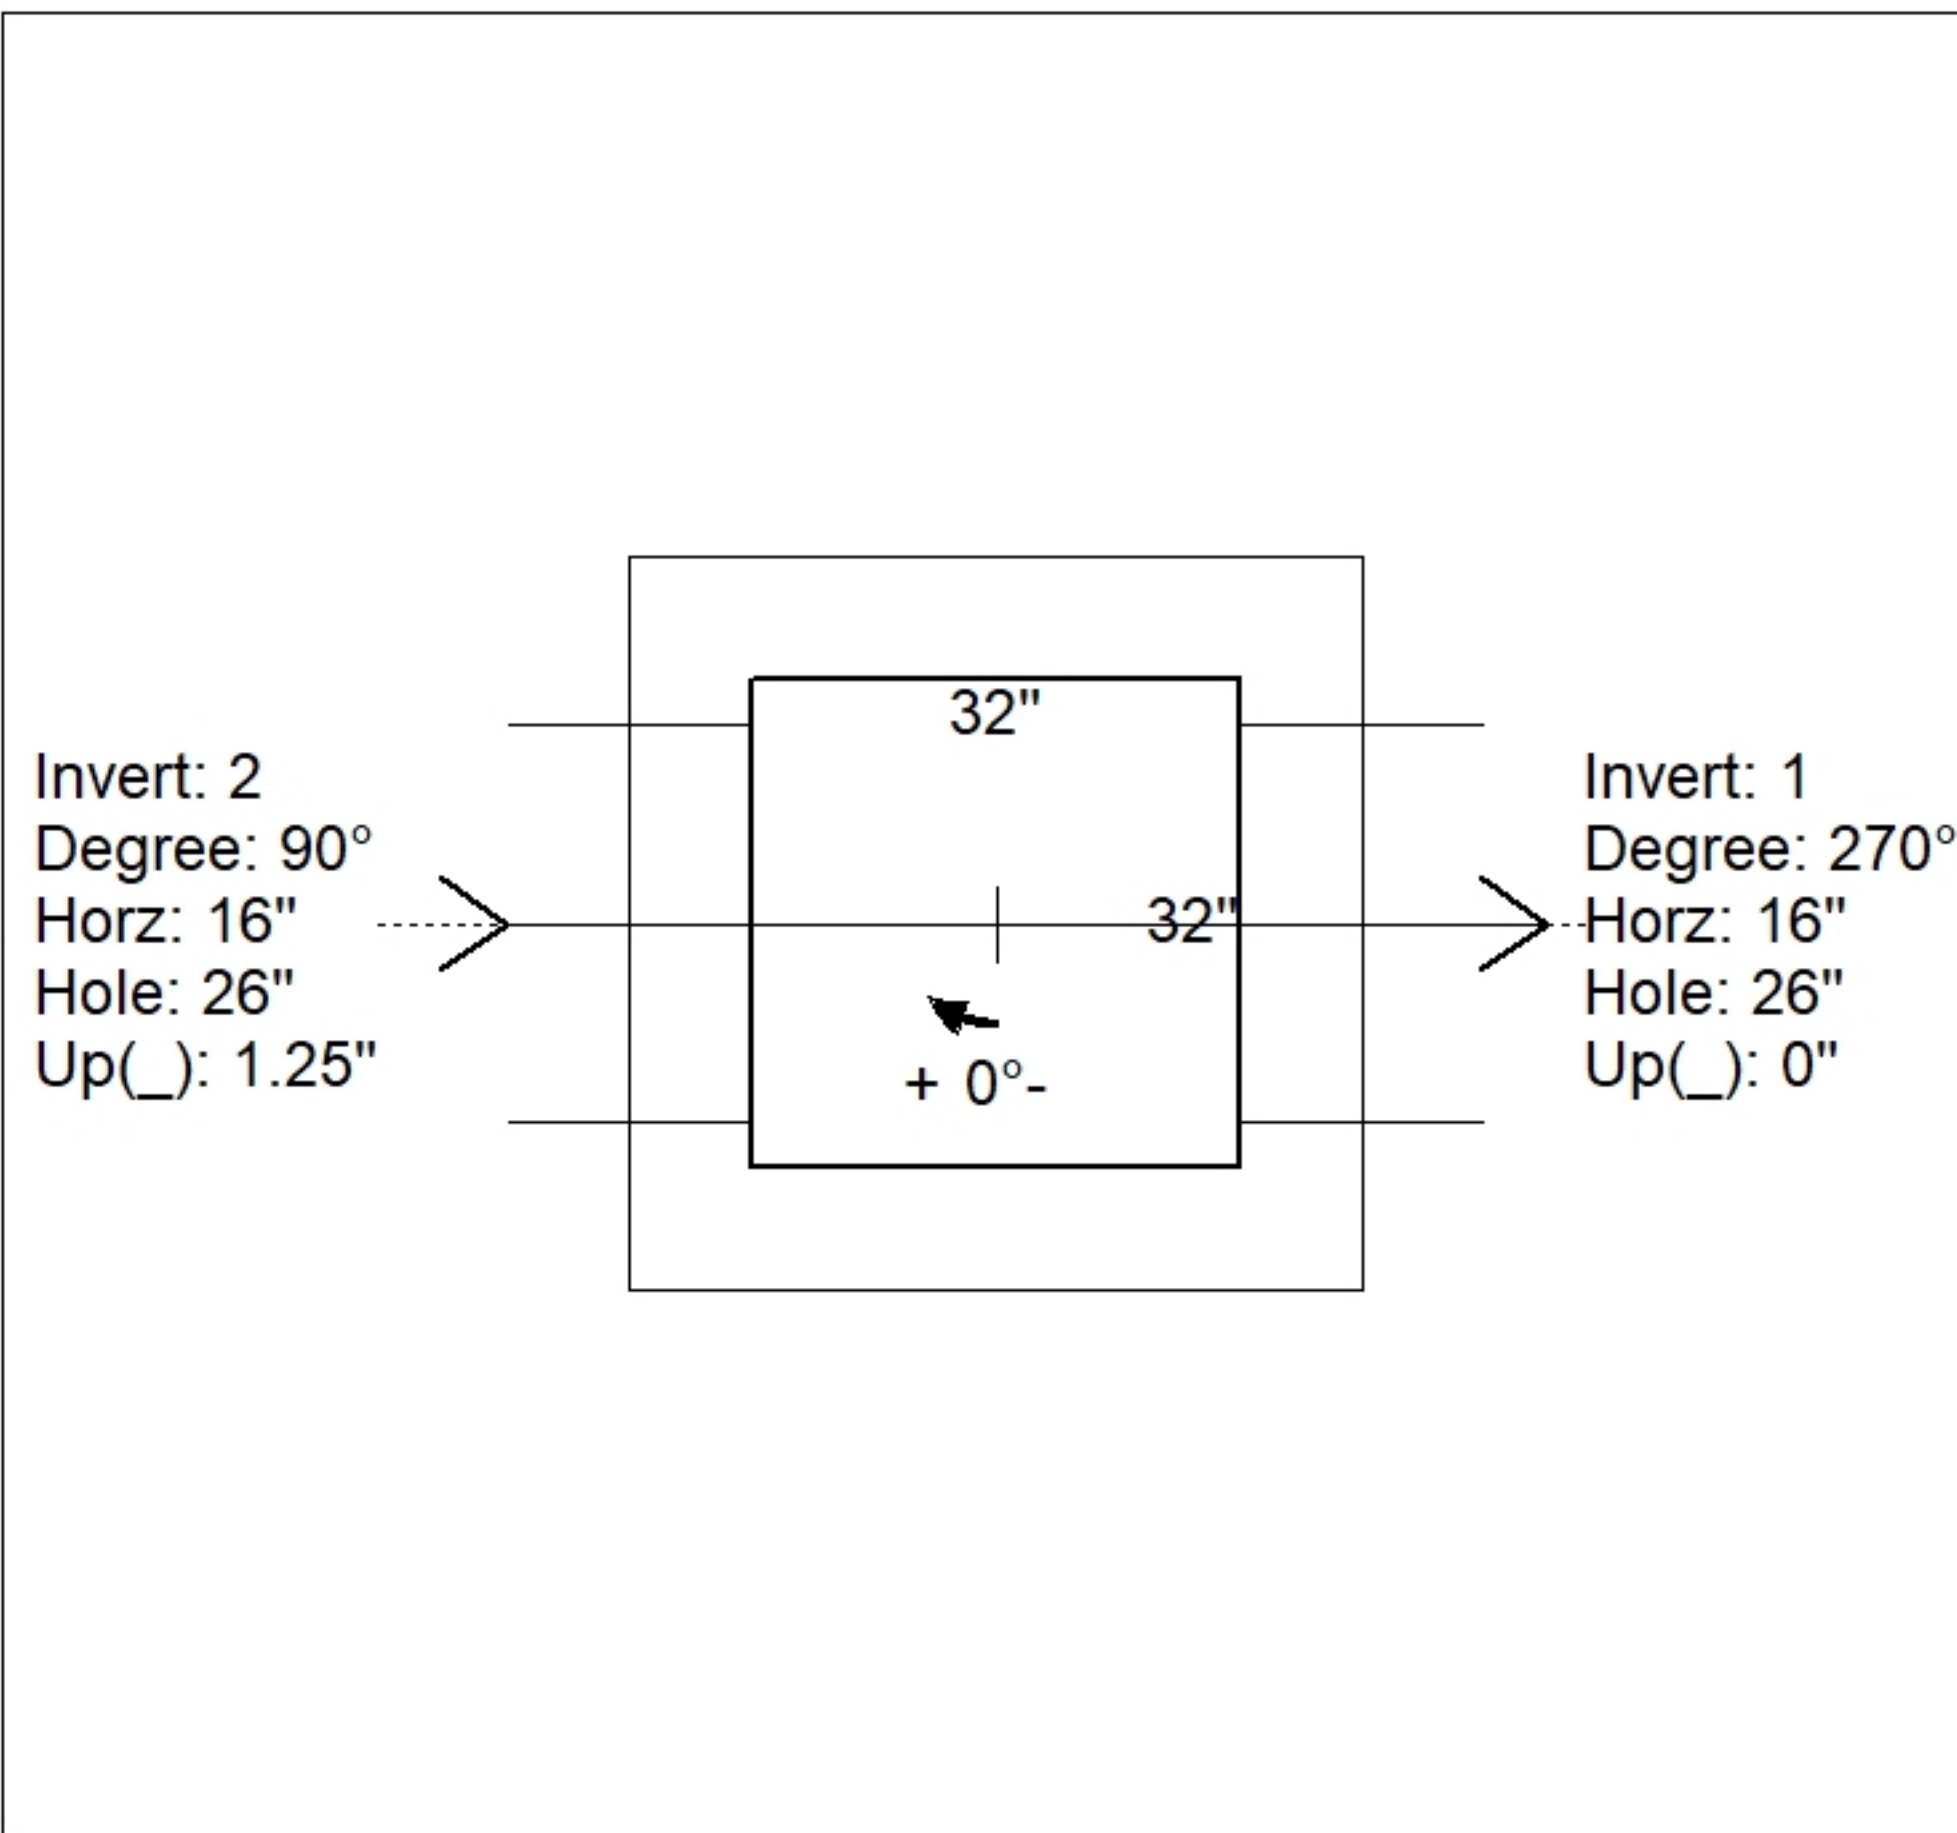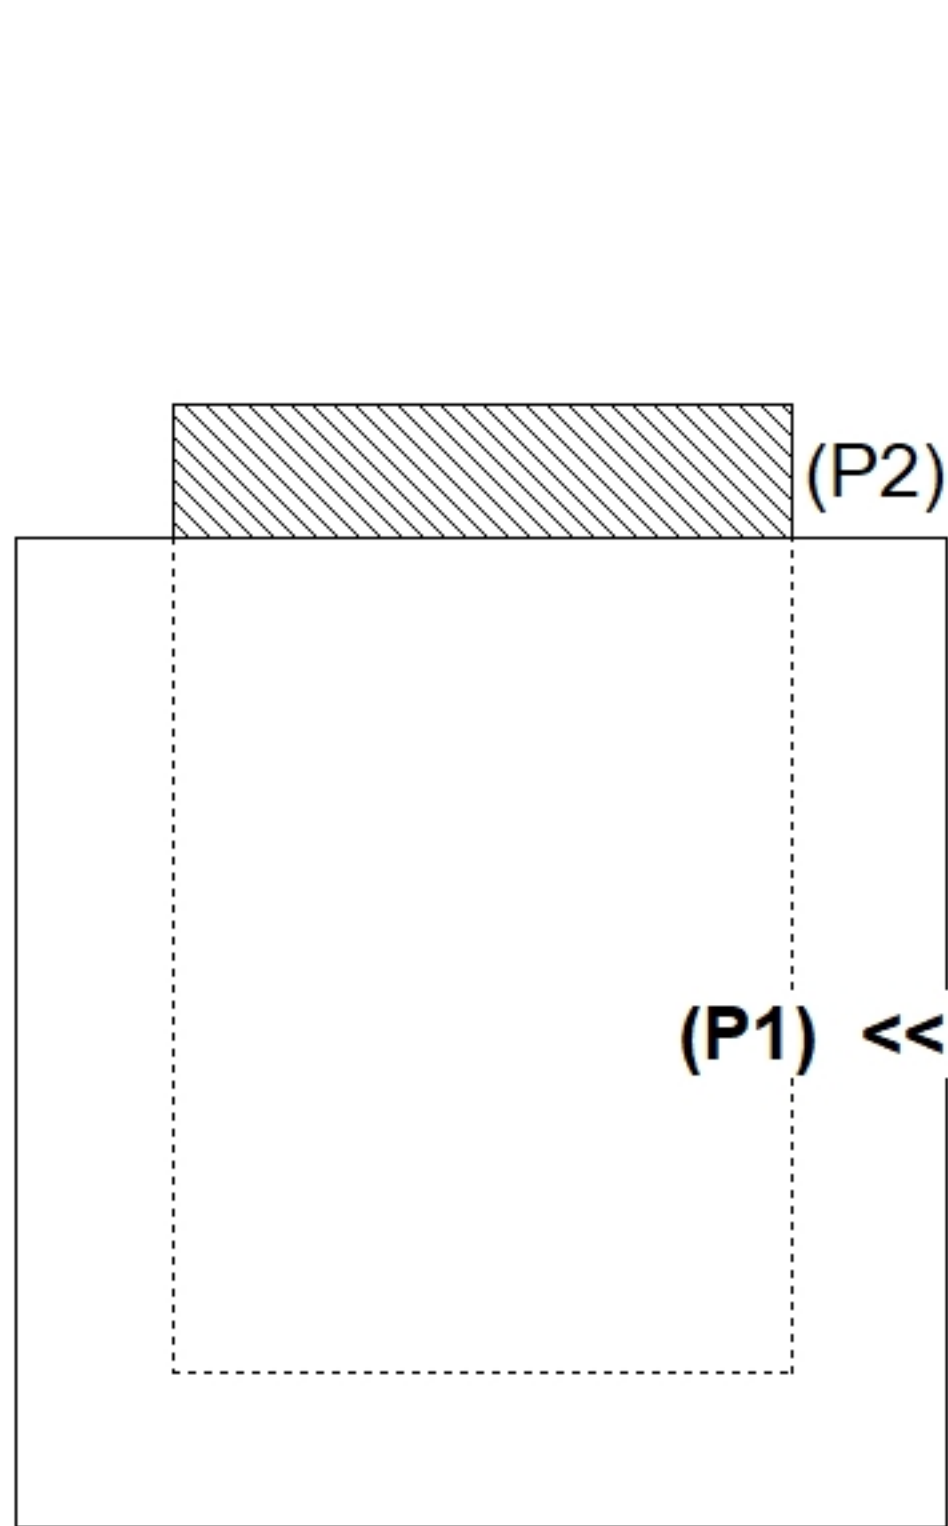

INSIDE WALL DIMENSIONS

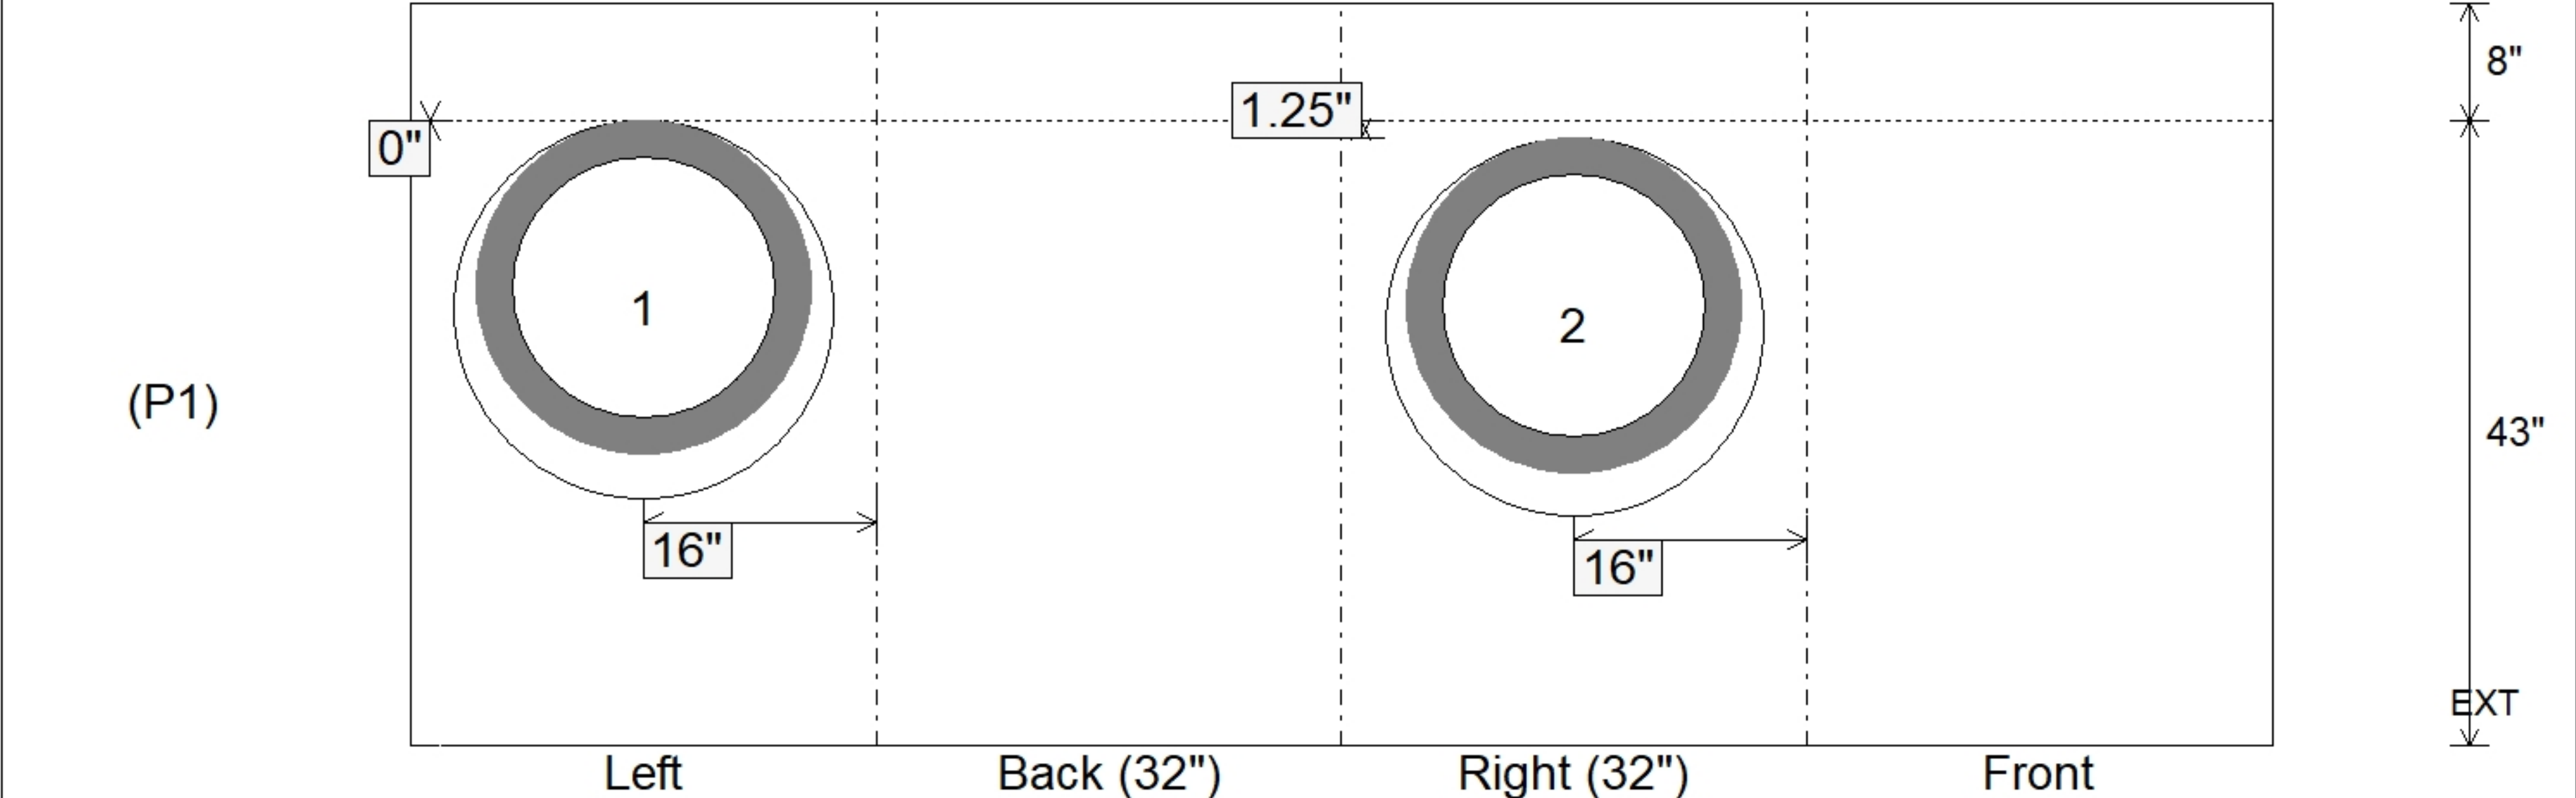

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 43" Height (Ext): 51"	Weight (Net): 5452 lb Volume (Net): 1.39cu.yd
----------------------------------	-------------------------------	--	--	--
