

Job Name: 25-2861 Spencer Co Bus Garage
 Job Location: Taylorsville, Ky
 Contractor: Louisville Paving and Construction

Plant: Beaver Dam

Tech: C.Russ

10/22/2025 10:49:48 AM

PC: J.Jarvis




Structure ID: DI-5B

P2 MH048LD07

MH FLAT TOP w/ 24" Center Hole F/F

P3) 24" - CASTING HEIGHT - 7"	0 lb
P2) 48" - MH FLAT TOP w/ 24" Center Hole F/F - 7"	1700 lb
P1) 48" - MH BASE Custom Ht F/n - 43"	4053 lb
1) CASTING - HOE 280T F/G	182 lb
1) 48" - SGL 1"x14.5' Butyl (2x)	0 lb
1) Hole - 20	0 lb
1) Hole - 6	0 lb
1) Hole - 16	0 lb
1) Hole - 12	0 lb
4) MH Step ML-10-TDS-NCR - 10"	0 lb
Structure Total:	5935 lb

Structure Notes:
 1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. MCB-315 B PROVIDED BY ICAST.
 4. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

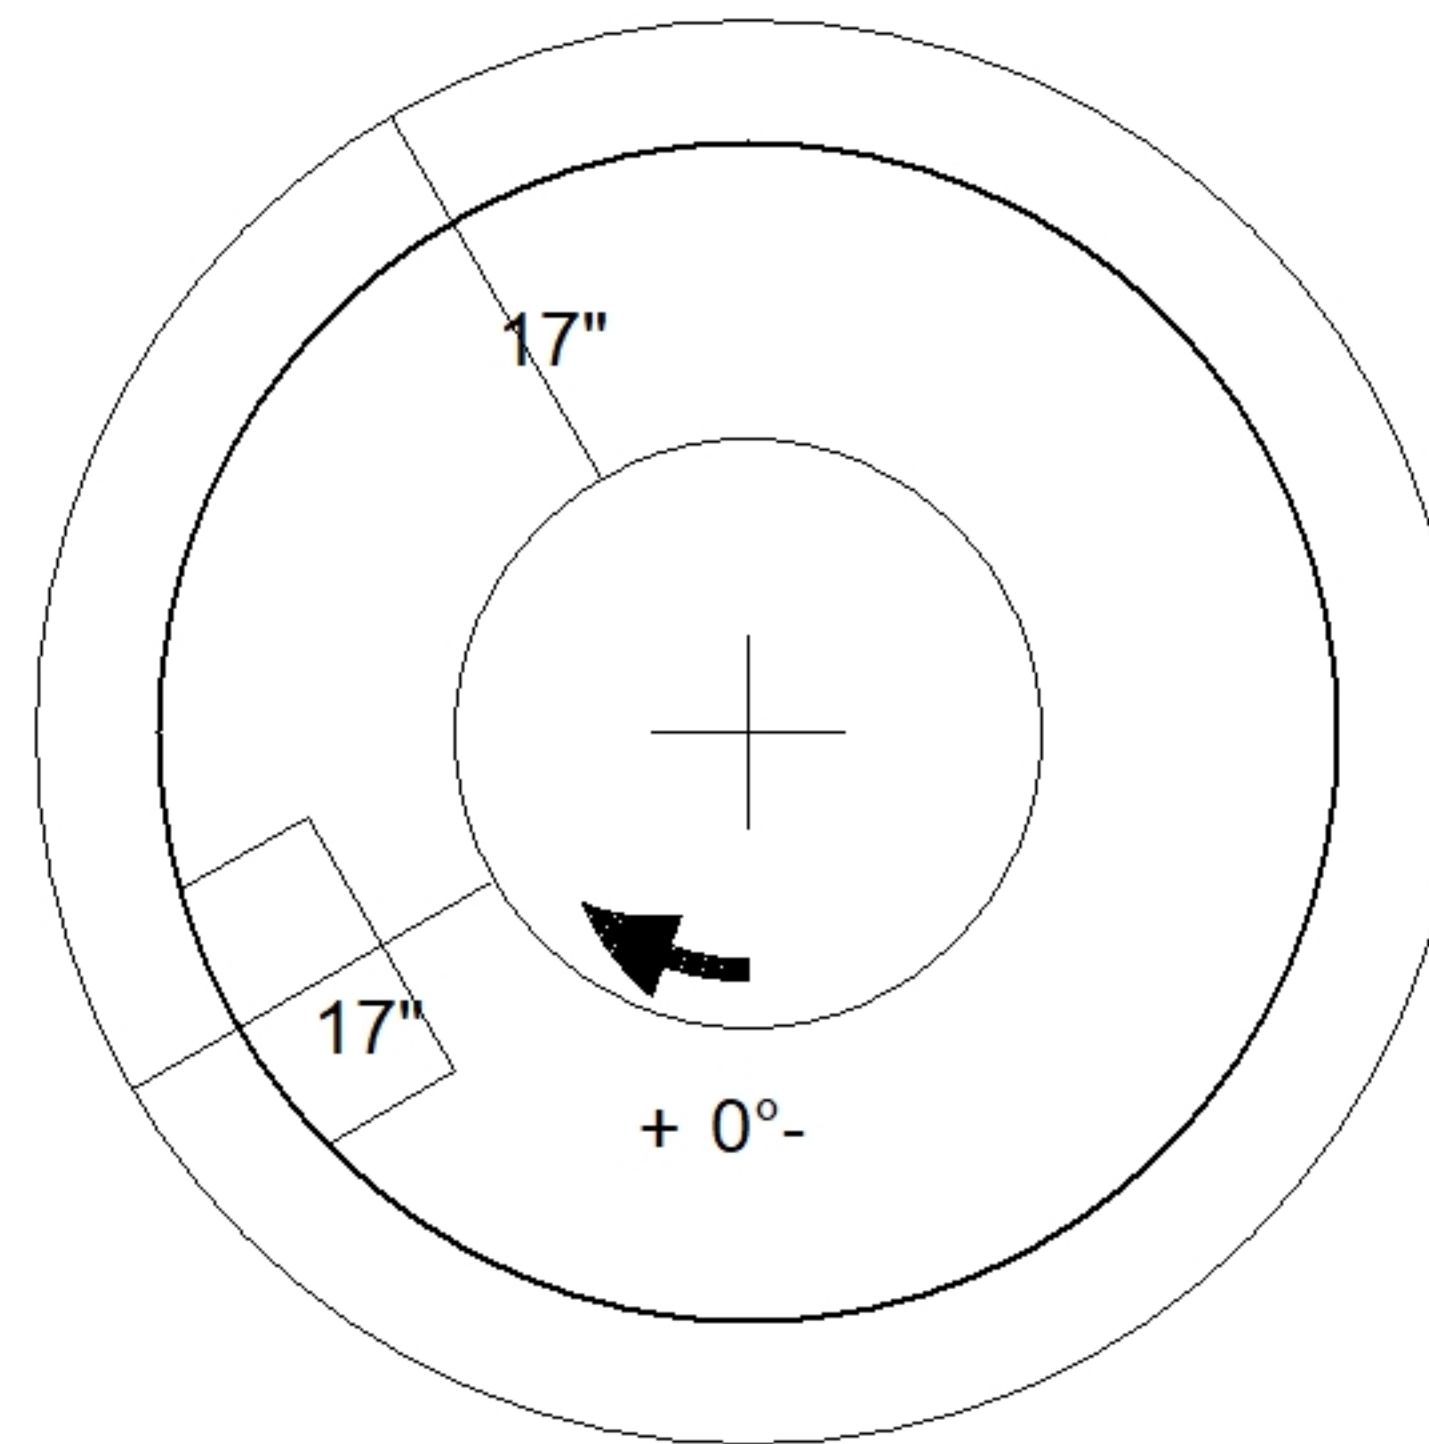

48" - MH FLAT TOP w/ 24" Center Hole F/F - 7" - (P2)

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 5"	Height (Ext): 7"	Weight (Net): 1700 lb Volume (Net): 0.42cu.yd
----------------------------------	--------------------------------	--------------------	------------------	--
