



Job Name: 25-2898 - Hunter's Ridge Ph.1 Job Location: Owensboro, KY Contractor: Ernie Davis & Sons Mechanical, Inc.					Plant: 100 5/29/2026 8:45:15 AM		Tech: Jared - A PC: A. Chambers														
Structure ID: AA-6 - AE-1																					
P2		MH048RSVF										MH RISER Custom Ht T/G									
P4) 24" x 36" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12" P2) 48" - MH RISER Custom Ht T/G - 46" P1) 48" - MH BASE T/n - 36" 2) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 26 1) Hole - 22 7) MH Step ML-10-TDS-NCR - 10"						0 lb 1300 lb 3049 lb 3379 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structures Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS AT 276 DEGREES 5. HOE-525 FRAME, GRATE, & CURB HOOD SUPPLIED BY OTHERS													
Structure Total:						7728 lb															
Rim: 455.47' Rim to Invert: 8.18' Slack: 0.66" Sump: 2.5" Step Position: 276°																					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset											
Invert 1																					
Invert 2	451.47'	90°	45.5"	15" RCP B WALL	19.5"	Hole 22	22"	22.854"	10.125"	0"											
Invert 3																					
Invert 4																					
Invert 5																					
Invert 6																					
Invert 7																					
Invert 8																					

RIGHT-SIDE UP VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

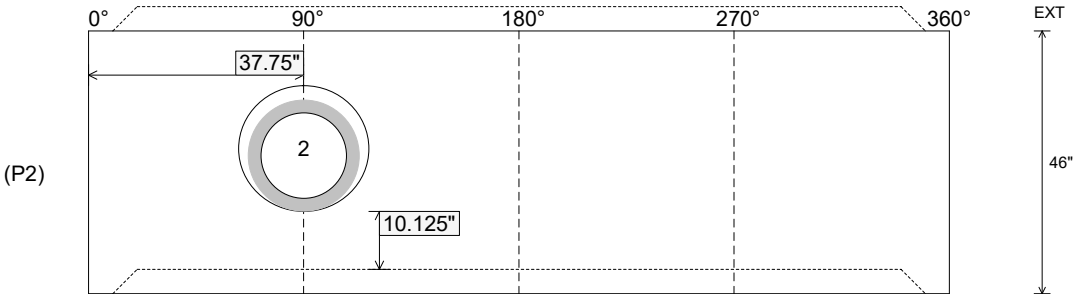

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 46" Height (Ext): 46"	Weight (Net): 3049 lb Volume (Net): 0.78cu.yd
----------------------------------	------------------------------------	--	--	--
