



Job Name: 25-2898 - Hunter's Ridge Ph.1 Job Location: Owensboro, KY Contractor: Ernie Davis & Sons Mechanical, Inc.					Plant: 100 5/29/2026 8:45:16 AM		Tech: Jared - A PC: A. Chambers				
Structure ID: BA-2 - BB-1											
P2 MH048RSVF			MH RISER Custom Ht T/G								
P4) 24" x 36" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12" P2) 48" - MH RISER Custom Ht T/G - 47" P1) 48" - MH BASE T/n - 42" 2) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 34 1) Hole - 22 7) MH Step ML-10-TDS-NCR - 10"					0 lb 1300 lb 3119 lb 3434 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 7853 lb		Structures Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS AT 82.5 DEGREES 5. HOE-525 FRAME, GRATE, & CURB HOOD SUPPLIED BY OTHERS				
Rim: 428.19' Rim to Invert: 8.74' Slack: 0.88" Sump: 3" Step Position: 82.5°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2	423.59'	165°	83.5"	15" RCP B WALL	19.5"	Hole 22	22"	22.854"	4.125"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

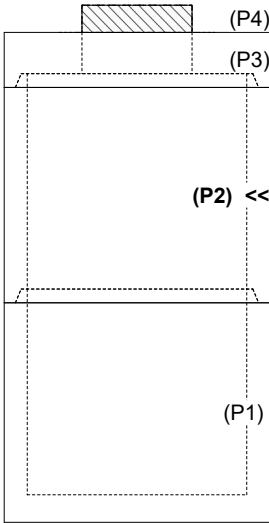

(P4)
(P3)
(P2) <<
(P1)

RIGHT-SIDE UP VIEW (int. dimensions)

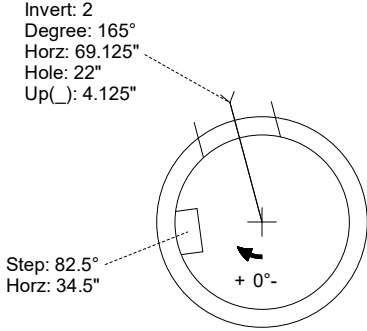


Invert: 2
Degree: 165°
Horz: 69.125"
Hole: 22"
Up(_): 4.125"

Step: 82.5°
Horz: 34.5"

+ 0°-

INSIDE WALL DIMENSIONS

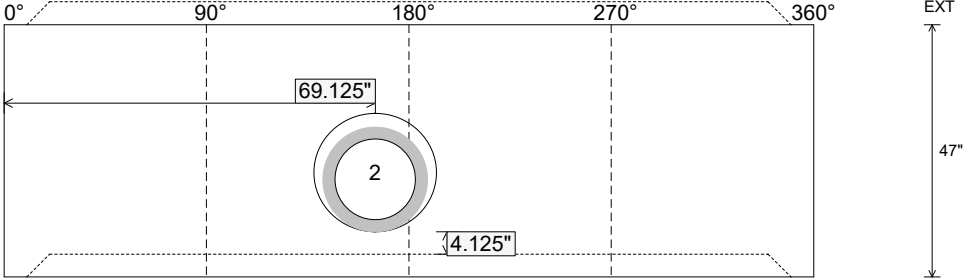

0° 90° 180° 270° 360°

69.125"

2

4.125"

EXT 47"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 47" Height (Ext): 47"	Weight (Net): 3119 lb Volume (Net): 0.8cu.yd
----------------------------------	------------------------------------	--	--	---
