

Job Name: 25-2943 Shelby Green Ph.2 Sec.3 Job Location: Junction City, KY Contractor: H&S,LLC	Plant: 100	Tech: J. Horsley - A	
	12/11/2025 1:20:06 PM	PC: Celina Goff	

**Structure ID: CI-C1**

**P1 BX2424-08BAVF**

**BOX BASE 8inW, 8inF, Variable Ht F/n**

- P2) 24" x 24" - CASTING HEIGHT - 5"
- P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 19"
- 1) CASTING - HOE KY-465 SET (CBI TY F)
- 1) 24" x 24" - Conseal CS-102 1.00"
- 1) DOGHOUSE INVRTD - 20"x20"

0 lb  
 2463 lb  
 465 lb  
 0 lb  
 0 lb  
 -----  
 Structure Total: 2928 lb




- Structure Notes:
1. PER ASTM C-913 SPECIFICATIONS
  2. CONCRETE: 4,000 PSI AT 28 DAYS
  3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
  4. HOE KY-465 FRAME, GRATE, & CURB HOOD SUPPLIED BY ICAST

Rim: 998.7'      Rim to Invert: 2'      Slack: 0"      Sump: 0"      Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ( )	Offset
Invert 1	996.7'	0°	20"	15" HDPE	17.6"	DOGHOUSE INVRTD 20"x20"	20" x 20"	20"	-1.3"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

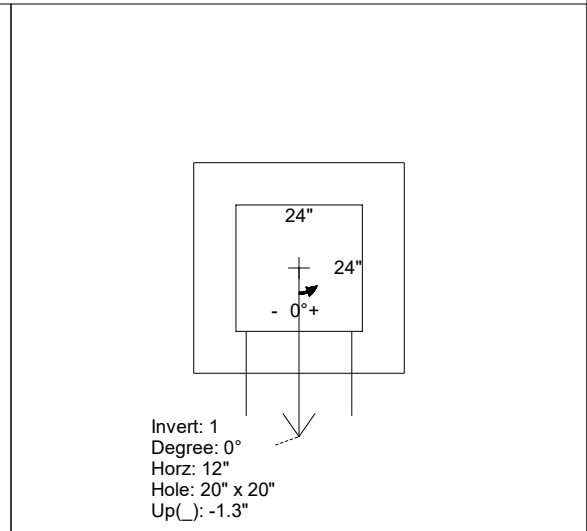

INSIDE WALL DIMENSIONS

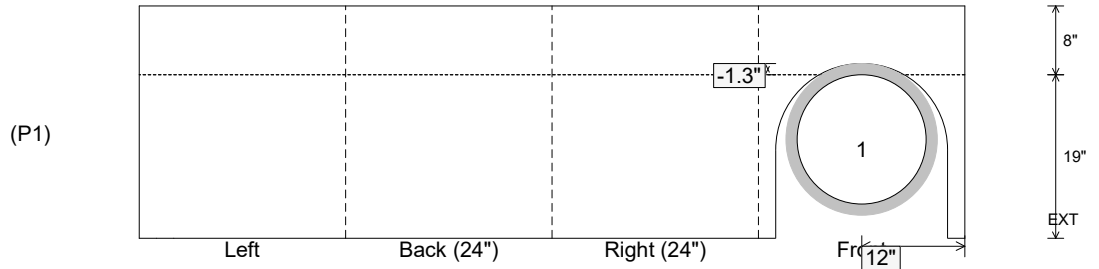

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 19" Height (Ext): 27"	Weight (Net): 2463 lb Volume (Net): 0.63cu.yd
----------------------------------	-------------------------------	--	--	--
