



Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction				Plant: 100 6/17/2026 5:01:17 PM		Tech: J. Horsley - A PC: J. Jarvis					
Structure ID: 12											
P1 BX18180606VF				BOX BASE 6inW, 6inF, Variable Ht F/n							
P2) 18" x 18" - CASTING HEIGHT - 4" P1) 18" x 18" - BOX BASE 6inW, 6inF, Variable Ht F/n - 23" 1) 18" x 18" - Conseal CS-102 1.00" 1) Hole - 18						0 lb 1469 lb 0 lb 0 lb ----- 1469 lb Structure Total:		Structure Notes: 1. PER MSD YARD DRAIN / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #4 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE 165-A FRAME & GRATE SUPPLIED BY OTHERS			
Rim: 562.6'				Rim to Invert: 2.25'		Slack: 0"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	560.35'	0°	15"	12" HDPE	14.5"	Hole 18	18"	18"	-3"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

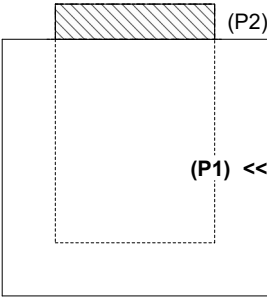


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

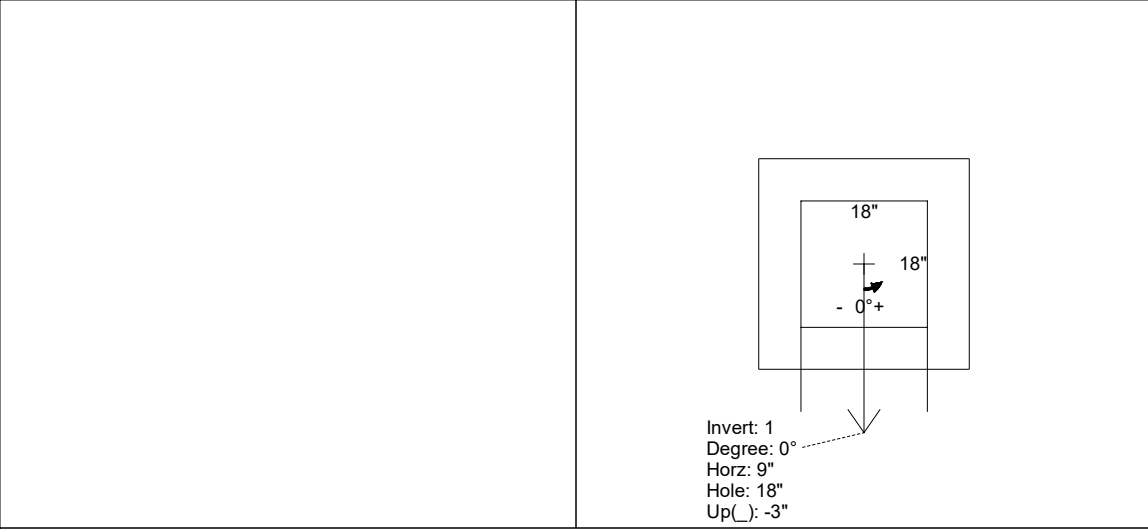

INSIDE WALL DIMENSIONS

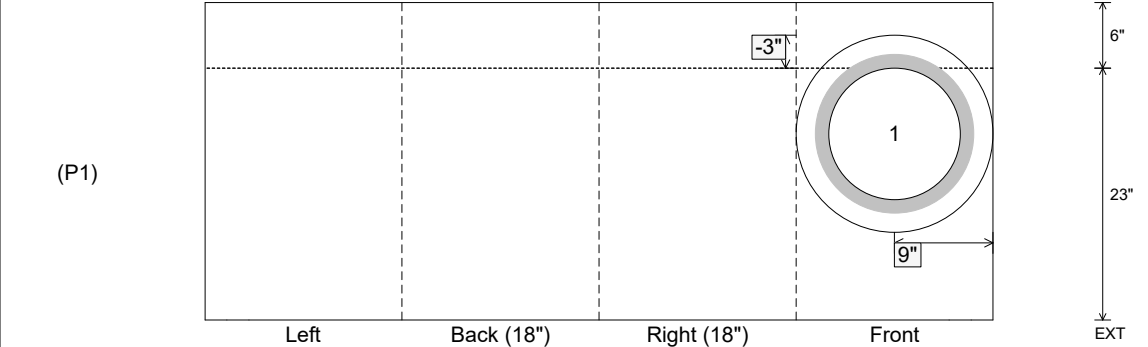

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 6" Floor Height: 6"	Height (Int): 23" Height (Ext): 29"	Weight (Net): 1469 lb Volume (Net): 0.38cu.yd
----------------------------------	-------------------------------	--	--	--
