

Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)  
Job Location: Indiana, KY  
Contractor: Louisville Paving and Construction

Plant: 100

6/22/2026 2:07:59 PM

Tech: J. Horsley - A

PC: J. Jarvis



## Structure ID: 128

### P1 BX3636-08BA60

### BOX BASE 8inW, 8inF

P2) 36" x 36" - CASTING HEIGHT - 3"  
P1) 36" x 36" - BOX BASE 8inW, 8inF - 60"  
1) 36" x 36" - Con Seal CS-102 1.00"  
3) Hole - 20

0 lb  
8271 lb  
0 lb  
0 lb  
-----  
8271 lb

Structure Total:

#### Structure Notes:

#### Structure Notes:



1. PER MSD CB TYPE 1 / ASTM C-913 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60)
4. HOE 595 FRAME & GRATES SUPPLIED BY OTHERS

Rim: 566.2' Rim to Invert: 5.3' Slack: 0.6" Sump: 0" Step Position:


| Position | Elev   | Angle | Ext. (cw) | Pipe     | Pipe OD | Connector | Hole | Horz Size | Up ( ) | Offset |
|----------|--------|-------|-----------|----------|---------|-----------|------|-----------|--------|--------|
| Invert 1 | 560.9' | 90°   | 26"       | 15" HDPE | 17.6"   | Hole 20   | 20"  | 20"       | -2.5"  | 0"     |
| Invert 2 | 560.9' | 180°  | 26"       | 15" HDPE | 17.6"   | Hole 20   | 20"  | 20"       | -2.5"  | 0"     |
| Invert 3 | 560.9' | 270°  | 26"       | 15" HDPE | 17.6"   | Hole 20   | 20"  | 20"       | -2.5"  | 0"     |
| Invert 4 |        |       |           |          |         |           |      |           |        |        |
| Invert 5 |        |       |           |          |         |           |      |           |        |        |
| Invert 6 |        |       |           |          |         |           |      |           |        |        |
| Invert 7 |        |       |           |          |         |           |      |           |        |        |
| Invert 8 |        |       |           |          |         |           |      |           |        |        |

#### RIGHT-SIDE UP VIEW (int. dimensions)

#### UPSIDE-DOWN VIEW (int. dimensions)

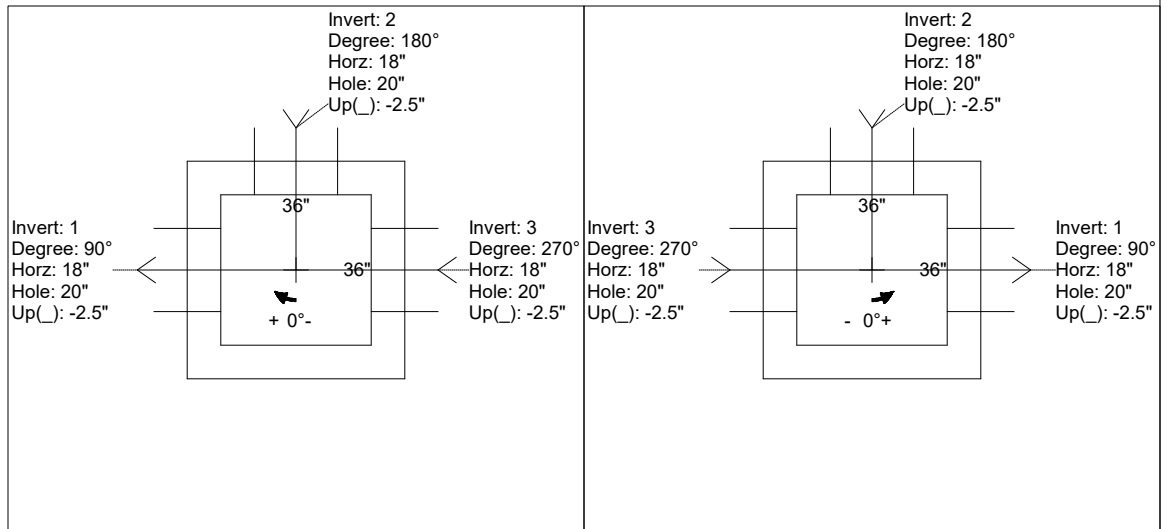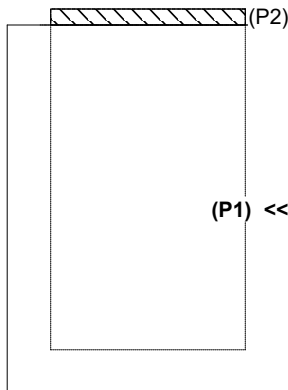

#### INSIDE WALL DIMENSIONS

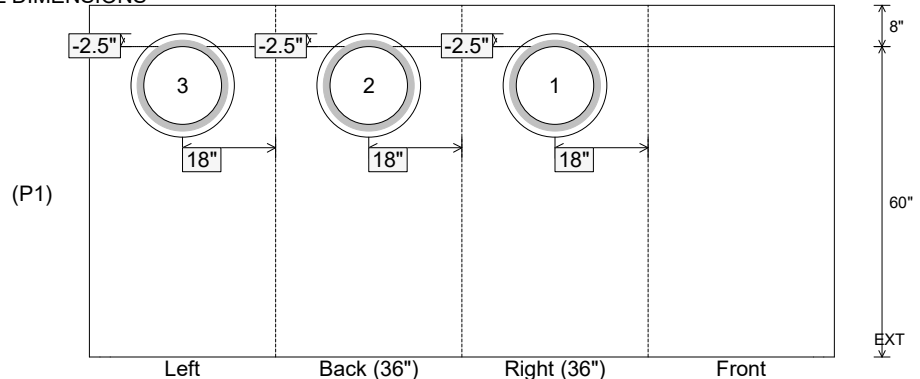

Coating (Int):  
Coating (Ext):

Seam Up: Flat  
Seam Dn: n/a

Wall Thickness: 8"  
Floor Height: 8"

Height (Int): 60"  
Height (Ext): 68"

Weight (Net): 8271 lb  
Volume (Net): 2.11cu.yd
