

**Contractor: Louisville Paving and Construction**

TECH: J. Horsley - A

Plant: 100




Slack: 0.6"

1. PER MSD CB TYPE 1 / ASTM C-913 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60)
4. HOE 595 FRAME & GRATES SUPPLIED BY OTHERS

P2) 36" x 36" - CASTING HEIGHT - 3"  
P1) 36" x 36" - BOX BASE 8inW, 8inF - 60"  
1) 36" x 36" - Conseal CS-102 1.00"  
3) Hole - 20


0 lb  
8271 lb  
0 lb  
0 lb

Structure Total: 8271 lb

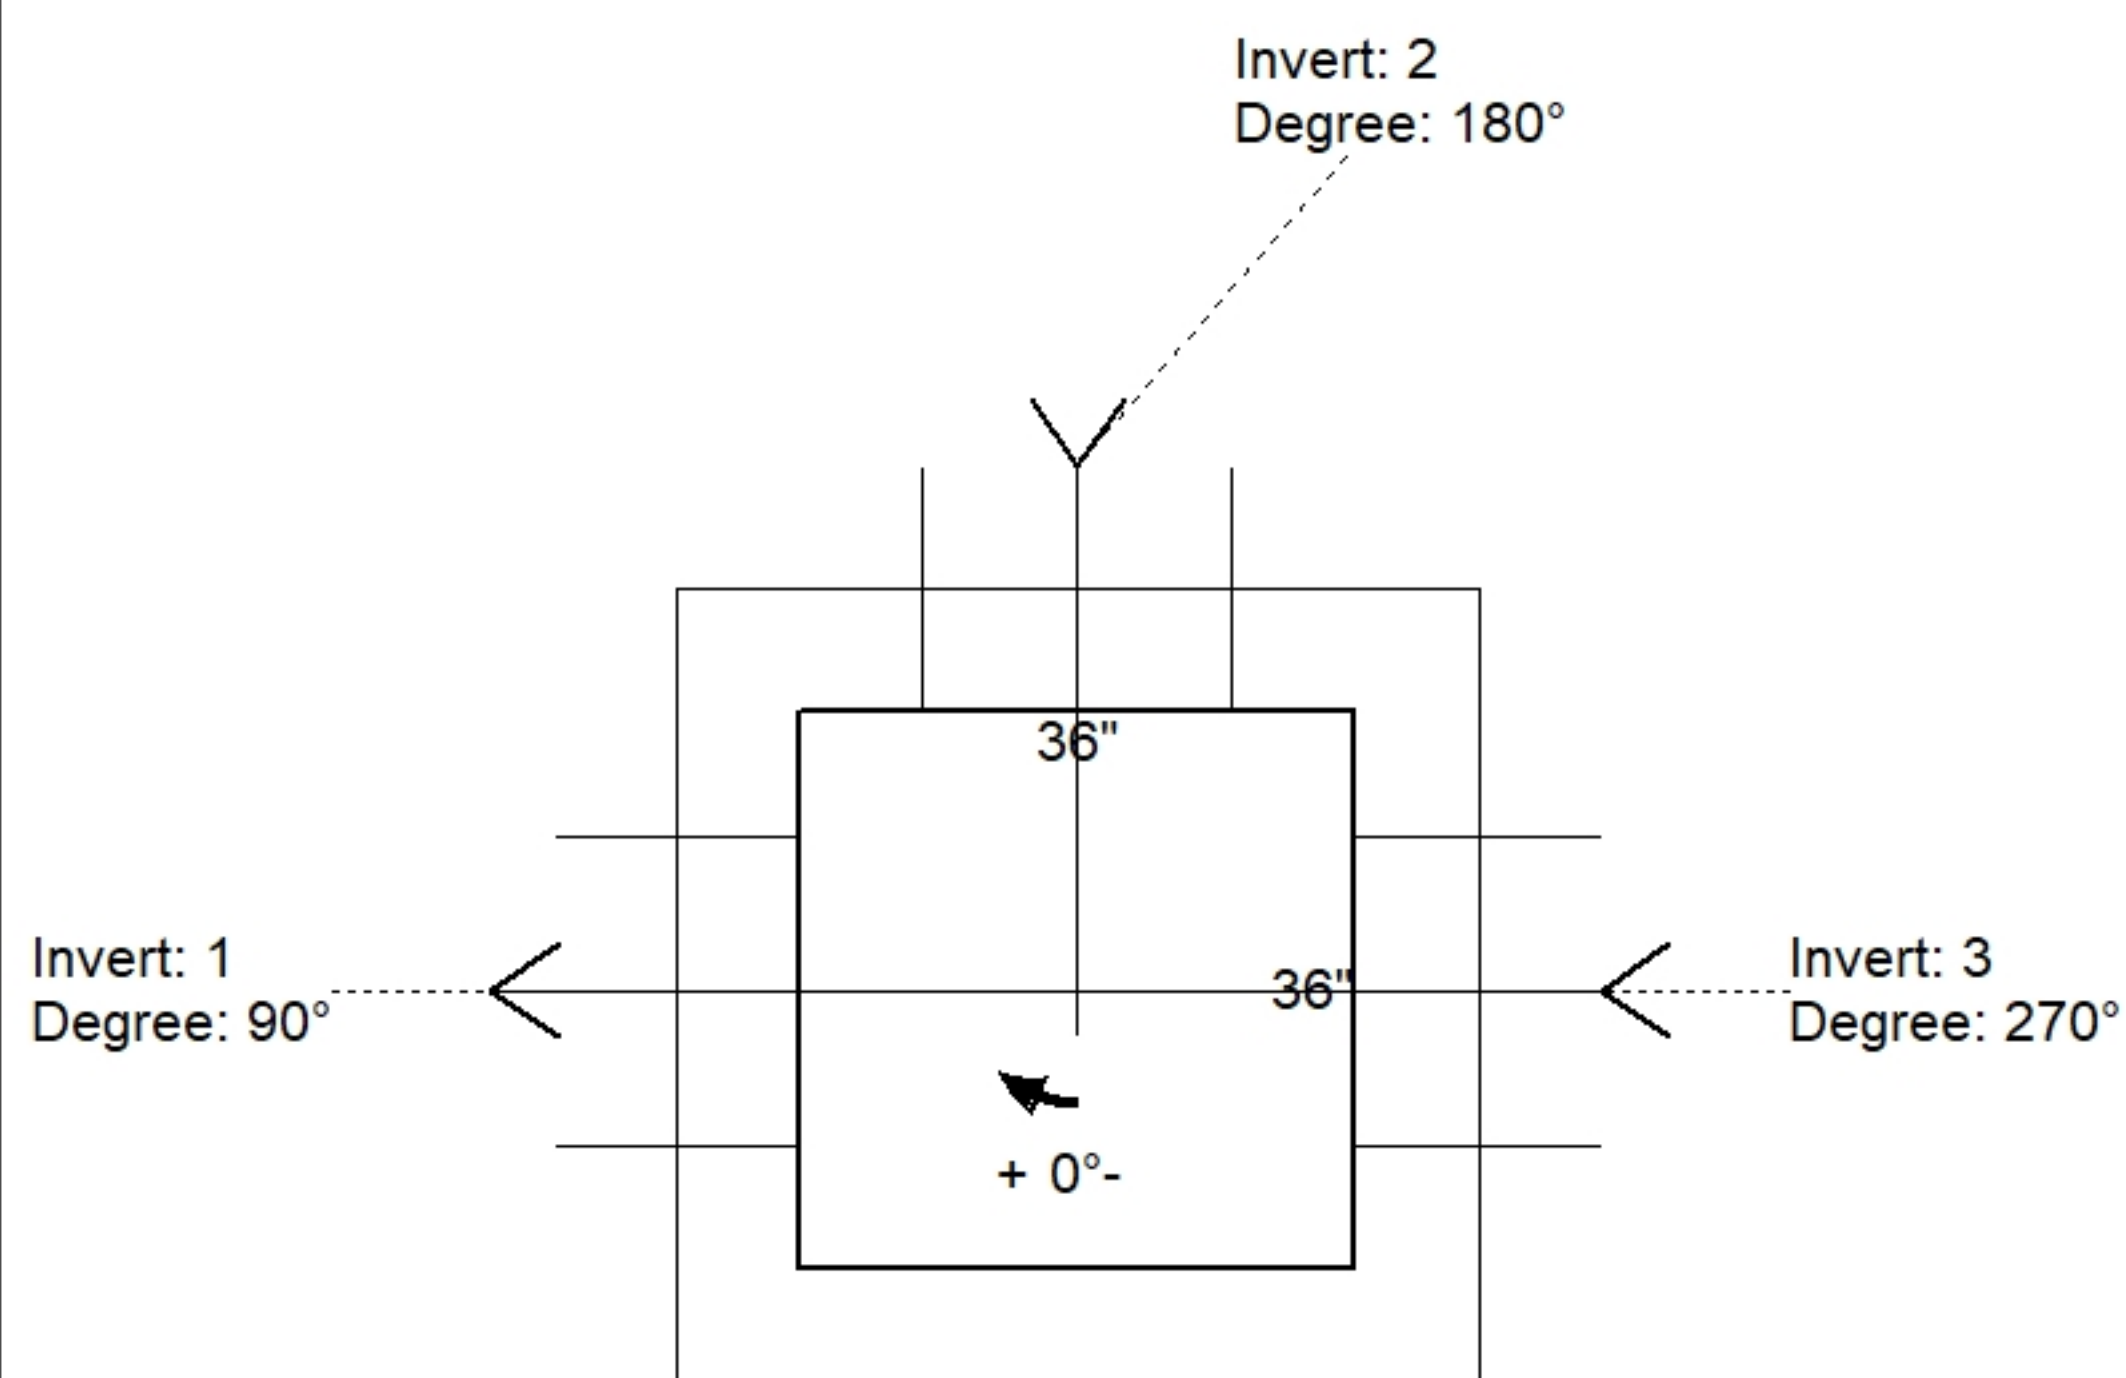

| Position | Elev   | Angle | Pipe     | Pipe OD | Hole | Connector | Up (↓) | Ref |
|----------|--------|-------|----------|---------|------|-----------|--------|-----|
| Rim      | 566.2' |       |          |         |      |           |        |     |
| Reducer  |        |       |          |         |      |           |        |     |
| Invert 1 | 560.9' | 90°   | 15" HDPE | 17.6"   | 20"  | Hole 20   | -2.5"  | P1  |
| Invert 2 | 560.9' | 180°  | 15" HDPE | 17.6"   | 20"  | Hole 20   | -2.5"  | P1  |
| Invert 3 | 560.9' | 270°  | 15" HDPE | 17.6"   | 20"  | Hole 20   | -2.5"  | P1  |
| Invert 4 |        |       |          |         |      |           |        |     |
| Invert 5 |        |       |          |         |      |           |        |     |
| Invert 6 |        |       |          |         |      |           |        |     |
| Invert 7 |        |       |          |         |      |           |        |     |
| Invert 8 |        |       |          |         |      |           |        |     |

### Default - Interior Dimensions

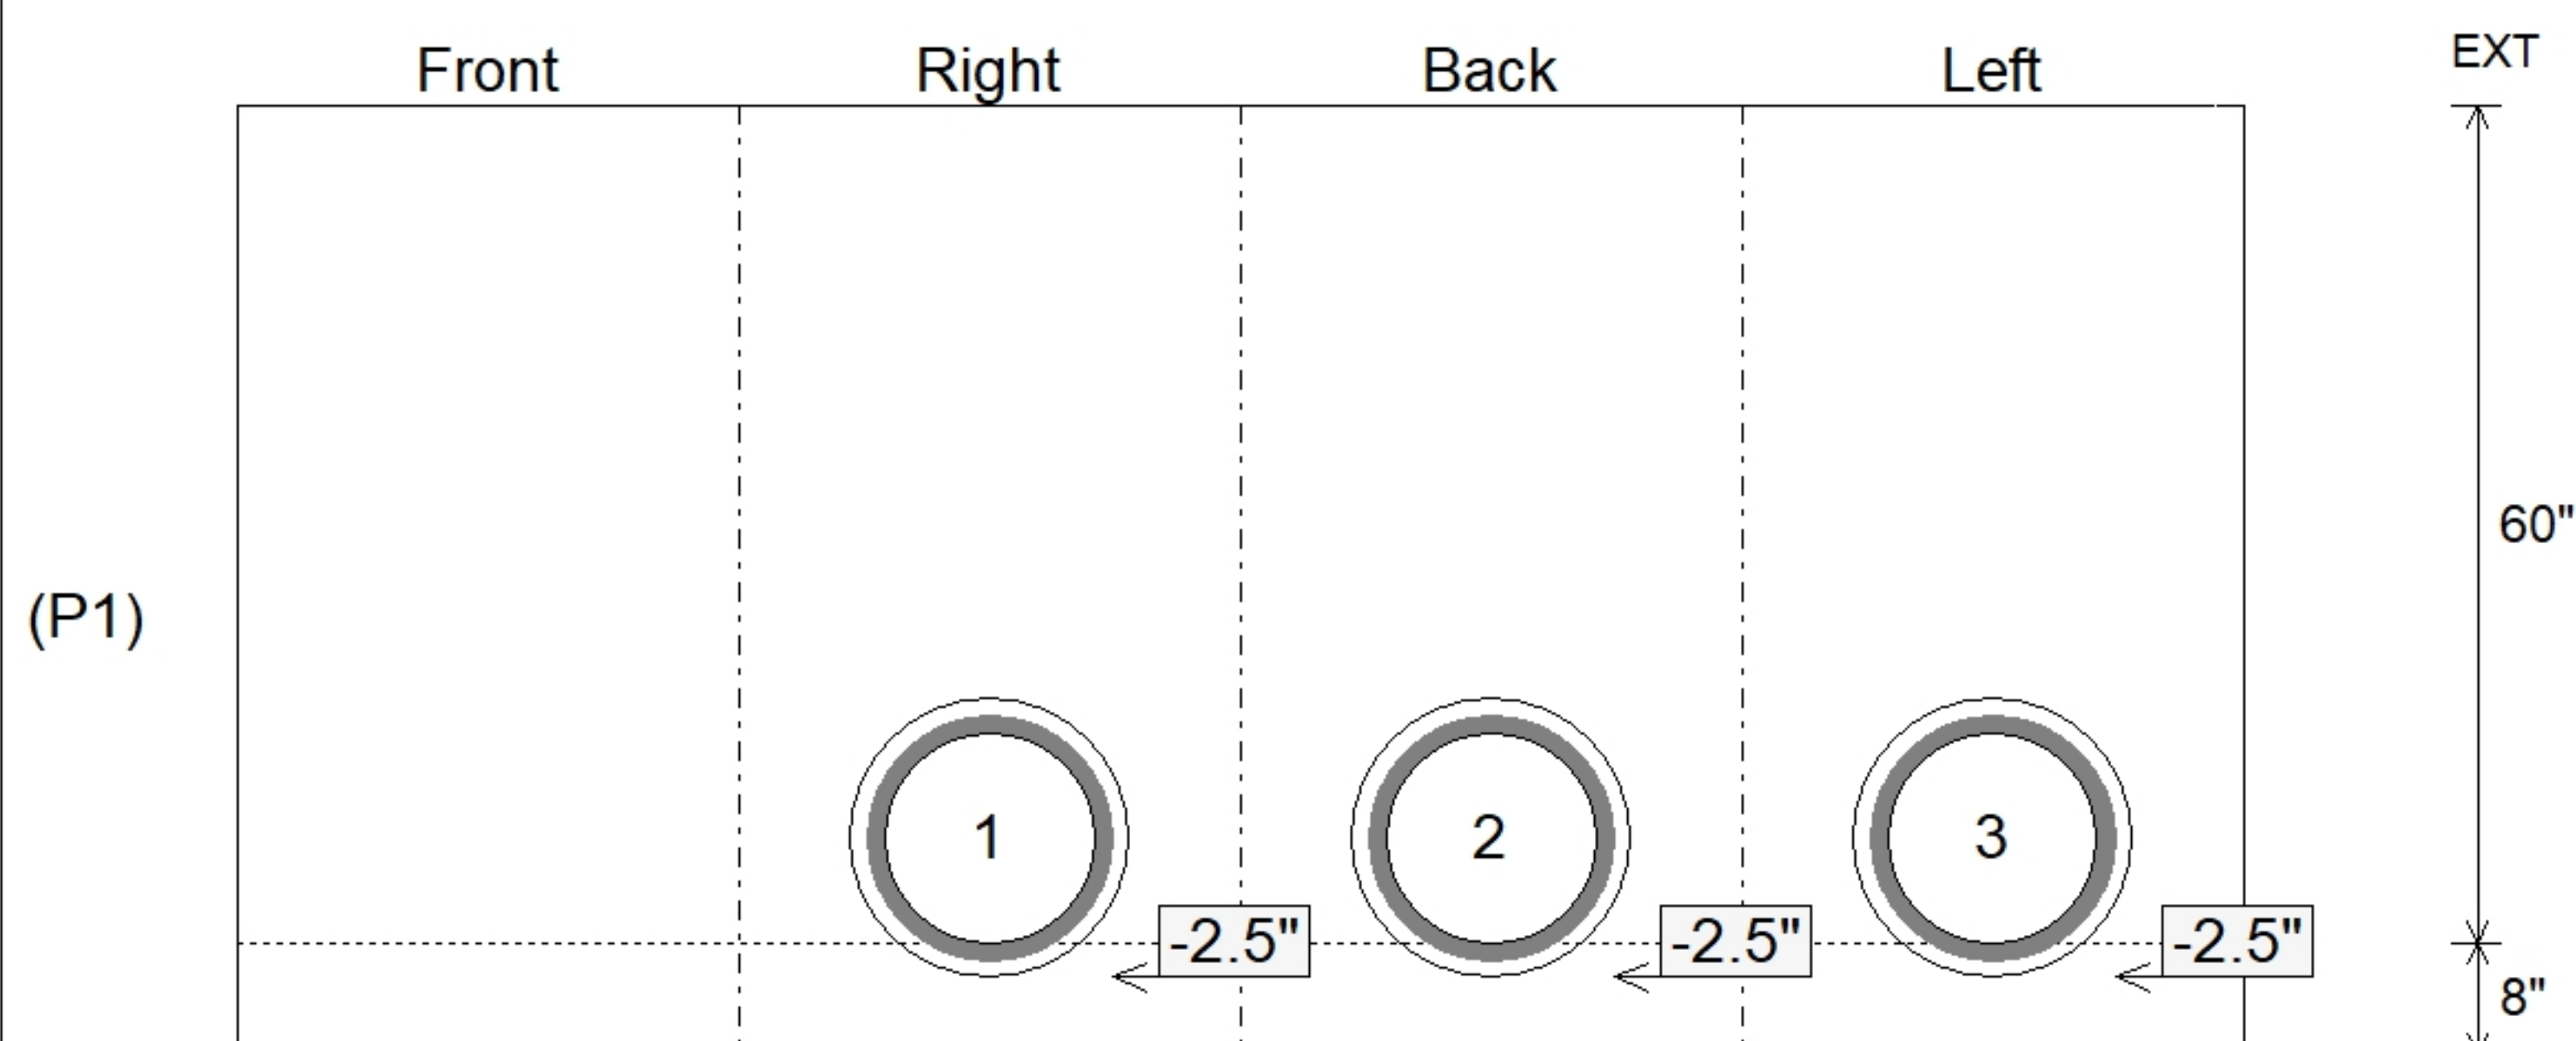

Submittal Drawing  
6/22/2026 2:17:39 PM

SUBMITTAL  
APPROVED BY:
