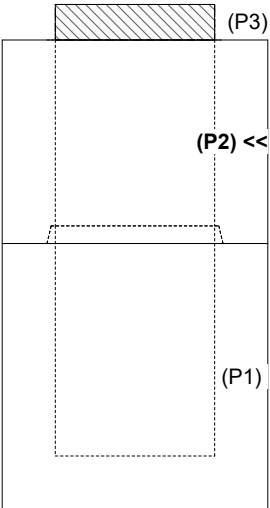

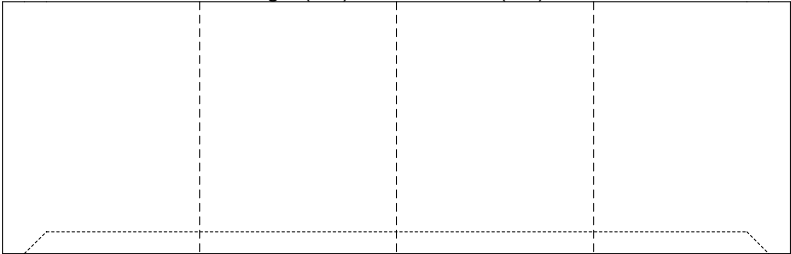


Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction					Plant: 100 6/17/2026 5:41:14 PM		Tech: J. Horsley - A PC: J. Jarvis				
Structure ID: 133											
P2		BX1818-06RVF		BOX RISER 6inW, Variable Ht F/G							
P3) 18" x 18" - CASTING HEIGHT - 4" P2) 18" x 18" - BOX RISER 6inW, Variable Ht F/G - 23" P1) 18" x 18" - BOX BASE 6inW, 6inF T/n - 24" 2) 18" x 18" - Conseal CS-102 1.00" 2) Hole - 18						0 lb 1112 lb 1421 lb 0 lb 0 lb ----- Structure Total: 2533 lb		Structure Notes: 1. PER MSD YARD DRAIN / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #4 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE 165-A FRAME & GRATE SUPPLIED BY OTHERS			
Rim: 566.5'		Rim to Invert: 4.25'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
(P2)		FrontRight (18")Back (18")Left				EXT 23"					
											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: Groove		Wall Thickness: 6" Floor Height: 0"		Height (Int): 23" Height (Ext): 23"		Weight (Net): 1112 lb Volume (Net): 0.28cu.yd	
