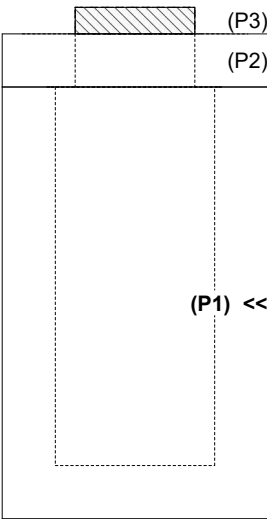
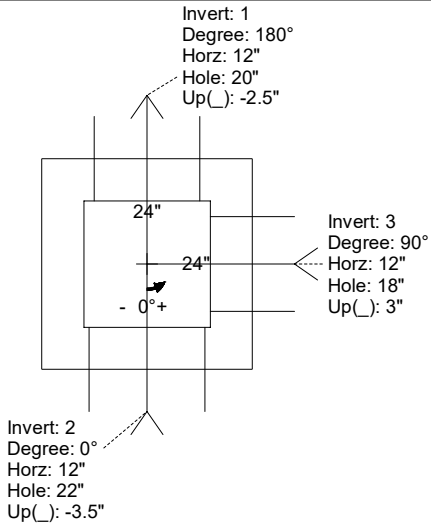
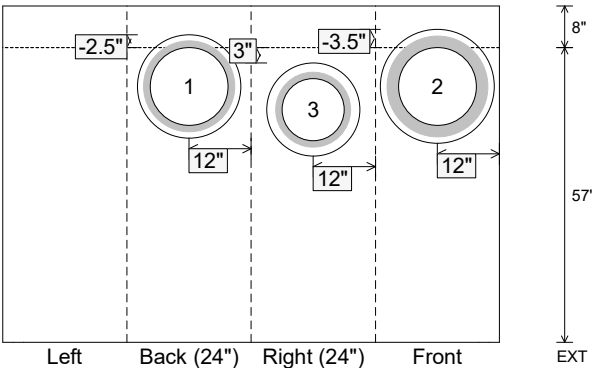


Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction					Plant: 100 6/17/2026 5:40:53 PM		Tech: J. Horsley - A PC: J. Jarvis				
Structure ID: 134											
P1 BX2424-08BAVF BOX BASE 8inW, 8inF, Variable Ht F/n											
P3) 18" x 18" - CASTING HEIGHT - 4" P2) 24" x 24" - CB FLAT TOP 8"W w/18"x18" HOLE F/F - 8" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 57" 1) 24" x 24" - Conseal CS-102 1.00" 1) 18" x 18" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 22 1) Hole - 18						0 lb 857 lb 5335 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 6192 lb		Structure Notes: 1. PER MSD YARD DRAIN / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #4 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE 165-A FRAME & GRATE SUPPLIED BY OTHERS			
Rim: 566.5' Rim to Invert: 5.75' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	560.75'	180°	20"	15" HDPE	17.6"	Hole 20	20"	20"	-2.5"	0"	
Invert 2	560.75'	0°	20"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-3.5"	0"	
Invert 3	561.25'	90°	20"	12" HDPE	14.5"	Hole 18	18"	18"	3"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 57" Height (Ext): 65"		Weight (Net): 5335 lb Volume (Net): 1.36cu.yd	
