

Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)
Job Location: Indiana, KY
Contractor: Louisville Paving and Construction

Plant: 100

6/12/2026 3:12:21 PM

Tech: J. Horsley - A

PC: J. Jarvis



Structure ID: 14

P2 BX036036-08LD08S

CB FLAT TOP 8"W SPEC. (KY-328 CAST IN) F/F

- P3) 36" x 36" - CASTING (cast in) - 3"
P2) 36" x 36" - CB FLAT TOP 8"W SPEC. (KY-328 CAST IN) F/F - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 40"
1) This Structure Includes a Cast-in Item - HOE KY-328 Frame (Supplied by Others)
2) 36" x 36" - Conseal CS-102 1.00"
2) Hole - 32

Structure Total:




0 lb
996 lb
5461 lb
0 lb
0 lb
0 lb

6457 lb

Structure Notes:

**** KYTC STATE PROJECT ****

1. PER KYTC DBI TYPE 3 / ASTM C-913 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. HOE KY-328 FRAME & GRATES SUPPLIED BY OTHERS - FRAME TO BE CAST INTO FLAT LID
5. LIFTERS: 2 EA. CONAC A-W ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED AS SHOWN
- IF NEEDED, MODIFY A-W RRF CUP TO PREVENT INTERFERENCE WITH CAST-IN FRAME
6. TOP SURFACE TO RECEIVE LIGHT BRUSH FINISH

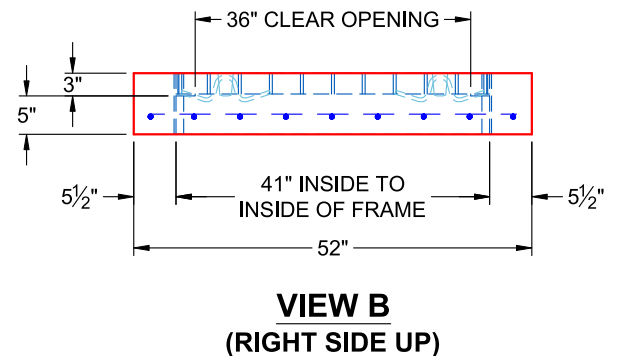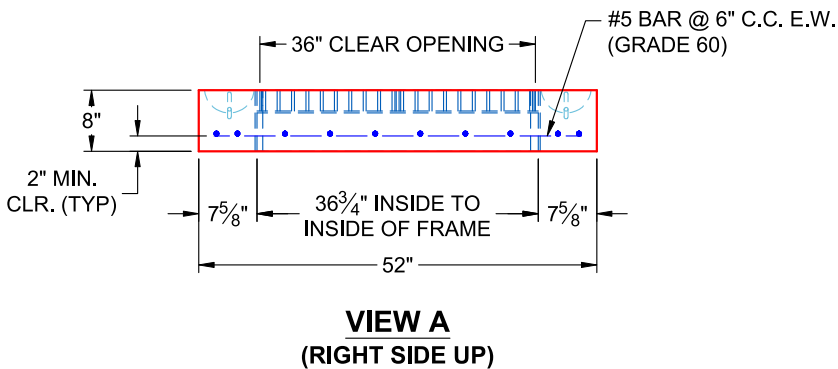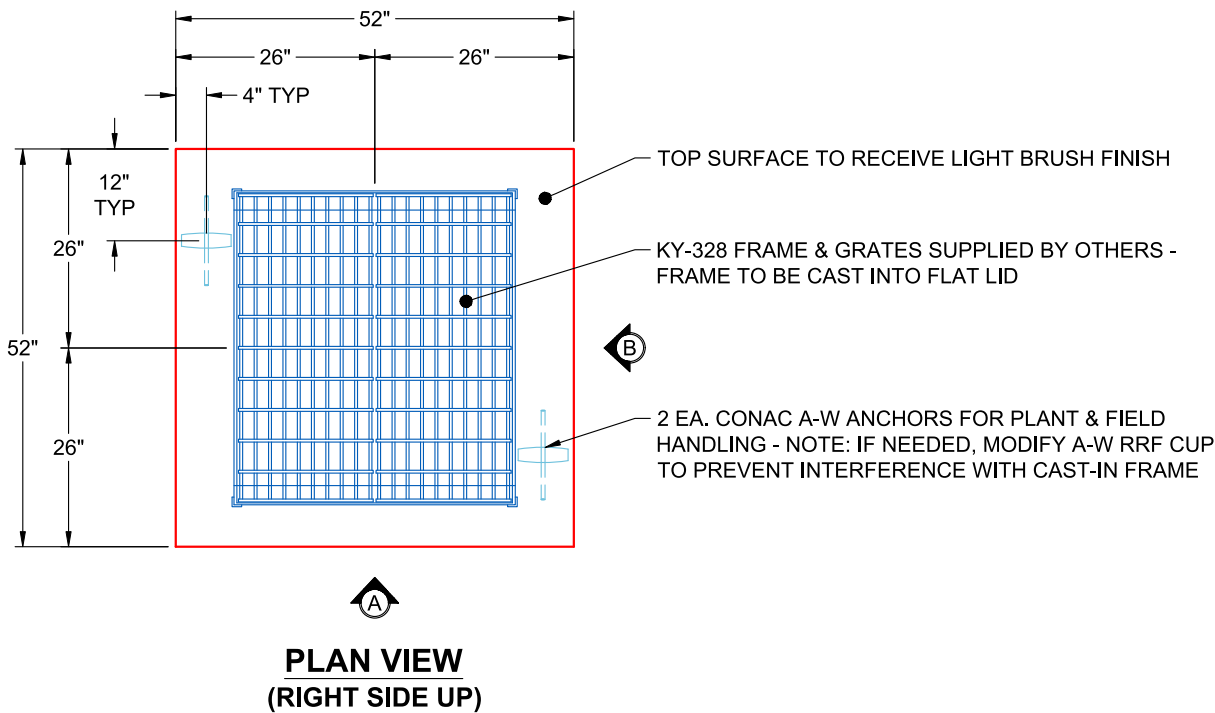

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 996 lb
Volume (Net): 0.25cu.yd

Job Number:

25-2952

Job Name:

KYTC Jefferson Co Call 106
(251315)

Structure:

14

Note:

HOE KY-328 Frame Supplied By
Others To Be Cast Into Flat Lid
