



Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction				Plant: 100 6/12/2026 3:09:35 PM		Tech: J. Horsley - A PC: J. Jarvis				
Structure ID: 14A										
P1 BX3636-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n						
P3) 36" x 36" - CASTING (cast in) - 3" P2) 36" x 36" - CB FLAT TOP 8"W SPEC. (KY-328 CAST IN) F/F - 8" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 28" 1) This Structure Includes a Cast-in Item - HOE KY-328 Frame (Supplied by Others) 2) 36" x 36" - Conseal CS-102 1.00" 1) Hole - 20						0 lb 996 lb 4912 lb 0 lb 0 lb 0 lb Structure Total: 5908 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC DBI TYPE 3 / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-328 FRAME & GRATES SUPPLIED BY OTHERS - FRAME TO BE CAST INTO FLAT LID		
Rim: 560.85' Rim to Invert: 3' Slack: 0" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	557.85'	0°	26"	15" HDPE	17.6"	Hole 20	20"	20"	-2.5"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										




RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)



Invert: 1
Degree: 0°
Horz: 18"
Hole: 20"
Up(): -2.5"

INSIDE WALL DIMENSIONS

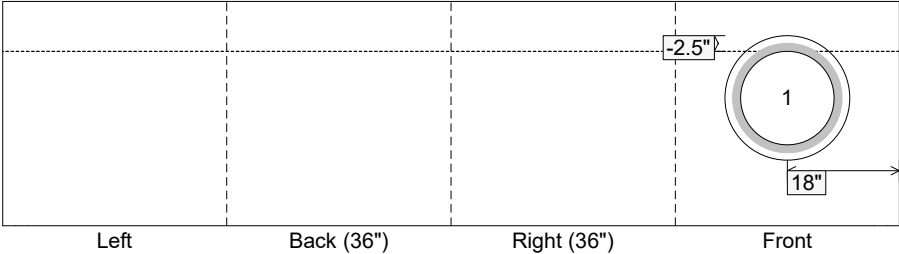

Left Back (36") Right (36") Front

18" 2.5" 28" 8" EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 28" Height (Ext): 36"	Weight (Net): 4912 lb Volume (Net): 1.25cu.yd
----------------------------------	-------------------------------	--	--	--
