

Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)

Job Location: Indiana, KY

Contractor: Louisville Paving and Construction

Plant: 100

6/12/2026 3:09:34 PM

Tech: J. Horsley - A

PC: J. Jarvis



Structure ID: 16

P1 BX3636-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

P3) 36" x 36" - CASTING (cast in) - 3"

P2) 36" x 36" - CB FLAT TOP 8"W SPEC. (KY-328 CAST IN) F/F - 8"

P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 43"

1) This Structure Includes a Cast-in Item - HOE KY-328 Frame (Supplied By Others)

2) 36" x 36" - Conseal CS-102 1.00"

2) Hole - 32

0 lb

996 lb

5816 lb

0 lb

0 lb

0 lb

Structure Total: 6812 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC DBI TYPE 3 / ASTM C-913 SPECS

2. CONCRETE: 4,000 PSI AT 28 DAYS

3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)

4. HOE KY-328 FRAME & GRATES SUPPLIED BY OTHERS - FRAME TO BE CAST INTO FLAT LID

Rim: 559.5'

Rim to Invert: 4.25'


Slack: 0"

Sump: 0"


Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	555.25'	90°	26"	24" HDPE	27.8"	Hole 32	32"	32"	-4"	0"
Invert 2	555.25'	270°	26"	24" HDPE	27.8"	Hole 32	32"	32"	-4"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

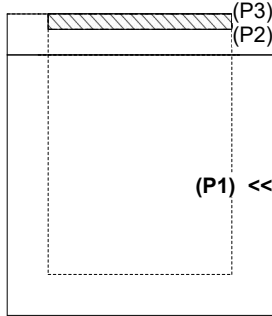

UPSIDE-DOWN VIEW (int. dimenions)



INSIDE WALL DIMENSIONS

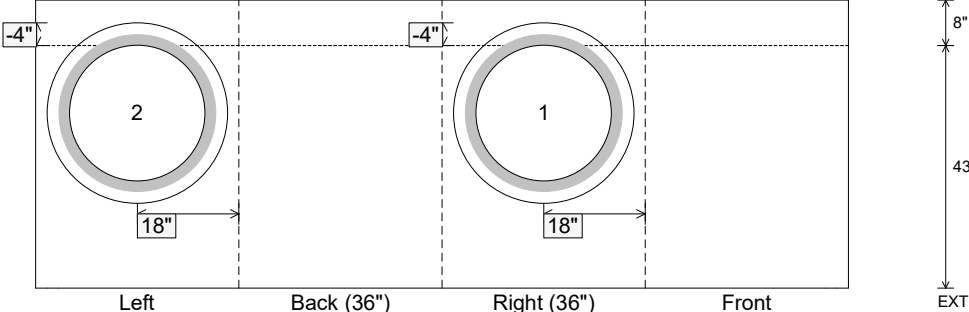

Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 43"

Height (Ext): 51"

Weight (Net): 5816 lb

Volume (Net): 1.49cu.yd
