



Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction					Plant: 100 6/12/2026 3:09:26 PM		Tech: J. Horsley - A PC: J. Jarvis				
Structure ID: 52											
P1 BX24300808VF BOX BASE 8inW, 8inF, Variable Ht F/n											
P3) 15" x 27" - P.I.P. - BY OTHERS - 8" P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 44" 1) 24" x 30" - Conseal CS-102 1.00" 1) 15" x 27" - Conseal CS-102 1.00" 1) Hole - 20 2) Hole - 4					0 lb 963 lb 5143 lb 0 lb 0 lb 0 lb 0 lb -----0 lb Structure Total: 6106 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC DBI TYPE 13G / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-230G FRAME & GRATE SUPPLIED BY OTHERS - POURED IN PLACE BY OTHERS				
Rim: 552.26' Rim to Invert: 5' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	547.26'	0°	20"	15" HDPE	17.6"	Hole 20	20"	20"	-2.5"	0"	
Invert 2	550.26'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	36"	0"	
Invert 3	550.26'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	36"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

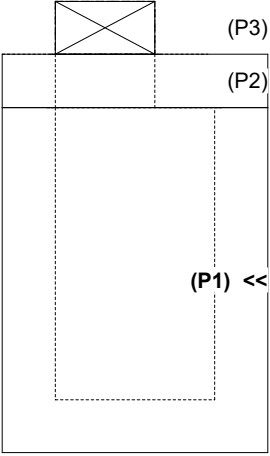

UPSIDE-DOWN VIEW (int. dimensions)

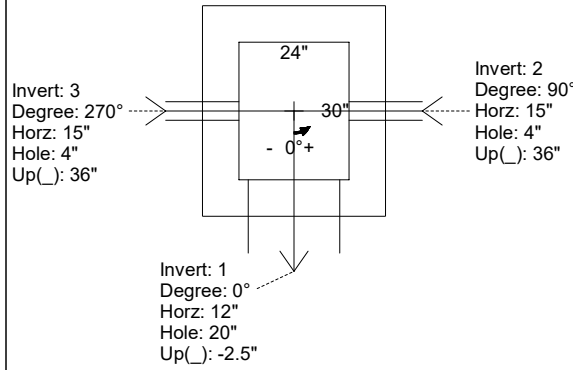

INSIDE WALL DIMENSIONS

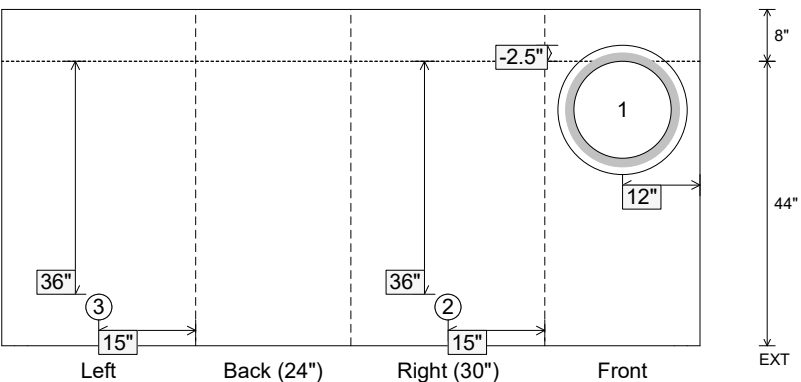

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 44" Height (Ext): 52"	Weight (Net): 5143 lb Volume (Net): 1.31cu.yd
----------------------------------	-------------------------------	--	--	--
