

Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)

Job Location: Indiana, KY

Contractor: Louisville Paving and Construction

Plant: 100

6/12/2026 3:09:54 PM

Tech: J. Horsley - A

PC: J. Jarvis



Structure ID: 71

P1 BX24300808VF

BOX BASE 8inW, 8inF, Variable Ht T/n

P4) 15" x 27" - P.I.P. - BY OTHERS - 8"

P3) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8"

P2) 24" x 30" - BOX RISER 8inW F/G - 36"

P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht T/n - 32"

2) 24" x 30" - Conseal CS-102 1.00"

1) 15" x 27" - Conseal CS-102 1.00"

1) Hole - 18

2) Hole - 4

0 lb

963 lb

3366 lb

4072 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 8402 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC DBI TYPE 13G / ASTM C-913 SPECS

2. CONCRETE: 4,000 PSI AT 28 DAYS

3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)

4. HOE KY-230G FRAME & GRATE SUPPLIED BY OTHERS - POURED IN PLACE BY OTHERS

Rim: 551.62'

Rim to Invert: 7'


Slack: 0"

Sump: 0"


Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	544.62'	90°	23"	12" HDPE	14.5"	Hole 18	18"	18"	-3"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

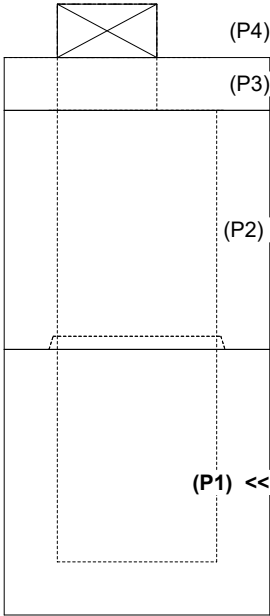

UPSIDE-DOWN VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

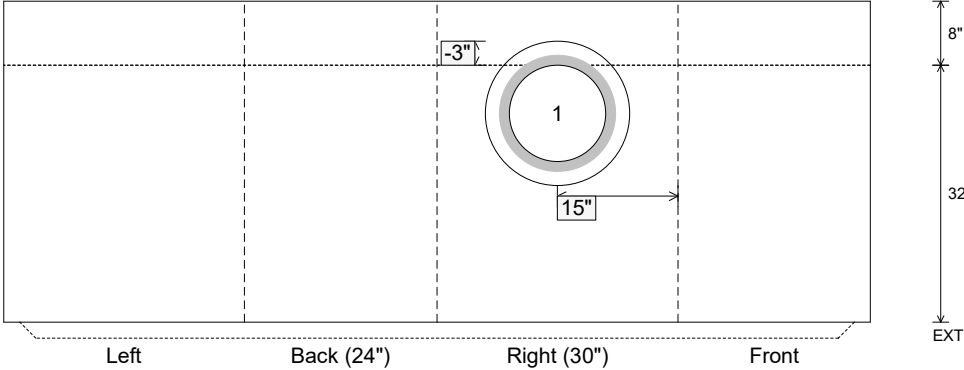

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 32"

Height (Ext): 40"

Weight (Net): 4072 lb

Volume (Net): 1.04cu.yd
