


Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc				Plant: 100 9/2/2026 1:31:39 PM		Tech: Jared - F PC: T. Ryan						
Structure ID: DMH1												
P1 MH048BA60CDARED				MH BASE w/DROP/ConBlock-CDA Red T/n								
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4" P3) 48" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red F/G - 12" P2) 48" - MH RISER w/DROP/ConBlock-CDA Red T/G - 60" P1) 48" - MH BASE w/DROP/ConBlock-CDA Red T/n - 60" 2) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 2) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) Kor-N-Seal2 - S206-20L 1) Drop Tee - 12" PVC 1) PSX - 16M NYLO 1) Drop Elbow - 12" PVC 10) MH Step ML-10-TDS-NGR - 10" Rim: 992.15' Rim to Invert: 11.75' Slack: 0" Sump: 2" Structure Total: 12693 lb						0 lb 270 lb 1580 lb 4140 lb 5249 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 6 lb 0 lb 8 lb 0 lb 0 lb		Structure Notes: - PER ASTM C478 SPECIFICATIONS. - CONCRETE = 4,000 PSI AT 28 DAYS. - ADMIXTURE = CONBLOCK CDA RED. - CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). - EXTERIOR DROP ASSEMBLY @ 90 DEGREES. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	980.4'	0°	0"	16" DI	17.5"	Kor-N-Seal2 S206-20L	20"	20.629"	0"	0"		
Invert 2												
Invert 3	980.65'	180°	91.125"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	3"	0"		
Invert 4	980.65'	90°	45.5"	12" PVC SDR35	12.5"	Drop Elbow 12" PVC	12.5"	12.646"	4.75"	0"		
Invert 5												
Invert 6												
Invert 7												
Invert 8												

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 60" Height (Ext): 66"	Weight (Net): 5249 lb Volume (Net): 1.34cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc				Plant: 100 9/2/2026 1:31:39 PM		Tech: Jared - F PC: T. Ryan						
Structure ID: DMH1												
P1 MH048BA60CDARED				MH BASE w/DROP/ConBlock-CDA Red T/n								
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4" P3) 48" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red F/G - 12" P2) 48" - MH RISER w/DROP/ConBlock-CDA Red T/G - 60" P1) 48" - MH BASE w/DROP/ConBlock-CDA Red T/n - 60" 2) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 2) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) Kor-N-Seal2 - S206-20L 1) Drop Tee - 12" PVC 1) PSX - 16M NYLO 1) Drop Elbow - 12" PVC 10) MH Step ML-10-TDS-NGR - 10" Rim: 992.15' Rim to Invert: 11.75' Slack: 0" Sump: 2" Structure Total: 12693 lb						0 lb 270 lb 1580 lb 4140 lb 5249 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 6 lb 0 lb 8 lb 0 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). 5. EXTERIOR DROP ASSEMBLY @ 90 DEGREES. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	980.4'	0°	0"	16" DI	17.5"	Kor-N-Seal2 S206-20L	20"	20.629"	0"	0"		
Invert 2												
Invert 3	980.65'	180°	91.125"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	3"	0"		
Invert 4	980.65'	90°	45.5"	12" PVC SDR35	12.5"	Drop Elbow 12" PVC	12.5"	12.646"	4.75"	0"		
Invert 5												
Invert 6												
Invert 7												
Invert 8												

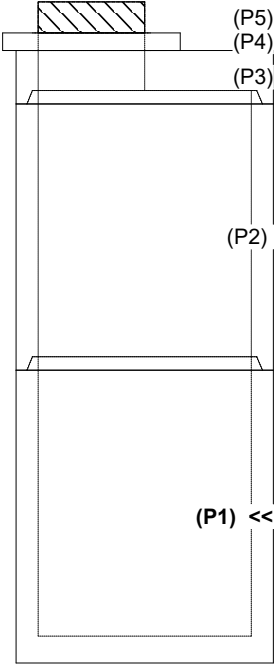


(P5)
(P4)
(P3)

(P2)

(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

FOR INVERT ONLY

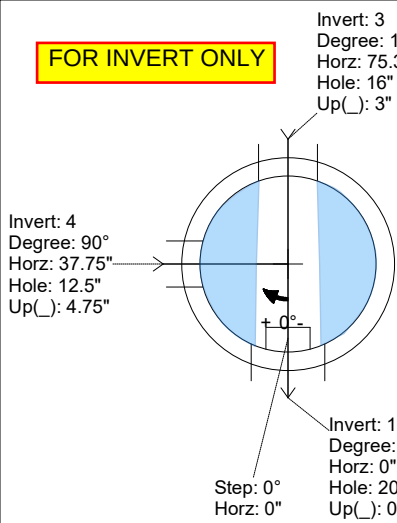


Invert: 3
Degree: 180°
Horz: 75.375"
Hole: 16"
Up(): 3"

Invert: 4
Degree: 90°
Horz: 37.75"
Hole: 12.5"
Up(): 4.75"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 20"
Up(): 0"

Step: 0°
Horz: 0"

UPSIDE-DOWN VIEW (int. dimensions)

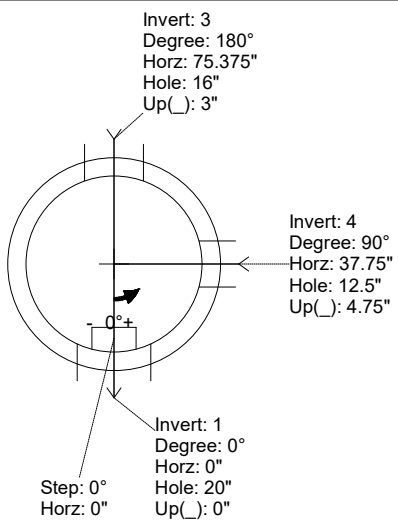


Invert: 3
Degree: 180°
Horz: 75.375"
Hole: 16"
Up(): 3"

Invert: 4
Degree: 90°
Horz: 37.75"
Hole: 12.5"
Up(): 4.75"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 20"
Up(): 0"

Step: 0°
Horz: 0"

INSIDE WALL DIMENSIONS

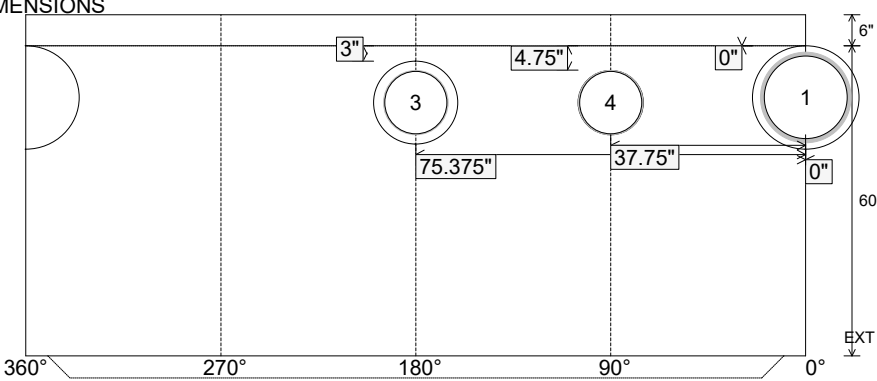

360° 270° 180° 90° 0°

3" 4.75" 0" 75.375" 37.75" 0" 60" 6" EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 60" Height (Ext): 66"	Weight (Net): 5249 lb Volume (Net): 1.34cu.yd
----------------------------------	---------------------------------	--	--	--
