

Job Name: 25-3040B - Stonedale Farms
Job Location: Nicholasville, KY
Contractor: Weddle Enterprises, Inc

Plant: 100

Tech: Jared - F

9/2/2026 1:32:12 PM

PC: T. Ryan



Structure ID: DMH1

P3 MH048LD12CDARED

MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red F/G

- P5) 24" - CASTING HEIGHT - 7"
P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4"
P3) 48" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red F/G - 12"
P2) 48" - MH RISER w/DROP/ConBlock-CDA Red T/G - 60"
P1) 48" - MH BASE w/DROP/ConBlock-CDA Red T/n - 60"
2) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
2) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
1) ADMIXTURE CONBLOCK CDA RED
2) 48" - Con Seal CS-102 1.00" (Double)
2) 24" - Con Seal CS-102 1.00" (Double)
1) Kor-N-Seal2 - S206-20L
1) Drop Tee - 12" PVC
1) PSX - 16M NYLO
1) Drop Elbow - 12" PVC
10) MH Step ML-10-TDS-NCR - 10"



0 lb
270 lb
1580 lb
4140 lb
5249 lb
0 lb
0 lb
1440 lb
0 lb
0 lb
0 lb
6 lb
0 lb
8 lb
0 lb
0 lb

Structure Total:

12693 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. ADMIXTURE = CONBLOCK CDA RED.
 4. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY).
 5. EXTERIOR DROP ASSEMBLY @ 90 DEGREES.
- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB = H20 LOADING.
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

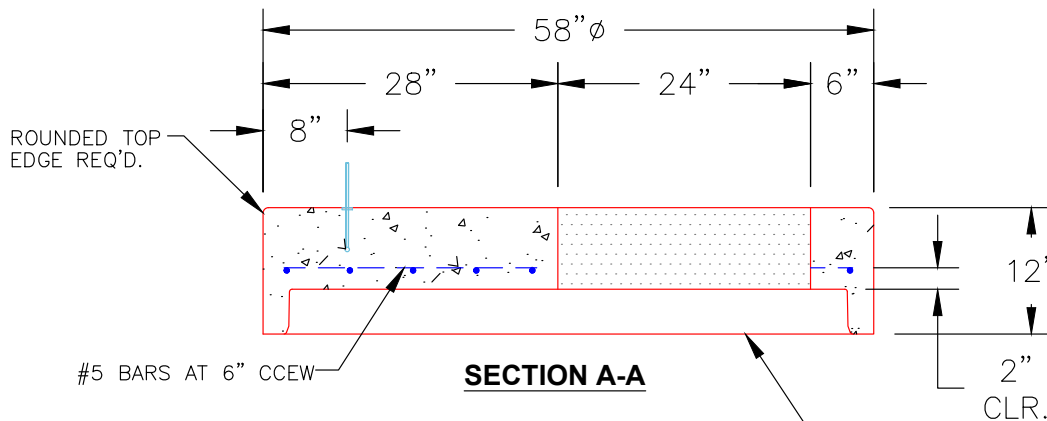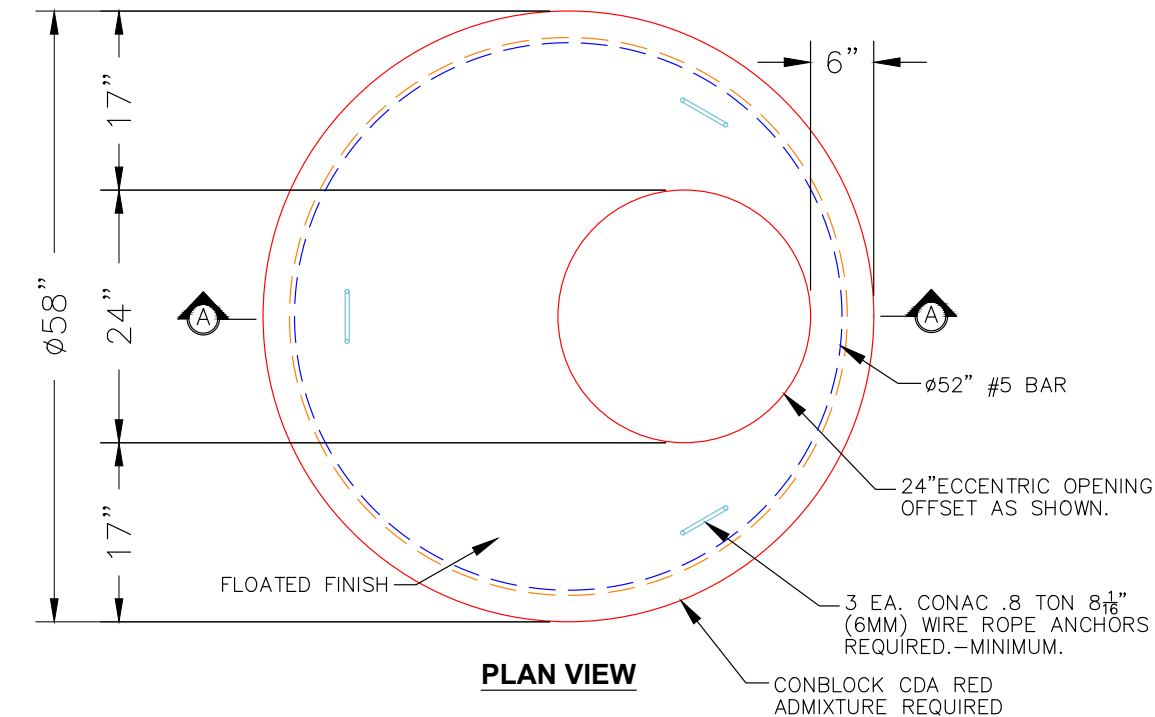

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1580 lb
Volume (Net): 0.39cu.yd
