

Job Name: 25-3040B - Stonedale Farms
Job Location: Nicholasville, KY
Contractor: Weddle Enterprises, Inc

Plant: 100

Tech: Jared - F

7/23/2026 3:35:42 PM

PC: T. Ryan



Structure ID: DMH14

P3 MH048CN24

ECC CONE w/ 24" HOLE F/G



- P4) 24" - CASTING HEIGHT - 7"
P3) 48" - ECC CONE w/ 24" HOLE F/G - 24"
P2) 48" - MH RISER T/G - 36"
P1) 48" - MH BASE w/DROP Custom Ht T/n - 58"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL - FULL HEIGHT
2) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
2) PSX - 16M NYLO
1) Drop Tee - 8" PVC
1) Drop Elbow - 8" PVC
10) MH Step ML-10-TDS-NCR - 10"

0 lb
1550 lb
2515 lb
7921 lb
0 lb
0 lb
1440 lb
0 lb
0 lb
0 lb
16 lb
0 lb
0 lb
0 lb

Structure Total: 13442 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY).
 4. EXTERIOR DROP ASSEMBLY @ 270 DEGREES.
- REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

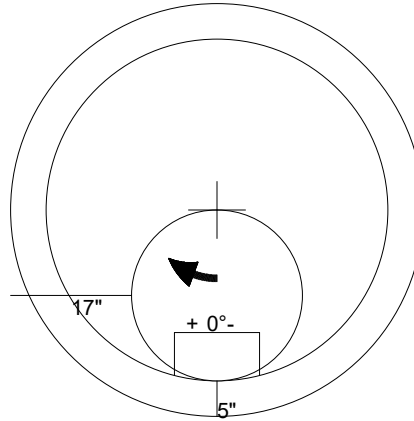

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 24"

Weight (Net): 1550 lb
Volume (Net): 0.33cu.yd
