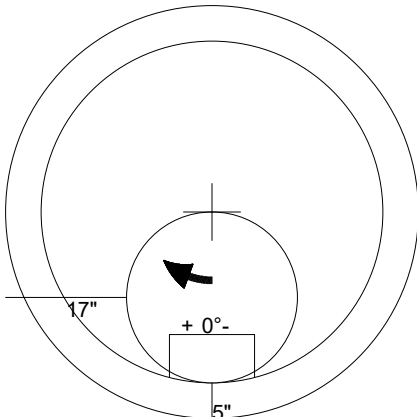



Job Name: 25-3040B - Stonedale Farms		Plant: 100	Tech: Jared - F	
Job Location: Nicholasville, KY		9/2/2026 1:34:38 PM	PC: T. Ryan	
Contractor: Weddle Enterprises, Inc				
Structure ID: DMH4				
P3 MH048CN36CDARED		ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G		
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 3" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 36" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 24" P1) 48" - MH BASE w/DROP/ConBlock-CDA Red T/n - 48" 2) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 2) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 16M NYLO 1) Drop Tee - 12" PVC 1) Drop Elbow - 12" PVC 9) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 2251 lb 1677 lb 4494 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 8 lb 0 lb 0 lb 0 lb Structure Total: 10072 lb	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). 5. EXTERIOR DROP ASSEMBLY @ 198 DEGREES . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 36" - (P3)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 2251 lb Volume (Net): 0.57cu.yd
