



Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc					Plant: 100 8/27/2026 1:49:28 PM		Tech: Jared - F PC: T. Ryan				
Structure ID: MH10											
P1 MH048BA24CDARED				MH BASE w/ConBlock-CDA Red T/n							
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 36" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24" 2) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 2) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 16M NYLO 8) MH Step ML-10-TDS-NCR - 10"					0 lb 1961 lb 2515 lb 2835 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 16 lb 0 lb ----- 8768 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 1018' Rim to Invert: 8' Slack: 1" Sump: 2" Step Position: 0"											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	1010'	0°	0"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	0"	0"	
Invert 2	1010.1'	177°	89.625"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

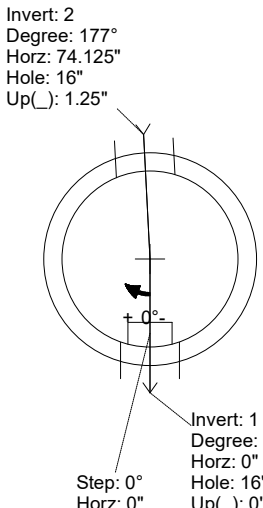

UPSIDE-DOWN VIEW (int. dimensions)

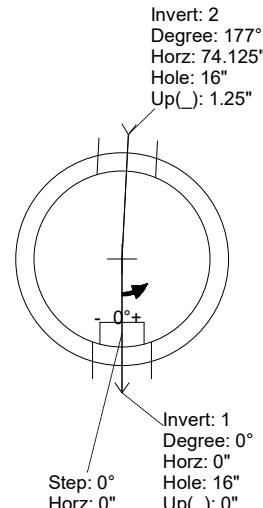

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2835 lb Volume (Net): 0.72cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc					Plant: 100		Tech: Jared - F			
					8/27/2026 1:49:28 PM		PC: T. Ryan			
Structure ID: MH10										
P1 MH048BA24CDARED					MH BASE w/ConBlock-CDA Red T/n					
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 36" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24" 2) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 2) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 16M NYLO 8) MH Step ML-10-TDS-NCR - 10"					0 lb 1961 lb 2515 lb 2835 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 8768 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1018' Rim to Invert: 8' Slack: 1" Sump: 2" Step Position: 0"										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1010'	0°	0"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	0"	0"
Invert 2	1010.1'	177°	89.625"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	1.25"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2835 lb Volume (Net): 0.72cu.yd
----------------------------------	---------------------------------	--	--	--
