


Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc					Plant: 100 8/27/2026 1:49:30 PM		Tech: Jared - F PC: T. Ryan			
Structure ID: MH12										
P1 MH048BA36CDARED					MH BASE w/ConBlock-CDA Red T/n					
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 16M NYLO 7) MH Step ML-10-TDS-NCR - 10"					0 lb 3116 lb 3588 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 8168 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1020.87' Rim to Invert: 6.92' Slack: 0.04" Sump: 2" Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1013.95'	0°	0"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	0"	0"
Invert 2	1014.05'	94°	47.625"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	1.25"	0"
Invert 3	1014.6'	176°	89.125"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	7.75"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

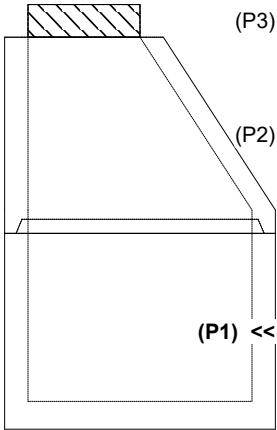


(P3)

(P2)

(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

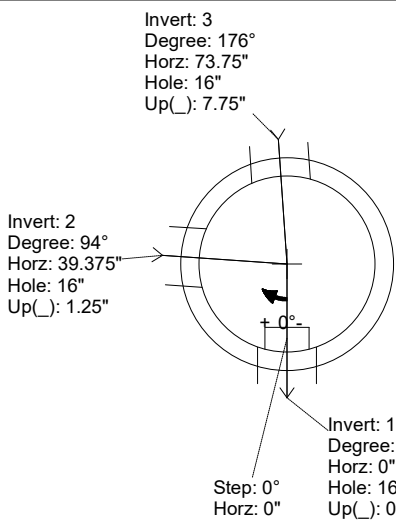


Invert: 3
Degree: 176°
Horz: 73.75"
Hole: 16"
Up(): 7.75"

Invert: 2
Degree: 94°
Horz: 39.375"
Hole: 16"
Up(): 1.25"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 16"
Up(): 0"

Step: 0°
Horz: 0"

UPSIDE-DOWN VIEW (int. dimensions)

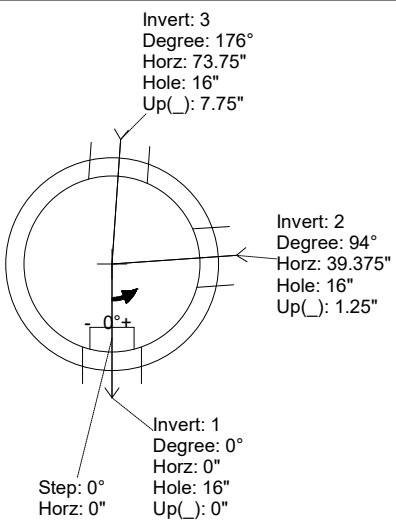


Invert: 3
Degree: 176°
Horz: 73.75"
Hole: 16"
Up(): 7.75"

Invert: 2
Degree: 94°
Horz: 39.375"
Hole: 16"
Up(): 1.25"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 16"
Up(): 0"

Step: 0°
Horz: 0"

INSIDE WALL DIMENSIONS

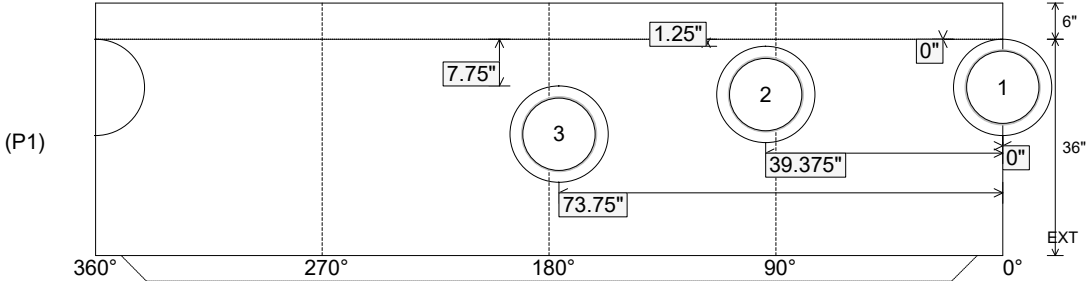

(P1)

360° 270° 180° 90° 0°

36"

42"

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3588 lb Volume (Net): 0.92cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc					Plant: 100		Tech: Jared - F			
					8/27/2026 1:49:30 PM		PC: T. Ryan			
Structure ID: MH12										
P1 MH048BA36CDARED					MH BASE w/ConBlock-CDA Red T/n					
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 16M NYLO 7) MH Step ML-10-TDS-NCR - 10"					0 lb 3116 lb 3588 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 8168 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1020.87' Rim to Invert: 6.92' Slack: 0.04" Sump: 2" Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1013.95'	0°	0"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	0"	0"
Invert 2	1014.05'	94°	47.625"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	1.25"	0"
Invert 3	1014.6'	176°	89.125"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	7.75"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3588 lb Volume (Net): 0.92cu.yd
----------------------------------	---------------------------------	--	--	--
