

Job Name: 25-3040B - Stonedale Farms

Job Location: Nicholasville, KY

Contractor: Weddle Enterprises, Inc

Plant: 100

7/23/2026 3:34:52 PM

Tech: Jared - F

PC: T. Ryan



Structure ID: MH13

P1 MH048BA30

MH BASE T/n

P3) 24" - CASTING HEIGHT - 7"

P2) 48" - ECC CONE w/ 24" HOLE F/G - 36"

P1) 48" - MH BASE T/n - 30"

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) 48" - MH INVERT CHANNEL - FULL HEIGHT

1) 48" - Conseal CS-102 1.00" (Double)

1) 24" - Conseal CS-102 1.00" (Double)

2) PSX - 16M NYLO

1) PSX - 12-08 NYLO

1) PSX - 12-06 NYLO

4) MH Step ML-10-TDS-NCR - 10"

0 lb

3000 lb

3159 lb

0 lb

0 lb

1440 lb

0 lb

0 lb

16 lb

8 lb

8 lb

0 lb

Structure Total: 7631 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY).

REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 1021.86'

Rim to Invert: 6'

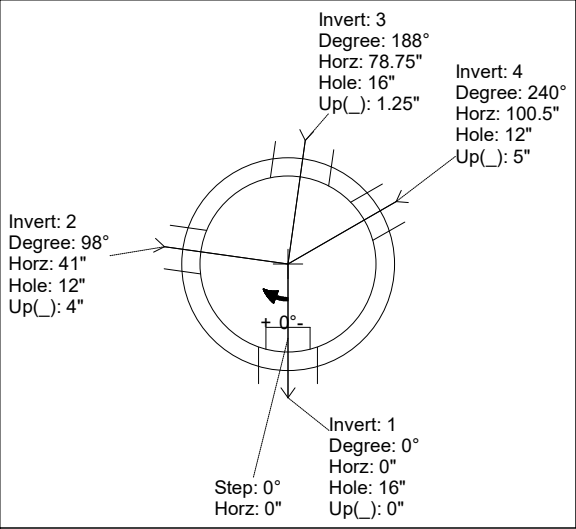
Slack: 1"

Sump: 2"


Step Position: 0°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1015.86'	0°	0"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	0"	0"
Invert 2	1016.19'	98°	49.625"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	4"	0"
Invert 3	1015.96'	188°	95.125"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	1.25"	0"
Invert 4	1016.36'	240°	121.5"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	5"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)



UPSIDE-DOWN VIEW (int. dimensions)

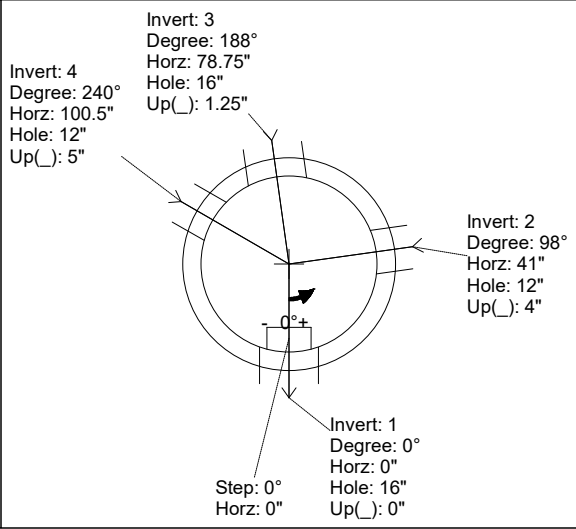

INSIDE WALL DIMENSIONS

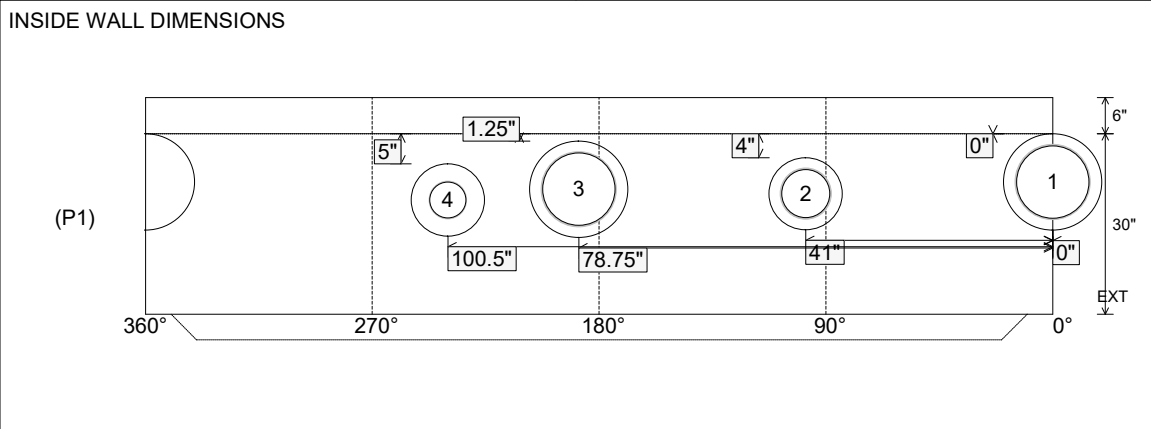

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 5"

Floor Height: 6"





Height (Int): 30"

Height (Ext): 36"

Weight (Net): 3159 lb

Volume (Net): 0.81cu.yd

Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc					Plant: 100 7/23/2026 3:34:52 PM		Tech: Jared - F PC: T. Ryan			
Structure ID: MH13										
P1 MH048BA30		MH BASE T/n								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 16M NYLO 1) PSX - 12-08 NYLO 1) PSX - 12-06 NYLO 4) MH Step ML-10-TDS-NCR - 10"					0 lb 3000 lb 3159 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 16 lb 8 lb 8 lb 0 lb ----- Structure Total: 7631 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1021.86' Rim to Invert: 6' Slack: 1" Sump: 2" Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1015.86'	0°	0"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	0"	0"
Invert 2	1016.19'	98°	49.625"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	4"	0"
Invert 3	1015.96'	188°	95.125"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	1.25"	0"
Invert 4	1016.36'	240°	121.5"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	5"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

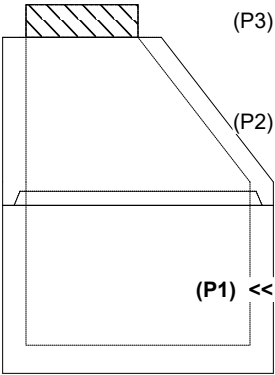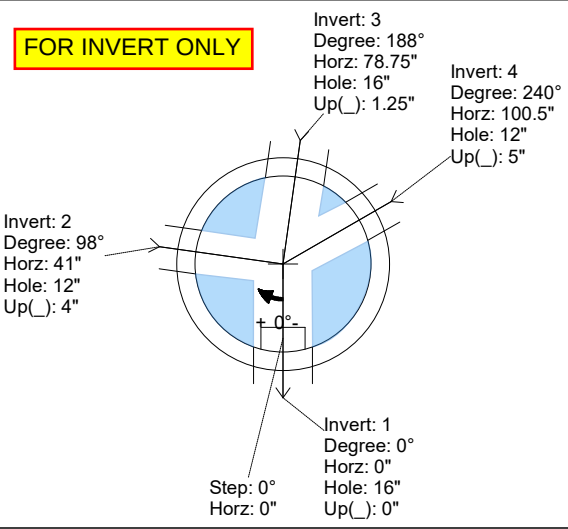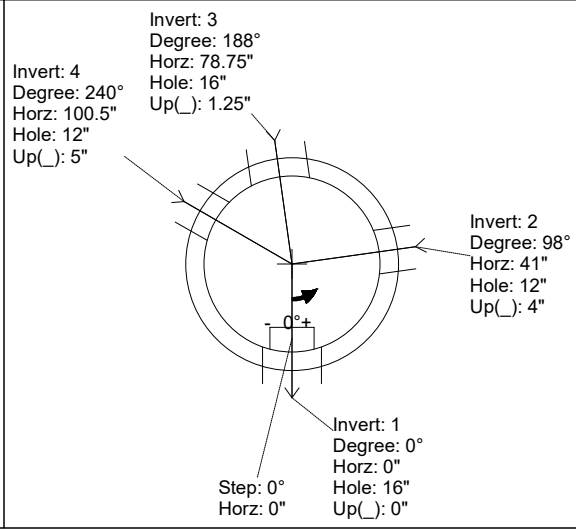	RIGHT-SIDE UP VIEW (int. dimensions)		UPSIDE-DOWN VIEW (int. dimensions)	
				
INSIDE WALL DIMENSIONS				
				

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3159 lb Volume (Net): 0.81cu.yd
----------------------------------	---------------------------------	--	--	--
