

Job Name: 25-3040B - Stonedale Farms
Job Location: Nicholasville, KY
Contractor: Weddle Enterprises, Inc

Plant: 100

7/24/2026 8:44:02 AM

Tech: Jared - F

PC: T. Ryan



Structure ID: MH17

P3 GR6

GRADE RING

P4) 24" - CASTING HEIGHT - 7"

P3) 24" - GRADE RING - 6"

P2) 48" - ECC CONE w/ 24" HOLE - 42"

P1) 48" - MH BASE - 36"

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) 48" - MH INVERT CHANNEL - FULL HEIGHT

1) 48" - Conseal CS-102 1.00" (Double)

2) 24" - Conseal CS-102 1.00" (Double)

2) PSX - 16M NYLO

6) MH Step ML-10-TDS-NCR - 10"

0 lb Structure Notes:

405 lb

3200 lb

3674 lb

0 lb

0 lb

1440 lb

0 lb

0 lb

16 lb

0 lb

Structure Total:

8735 lb

1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY).

REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)


- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


NOTES:

- GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS
-CONCRETE: 4,000 PSI @ 28 DAYS
-REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)

- WEIGHT: 6" 405 LBS.

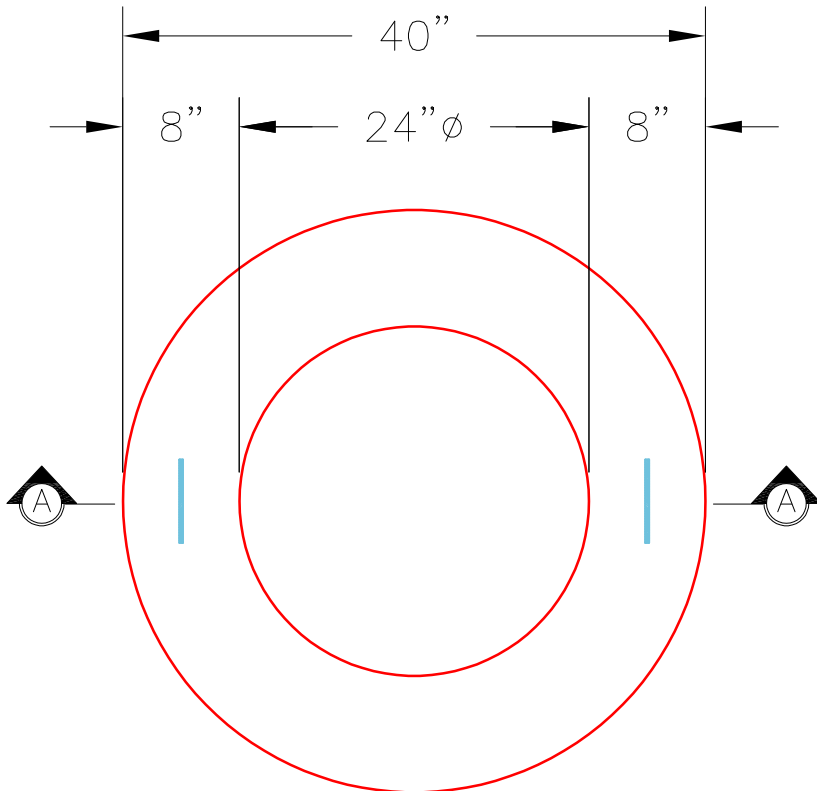


PLAN VIEW

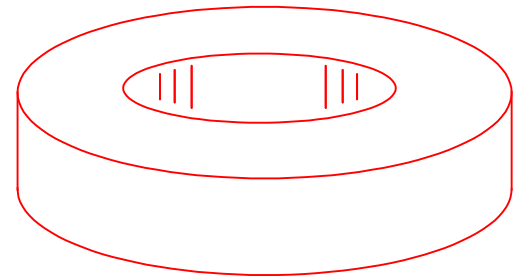

ISOMETRIC VIEW

2x CONAC WRA016 WIRE ROPE LIFTING ANCHORS

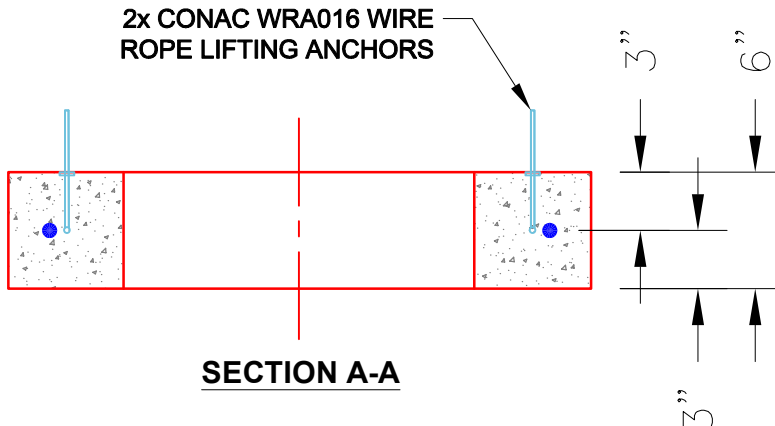

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 6"

Weight (Net): 405 lb
Volume (Net): 0.1cu.yd
