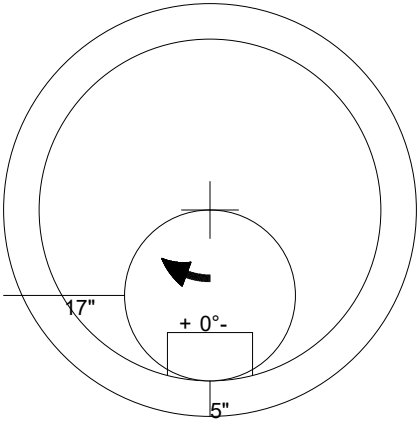



Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc		Plant: 100 7/23/2026 3:35:45 PM	Tech: Jared - F PC: T. Ryan		
Structure ID: MH19					
P3 MH048CN36		ECC CONE w/ 24" HOLE F/G			
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 36" P2) 48" - MH RISER T/G - 24" P1) 48" - MH BASE T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 16M NYLO 1) PSX - 12-08 NYLO 6) MH Step ML-10-TDS-NCR - 10"		0 lb 3000 lb 1677 lb 3121 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 24 lb 8 lb 0 lb ----- Structure Total: 9269 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
					
 48" - ECC CONE w/ 24" HOLE F/G - 36" - (P3)					
Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 3000 lb Volume (Net): 0.5cu.yd
