



Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc					Plant: 100 7/23/2026 3:35:22 PM		Tech: Jared - F PC: T. Ryan				
Structure ID: MH20											
P2		MH048RS48		MH RISER T/G							
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 24" P2) 48" - MH RISER T/G - 48" P1) 48" - MH BASE T/n - 18" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 7) MH Step ML-10-TDS-NCR - 10"					0 lb 1550 lb 3353 lb 2444 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 8811 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 1035.75' Rim to Invert: 8' Slack: 1" Sump: 2" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

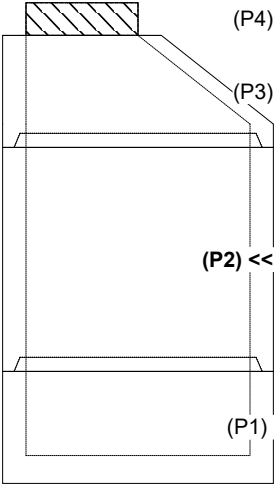


(P4)
(P3)
(P2) <<
(P1)

RIGHT-SIDE UP VIEW (int. dimensions)



Step: 0°
Horz: 0"

INSIDE WALL DIMENSIONS

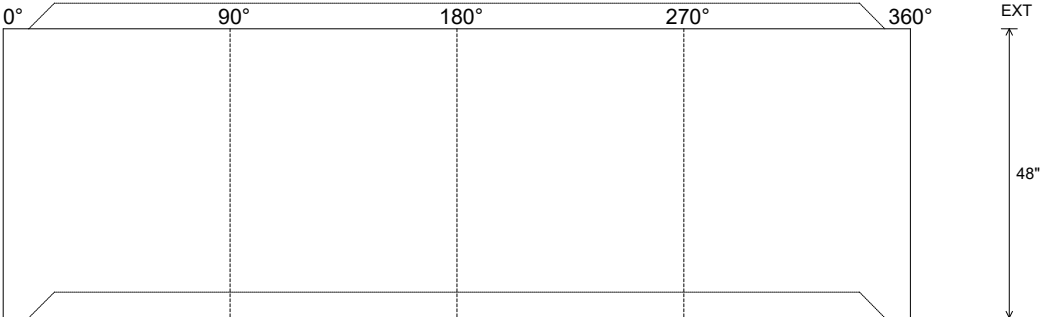

(P2)

EXT
48"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 3353 lb Volume (Net): 0.86cu.yd
----------------------------------	------------------------------------	--	--	--
