

Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc					Plant: 100		Tech: Jared - F			
					8/27/2026 1:49:30 PM		PC: T. Ryan			
Structure ID: MH25										
P1 MH048BA36CDARED					MH BASE w/ConBlock-CDA Red T/n					
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE CONBLOCK CDA RED 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 7) MH Step ML-10-TDS-NCR - 10"					0 lb 3116 lb 3701 lb 0 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 8282 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1016.75' Rim to Invert: 7' Slack: 1" Sump: 2" Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1009.75'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	1009.85'	90°	45.5"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"
Invert 3	1009.85'	180°	91.125"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)


UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3701 lb Volume (Net): 0.94cu.yd
----------------------------------	---------------------------------	--	--	--


Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc					Plant: 100 8/27/2026 1:49:30 PM		Tech: Jared - F PC: T. Ryan					
Structure ID: MH25												
P1 MH048BA36CDARED					MH BASE w/ConBlock-CDA Red T/n							
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE CONBLOCK CDA RED 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 7) MH Step ML-10-TDS-NCR - 10"					0 lb 3116 lb 3701 lb 0 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 8282 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 1016.75' Rim to Invert: 7' Slack: 1" Sump: 2" Step Position: 0°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	1009.75'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"		
Invert 2	1009.85'	90°	45.5"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"		
Invert 3	1009.85'	180°	91.125"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.25"	0"		
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

RIGHT-SIDE UP VIEW (int. dimensions)

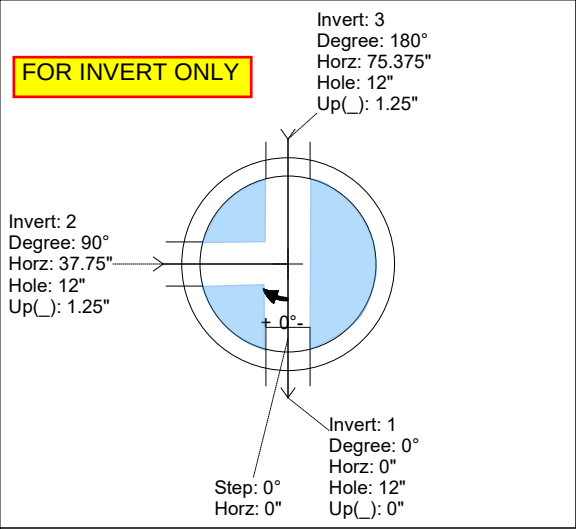


FOR INVERT ONLY

UPSIDE-DOWN VIEW (int. dimensions)

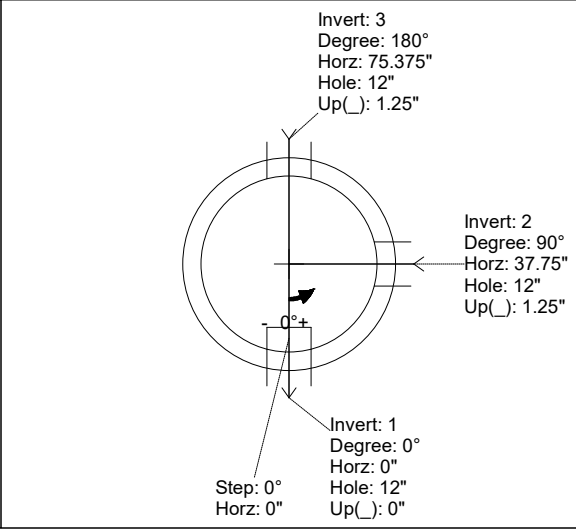

INSIDE WALL DIMENSIONS

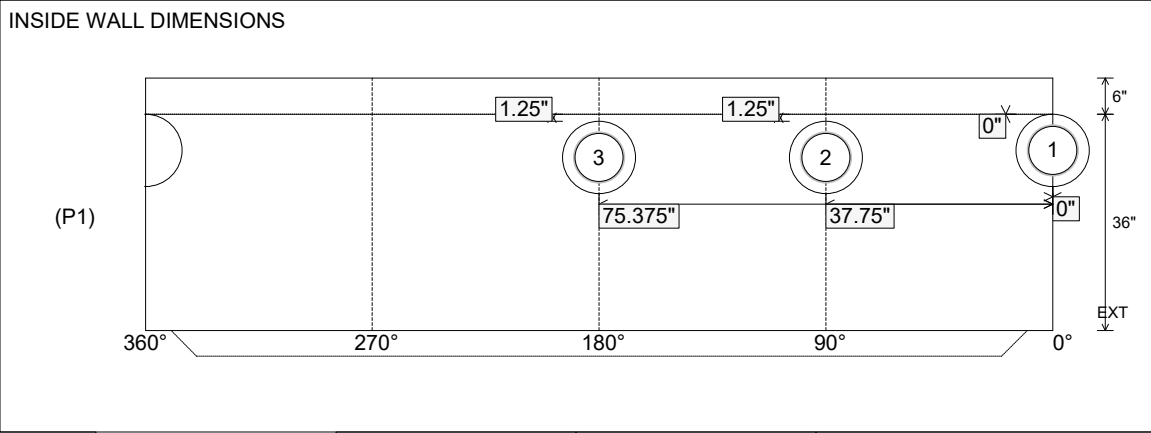

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 36" Height (Ext): 42"	Weight (Net): 3701 lb Volume (Net): 0.94cu.yd
----------------------------------	---------------------------------	--	--	--
