

Job Name: 25-3040B - Stonedale Farms
Job Location: Nicholasville, KY
Contractor: Weddle Enterprises, Inc

Plant: 100

7/24/2026 8:44:03 AM

Tech: Jared - F

PC: T. Ryan



Structure ID: MH28

P3 GR4

GRADE RING


- P4) 24" - CASTING HEIGHT - 7"
P3) 24" - GRADE RING - 4"
P2) 48" - ECC CONE w/ 24" HOLE - 30"
P1) 48" - MH BASE - 24"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL - FULL HEIGHT
1) 48" - Conseal CS-102 1.00" (Double)
2) 24" - Conseal CS-102 1.00" (Double)
1) PSX - 12-08 NYLO
1) PSX - 12-06 NYLO
4) MH Step ML-10-TDS-NCR - 10"

0 lb	Structure Notes:
270 lb	1. PER ASTM C478 SPECIFICATIONS.
2050 lb	2. CONCRETE = 4,000 PSI AT 28 DAYS.
2911 lb	3. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY).
0 lb	
0 lb	
1440 lb	REINFORCING PER ASTM A615 (GRADE 60).
0 lb	- CONE (As .12)
0 lb	- RISER/WALLS (As .12)
8 lb	- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
8 lb	
0 lb	


Structure Total: 6687 lb	

NOTES:


- GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS:
 - CONCRETE: 4,000 PSI @ 28 DAYS.
 - REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)
- WEIGHT: 4" 270 Lbs.

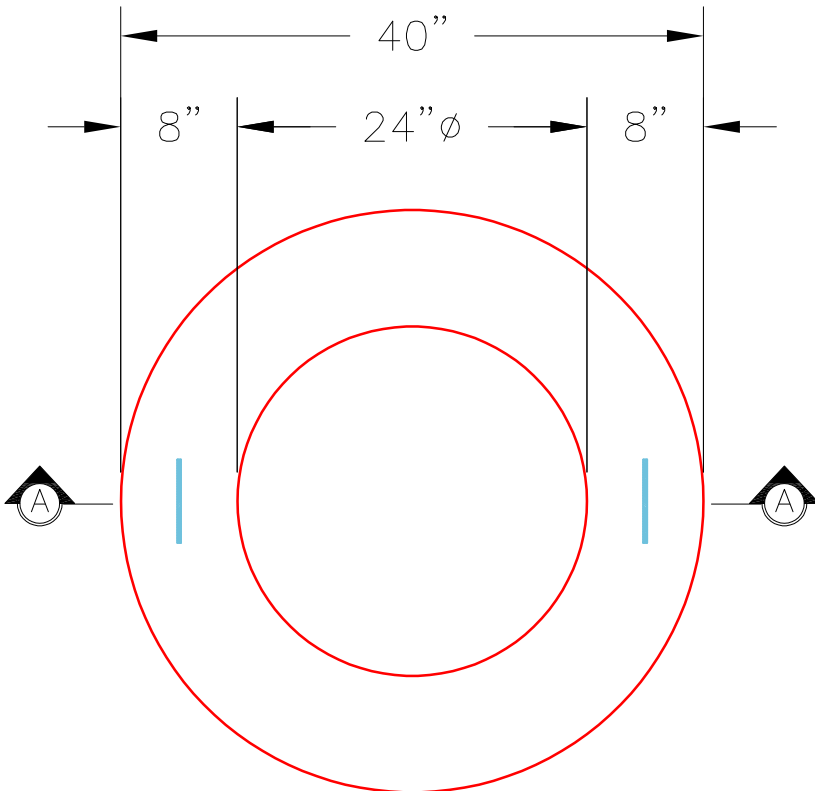

PLAN VIEW

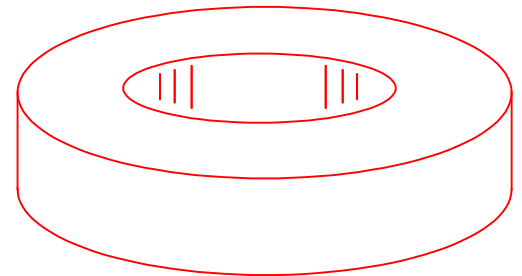

ISOMETRIC VIEW

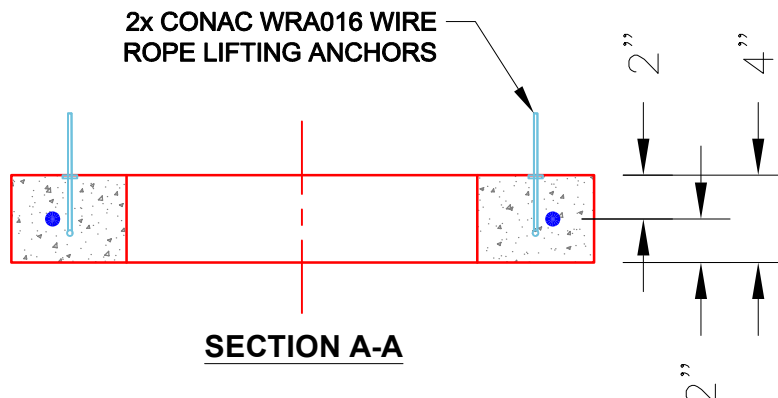

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 4"

Weight (Net): 270 lb
Volume (Net): 0.07cu.yd
