



Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc					Plant: 100 9/4/2026 12:10:23 PM		Tech: Jared - F PC: T. Ryan				
Structure ID: PS 2											
P3 MH144RSVFCDARED			MH RISER Custom Ht, w/ConBlock-CDA Red T/G								
P5) 36" x 60" - HATCH (CAST FLUSH) - 3" P4) 144" - MH FLAT TOP w/36"x60" Hatch w/Conblock CDA Red F/G - 18" P3) 144" - MH RISER Custom Ht, w/ConBlock-CDA Red T/G - 90" P2) 144" - MH RISER Custom Ht, w/ConBlock-CDA Red T/G - 90" P1) 144" - MH BASE EXT OCTAGON (12"F) Custom Ht, w/ConBlock-CDA Red T/n - 60" 3) JOINT WRAP - 12" WD x 144" MAC WRAP 1) HATCH (Alum.) - HALLIDAY W1S 36"x60" 1) ADMIXTURE CONBLOCK CDA RED 3) 144" - Conseal CS-231 1.00" (Double) 1) 36" x 60" - Conseal CS-231 1.00" (Double) 2) Kor-N-Seal2 - S206-20L 1) PSX - 12-06 NYLO					100 lb 22362 lb 48300 lb 48080 lb 59299 lb 0 lb 116 lb 0 lb 0 lb 0 lb 13 lb 8 lb		Structure Notes: . 1. PER ASCTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. HATCH BY ICAST (HALLIDAY W1S 36"x60"). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DOUBLE MAT) - WALLS/RISER (As .36) - FLOOR (As .31) #5 BARS AT 10" C.C.E.W. (DOUBLE MAT)				
Rim: 992.5' Rim to Invert: 20' Slack: 0" Sump: 18" Step Position:					Structure Total: 178279 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2	989.5'	0°	0"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.014"	63"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

NOTE:
4 EA. 8CA18 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING
– INSTALLED AT 45, 135, 225 & 315, 24" FROM TOP OF WALLS

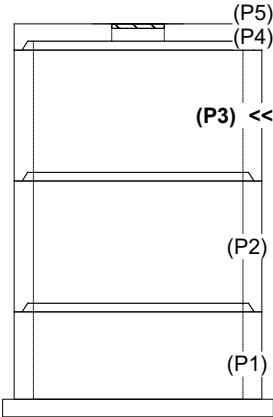

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 13" Floor Height: 0"	Height (Int): 90" Height (Ext): 90"	Weight (Net): 48300 lb Volume (Net): 12.34cu.yd
----------------------------------	------------------------------------	---	--	--
