


Floor (Bot): 970'
Overall Height: 22.5'
Slack: 0"

Structure Total: 178279 lb

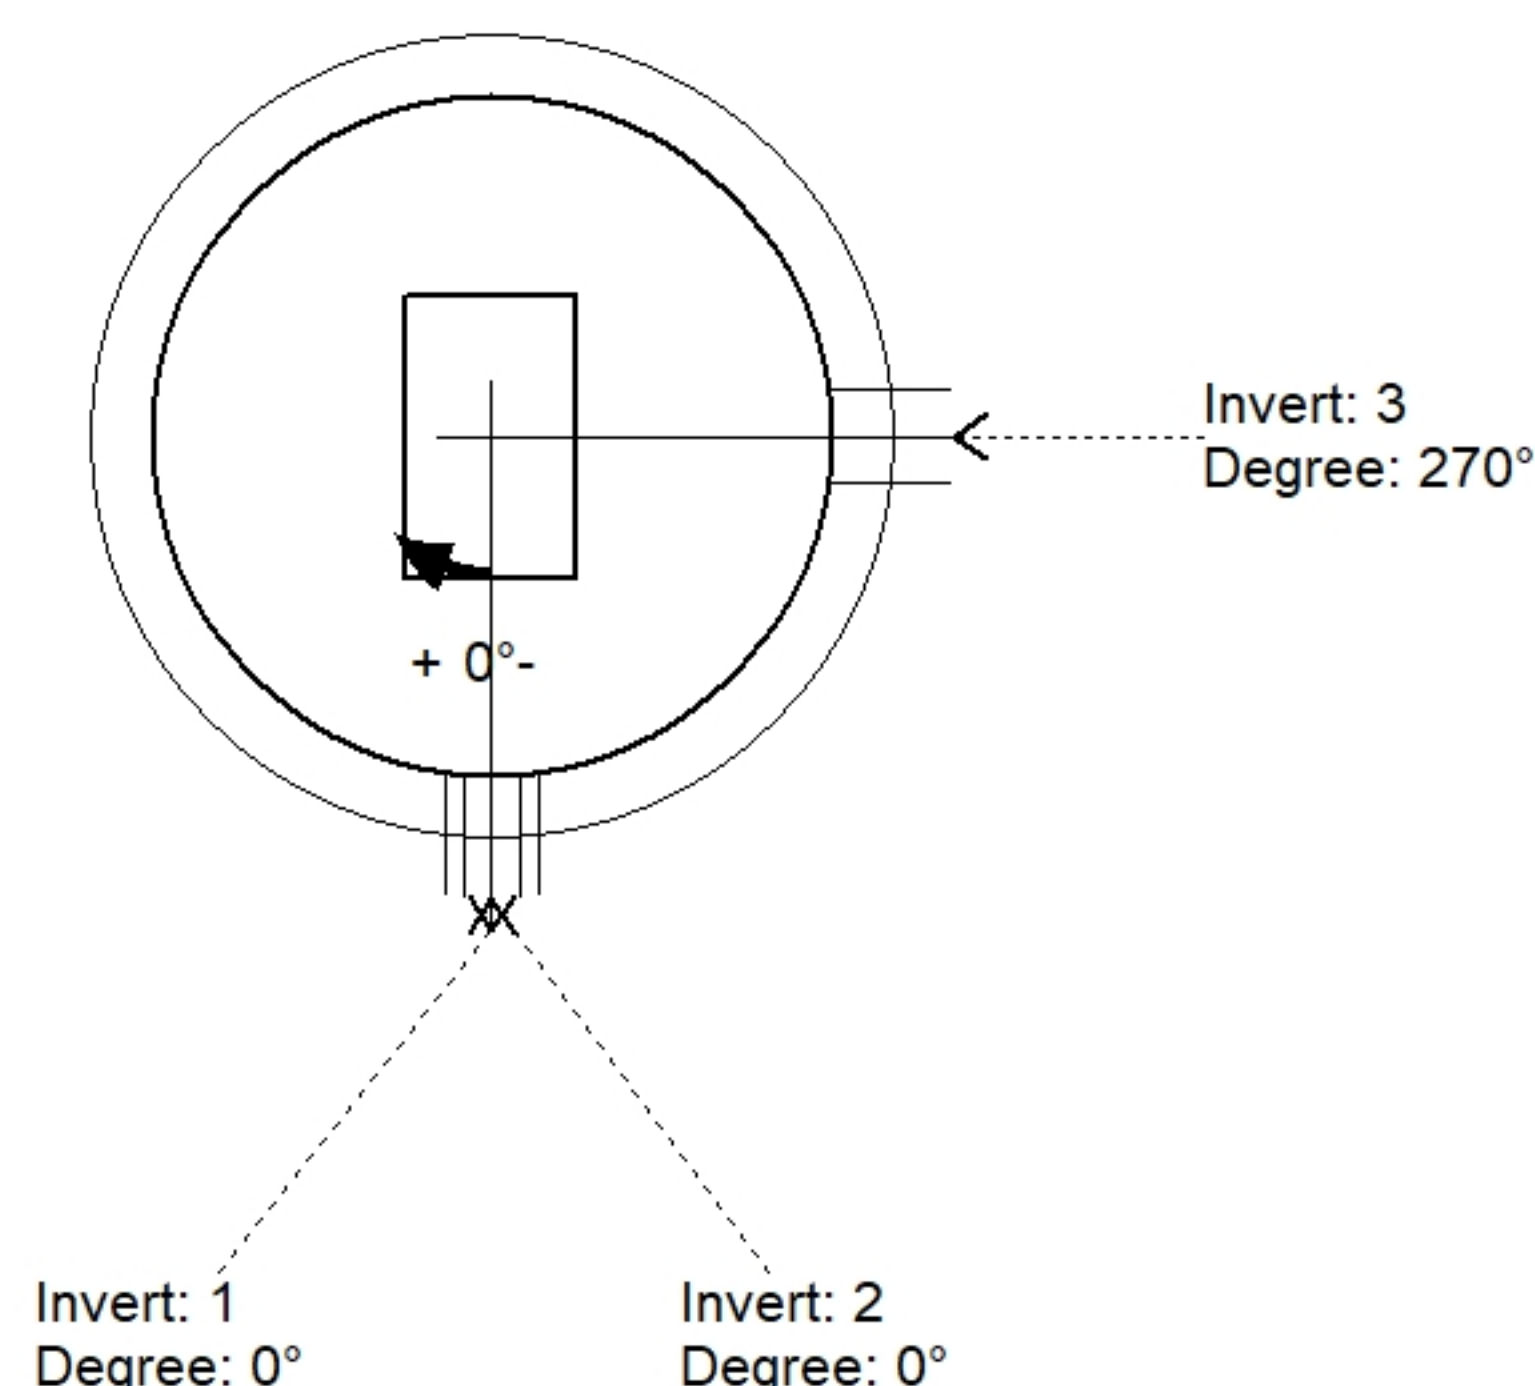

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	992.5'							
Reducer								
Invert 1	972.5'	0°	16" DI	17.5"	20"	Kor-N-Seal2 S206-20L	16"	P1
Invert 2	989.5'	0°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	63"	P3
Invert 3	979.83'	270°	16" DI	17.5"	20"	Kor-N-Seal2 S206-20L	37.96"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

SUBMITTAL
APPROVED BY:

