

Job Name: 25-3062 Portland Bypass
Job Location: Portland, TN
Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam
6/1/2026 8:23:16 AM

Tech: J. Coppage
PC: C. Goff



Structure ID: AD-4

P1 BX3232-08BAVF

BOX BASE 8inW, 8inF, Variable Ht

- P2) 32" x 32" - RECESS/GRATE SEAT - 2"
P1) 32" x 32" - BOX BASE 8inW, 8inF, Variable Ht - 36"
1) CASTING - JBS 4200 Grate
1) 32" x 32" - Conseal CS-102 1.00"
1) Hole - 25

Structure Total: 5543 lb



- Structure Notes:
1. PER TDOT D-CB-42S / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. JBS 4200 GRATE BY ICAST
4. 2" WD x 2" DEEP GRATE SEAT/RECESS IN TOP OF WALLS.
5. REINFORCING PER ASTM A615 (GRADE 60).
** SEE TDOT STD DRAWING D-CB-42S **
- WALLS (As .62) #5 BARS AT 6" C.C.E.W.
- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

Rim: 810.65' Rim to Invert: 2.86' Slack: 0.82" Sump: 2.5" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	807.79'	0°	24"	18" RCP B WALL	23"	Hole 25	25"	25"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

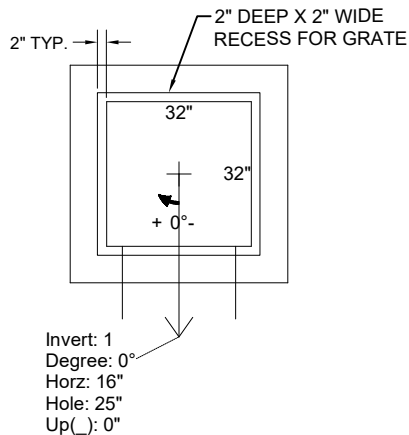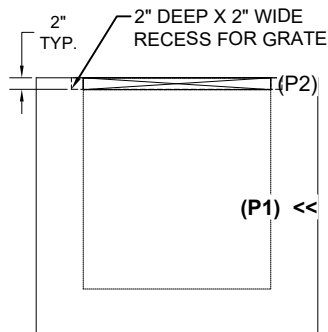

INSIDE WALL DIMENSIONS

(P1)

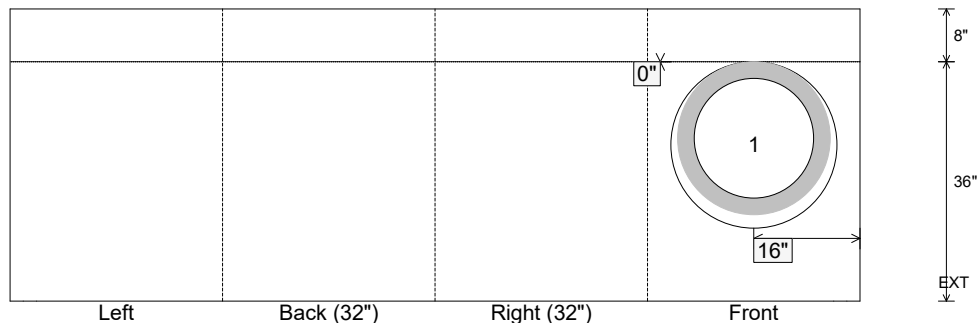

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 36"
Height (Ext): 44"

Weight (Net): 5084 lb
Volume (Net): 1.3cu.yd
